


Appendix C


Contractors Construction Progress Schedules

CAMINADA HEADLAND BACK BARRIER MARSH CREATION PROJECT (BA-0171) **GLDD Progress Schedule** Finish Task Name Duration Predecessors Half 1, 2020 F M A M J S O N D **Key Dates and Milestones** 650 days Thu 1/9/20 Wed 10/20/21 **Bid Date** Thu 1/9/20 Thu 1/9/20 0 days 1/9 3 NTP 0 days Mon 4/20/20 Mon 4/20/20 4/20 4 **Estimated Pre-Construction Conference** Mon 6/1/20 Mon 6/1/20 0 days ♦ 6/1 5 **Required Completion** 0 days Wed 10/20/21 Wed 10/20/21 3FS+548 days 10/20 6 | | Bird Nesting Season - No pipeline mobilization 184 days Sun 3/15/20 Tue 9/15/20 Bird Nesting Season - No pipeline mobilization activity during this time activity during this time Mobilization (TS-100, TS-101 & TS-102) 146 days Wed 9/16/20 Tue 2/9/21 Project Initial Team Mobilize to Site & Office Wed 1/20/21 Sat 1/30/21 Project Initial Team Mobilize to Site & Office Setup (TS-102) 10 days 1/20 ____ 1/30 Setup (TS-102) Mobilize and Install Pipelines (TS-101) 146 days Wed 9/16/20 Tue 2/9/21 Mobilize and Install Pipelines (TS-101) 9/16 Tow Dredge to Site and Prep (TS-100) 7 days Tue 2/2/21 Tue 2/9/21 Tow Dredge to Site and Prep (TS-100) 2/2 2/9 11 Surveys (TS-210) 372 days Tue 5/12/20 Wed 5/19/21 12 **Pre Construction Surveys** 274 days Tue 5/12/20 Wed 2/10/21 13 **Priority Surveys for Dike Construction** 55 days Tue 5/12/20 Mon 7/6/20 14 | | **Pre Construction Submittals** Tue 5/12/20 Tue 5/12/20 0 days 5/12 15 CPRA Pre-Construction Survey Submittal Approval 5/12 5/26 **CPRA Pre-Construction Survey Submittal** Tue 5/12/20 Tue 5/26/20 14 days 14 Approval 16 Mobilization, Project Setup, Project Tue 5/26/20 Thu 5/28/20 15 Mobilization, Project Setup, Project Control (Locate, Verify and Establish) 2 days 5/26 75/28 Control (Locate, Verify and Establish) 17 **Bathymetric and Topographic** 20 days Thu 5/28/20 Wed 6/17/20 18 Single Beam Bathymetric and Topographic Survey Equipment Access Corridors 5/28 6/4 Single Beam Bathymetric and 7 days Thu 5/28/20 Thu 6/4/20 16 **Topographic Survey Equipment Access** 19 Topographic Survey Centerline of Thu 6/4/20 Wed 6/17/20 18 Topographic Survey Centerline of Earthen Containment Dike 13 days 6/4 6/17 Earthen Containment Dike 20 Magnetometer 25 days Thu 5/28/20 Mon 6/22/20 21 Magnetometer Access Corridor Magnetometer Access Corridor 15 days Thu 5/28/20 Fri 6/12/20 16 5/28 6/12 1 Manual Progress Task **Project Summary** Manual Task Start-only Deadline 3 Project: 84768 - Caminanda Head Split Inactive Task **Duration-only** Finish-only Critical Date: Wed 5/13/20 Manual Summary Rollup Milestone Inactive Milestone External Tasks Critical Split **Inactive Summary** Manual Summary Progress Summary



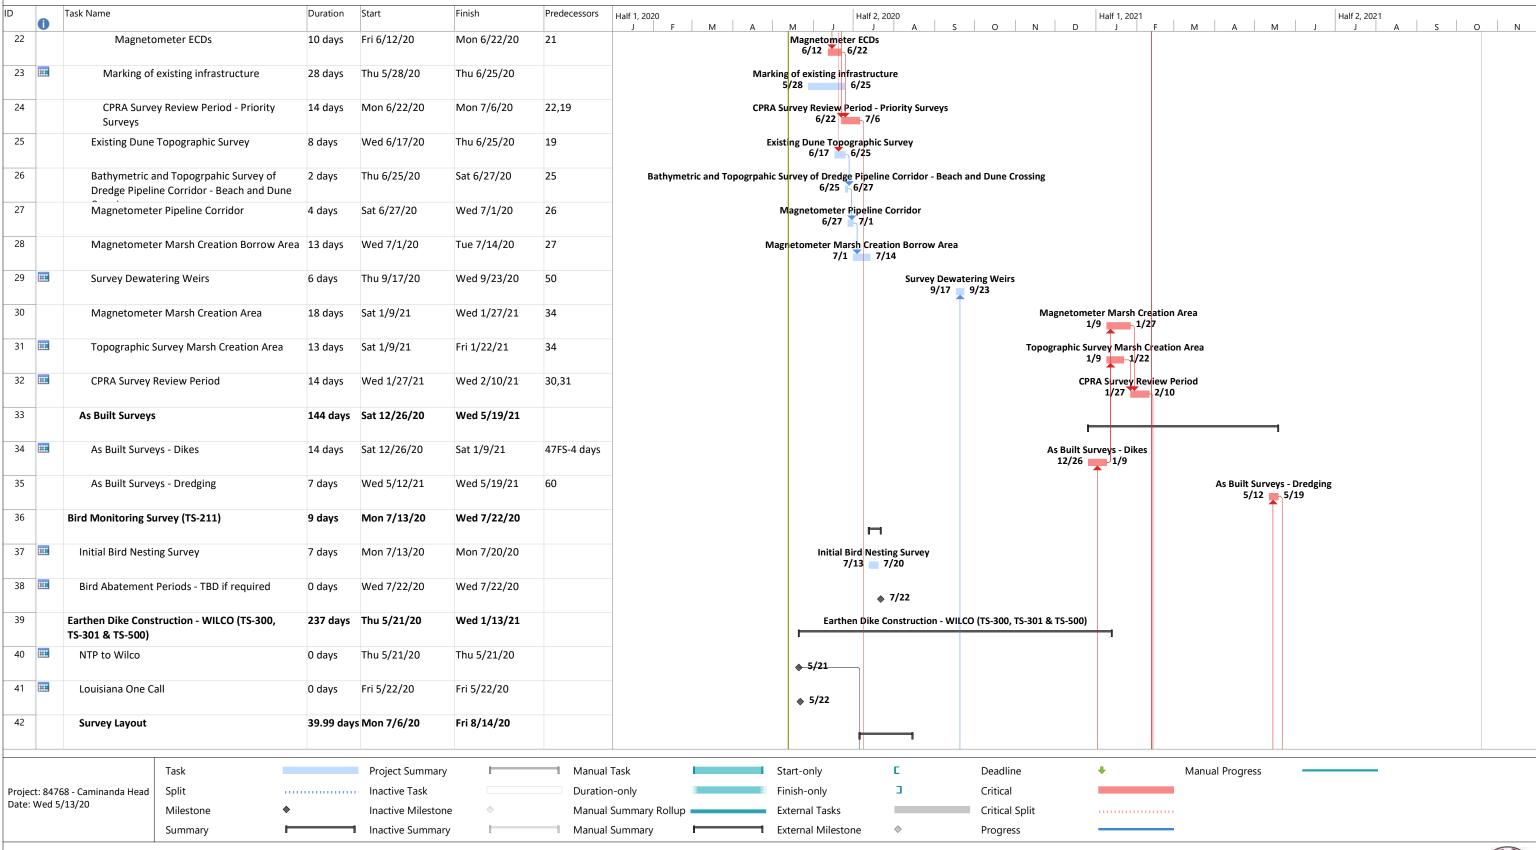



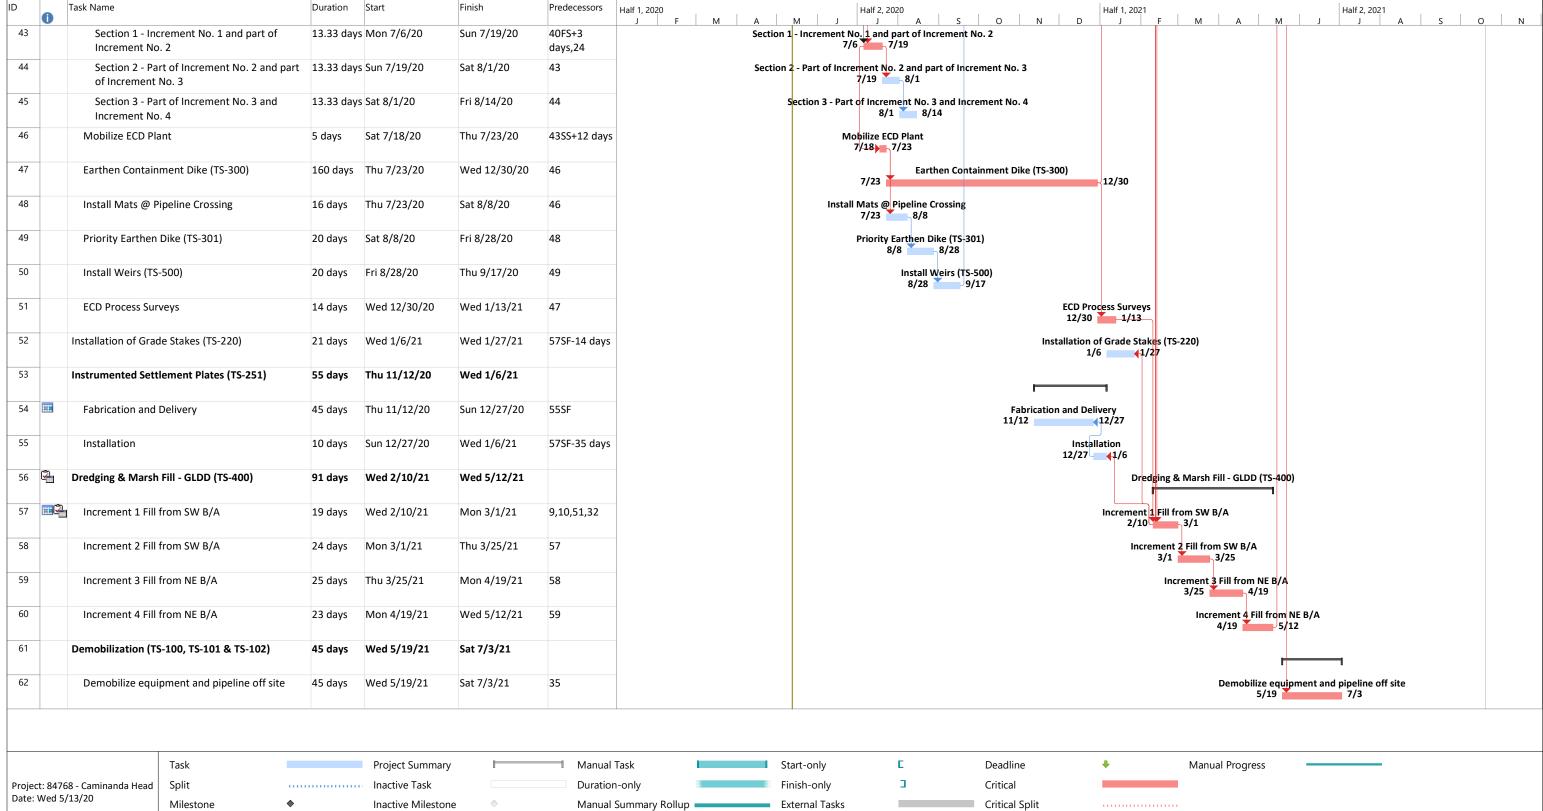

Wed 5/13/20 11:34 AM

Summary

Inactive Summary





■ External Milestone


Progress


Manual Summary




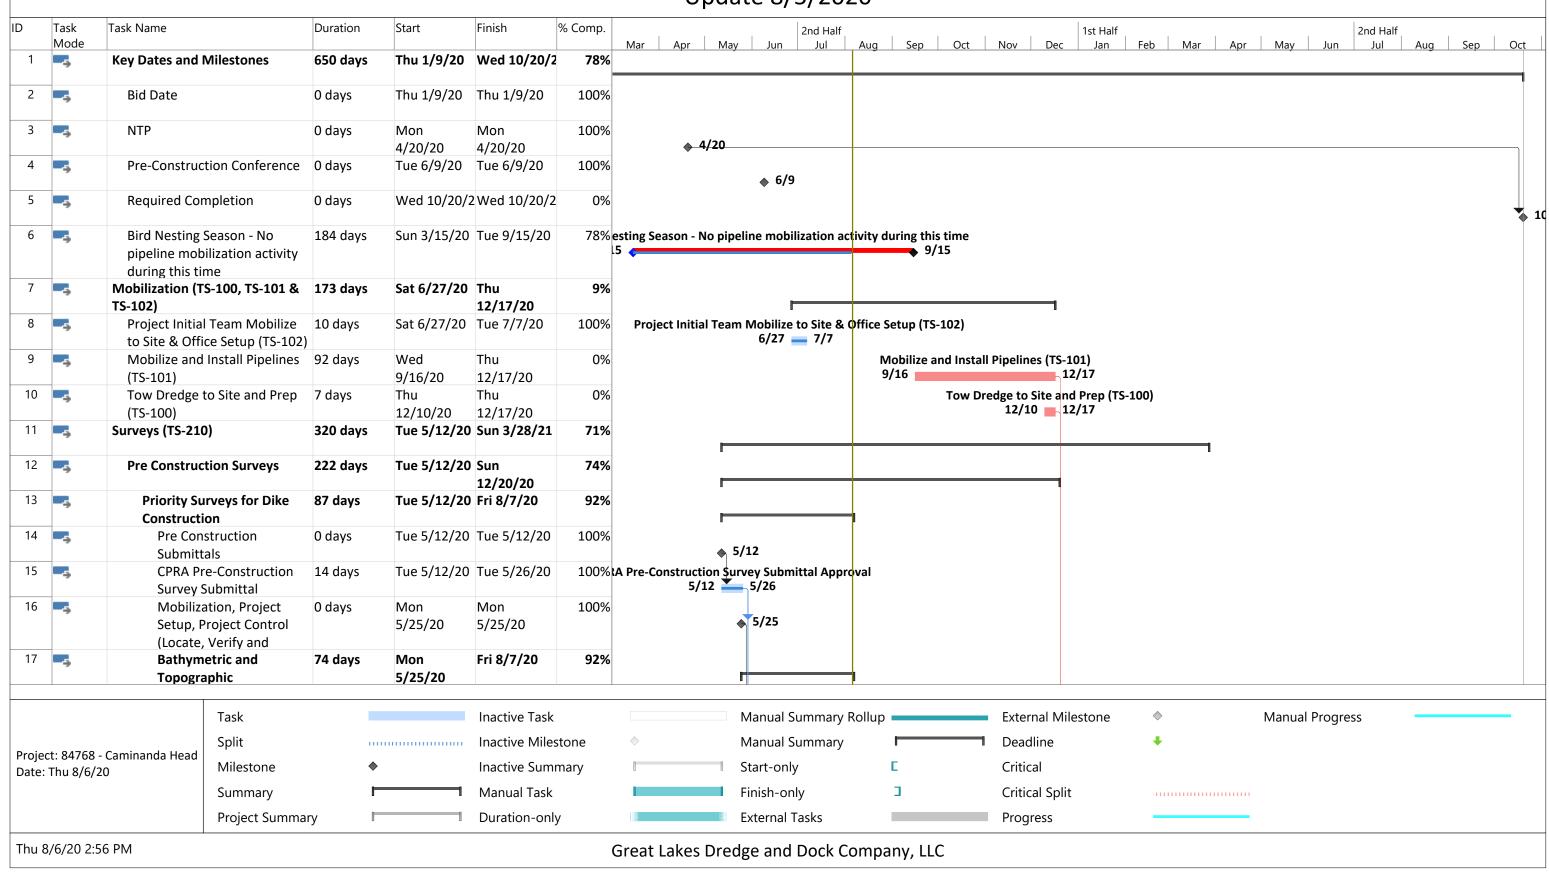


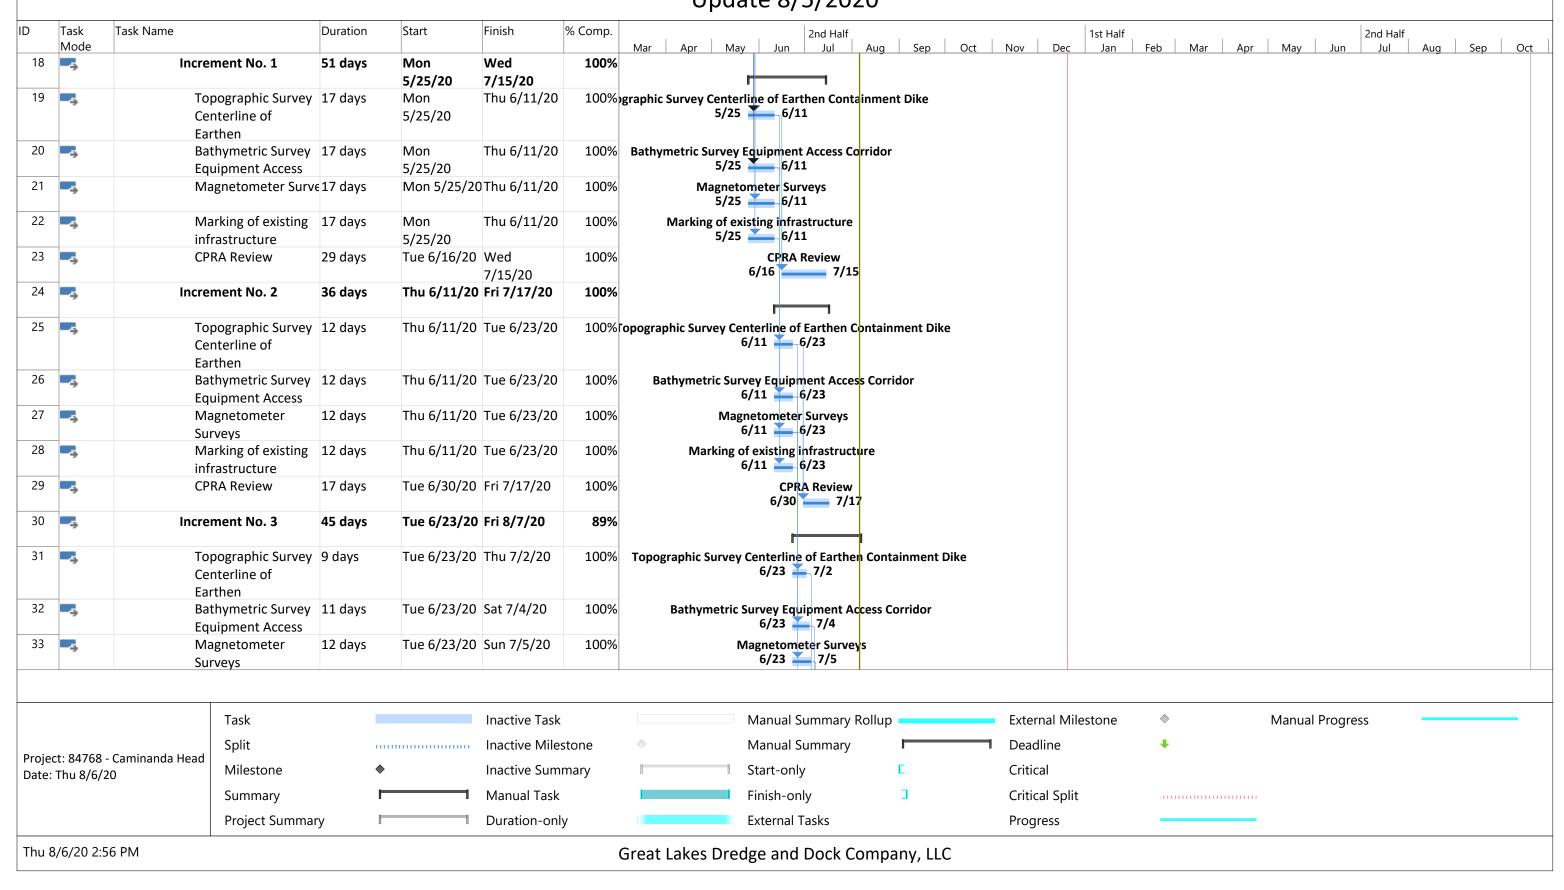


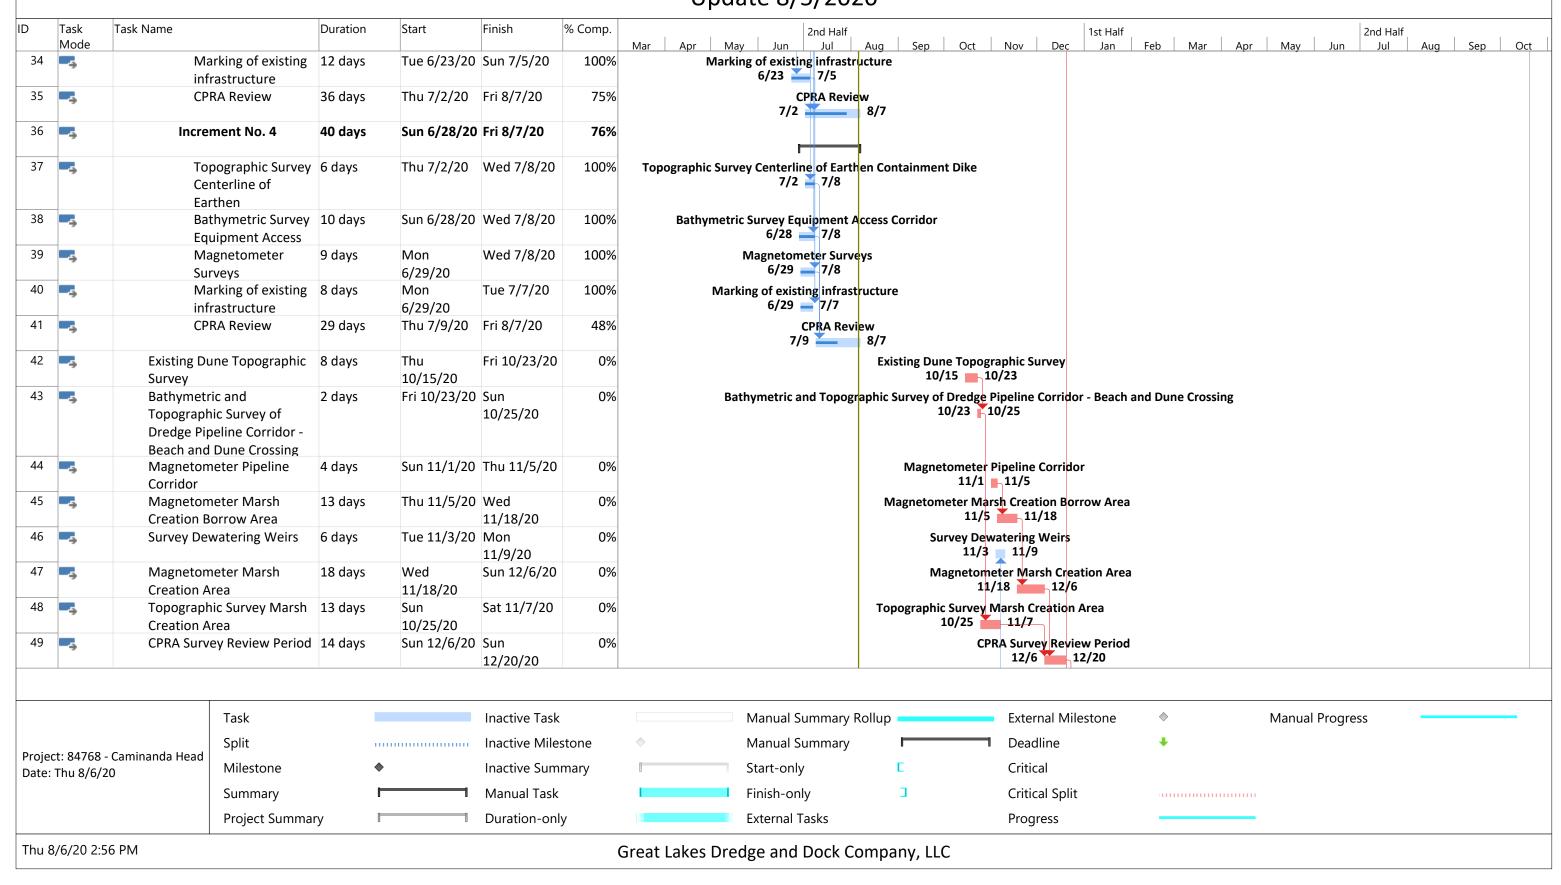


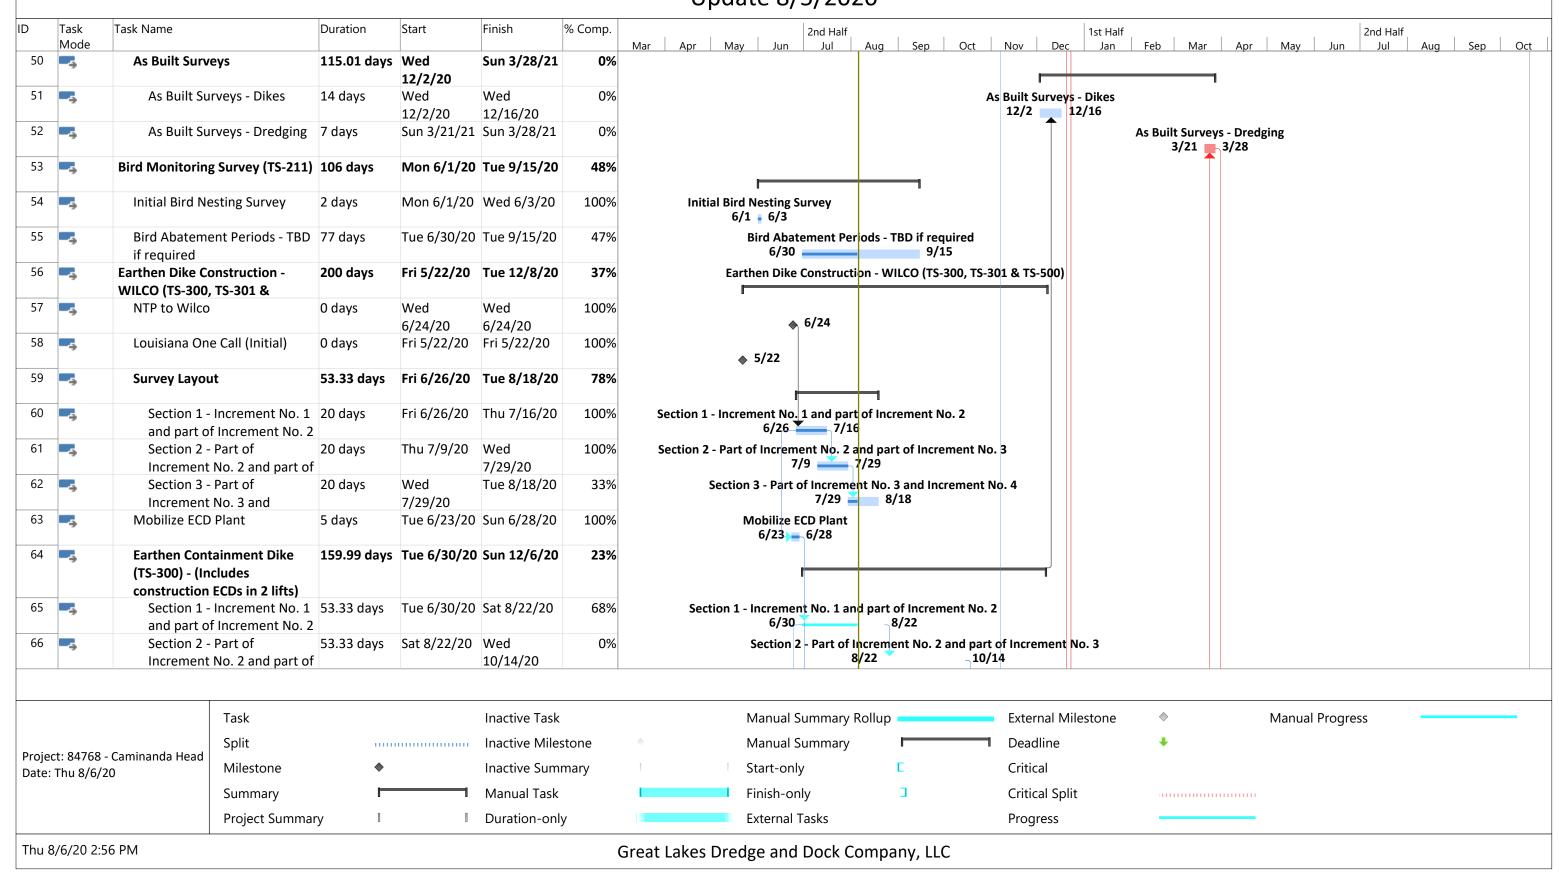


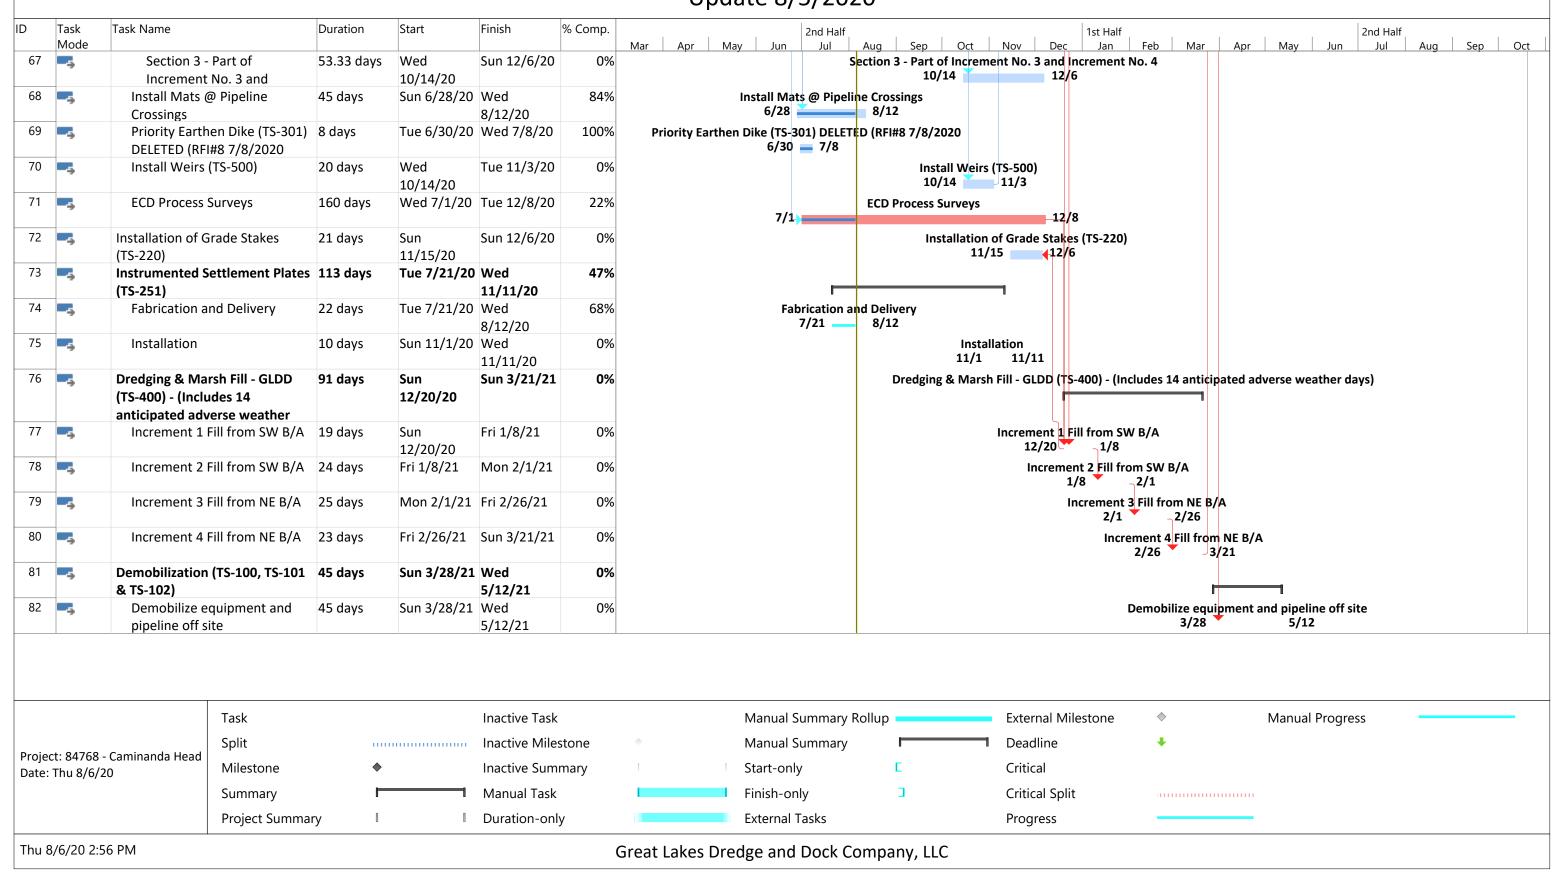


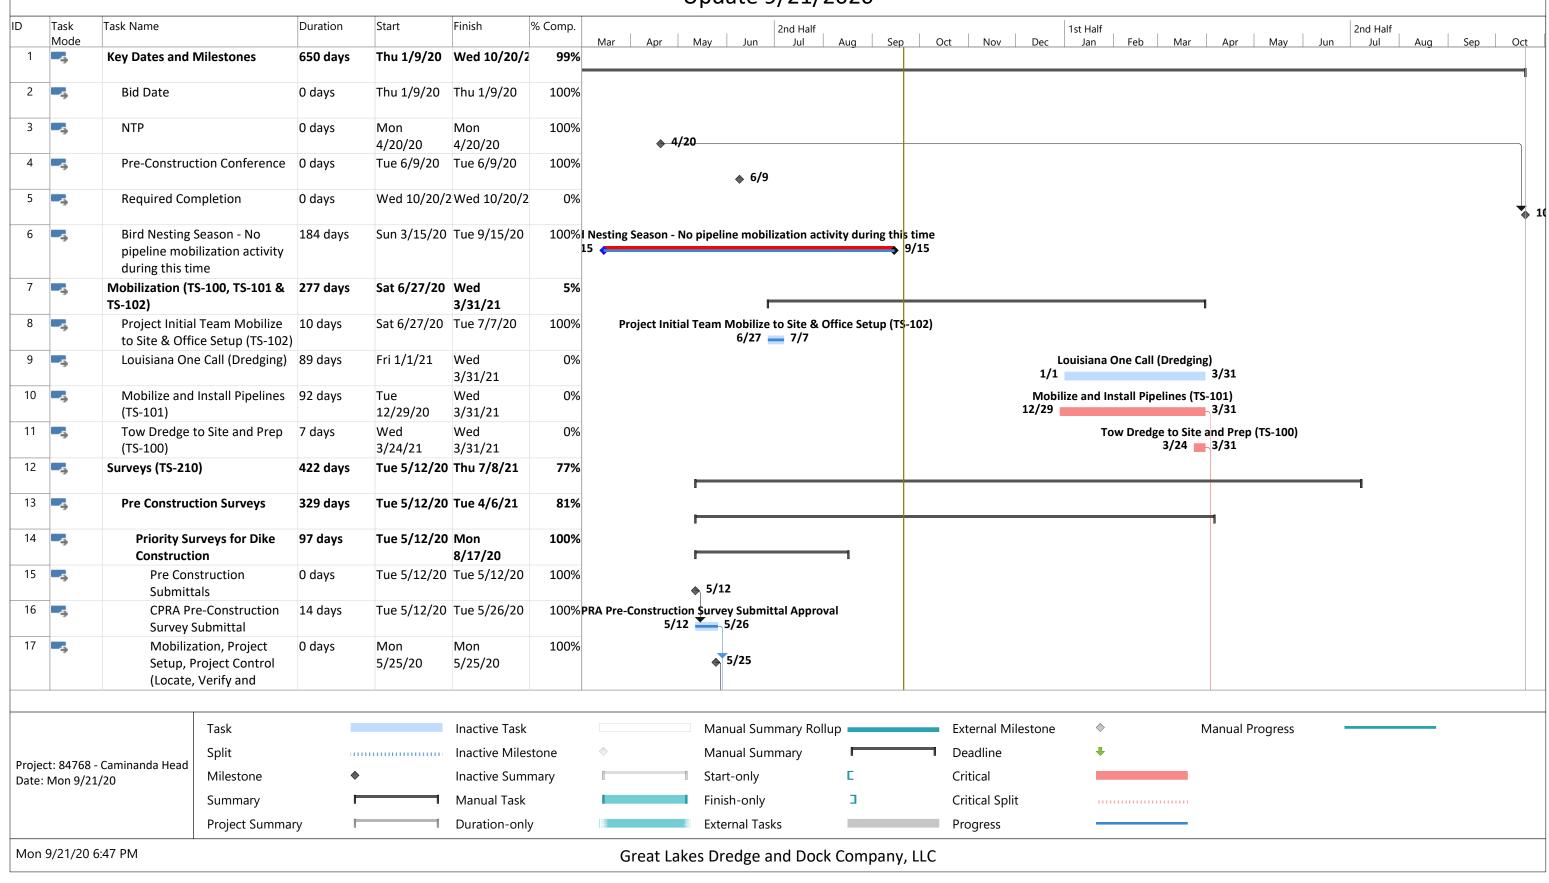


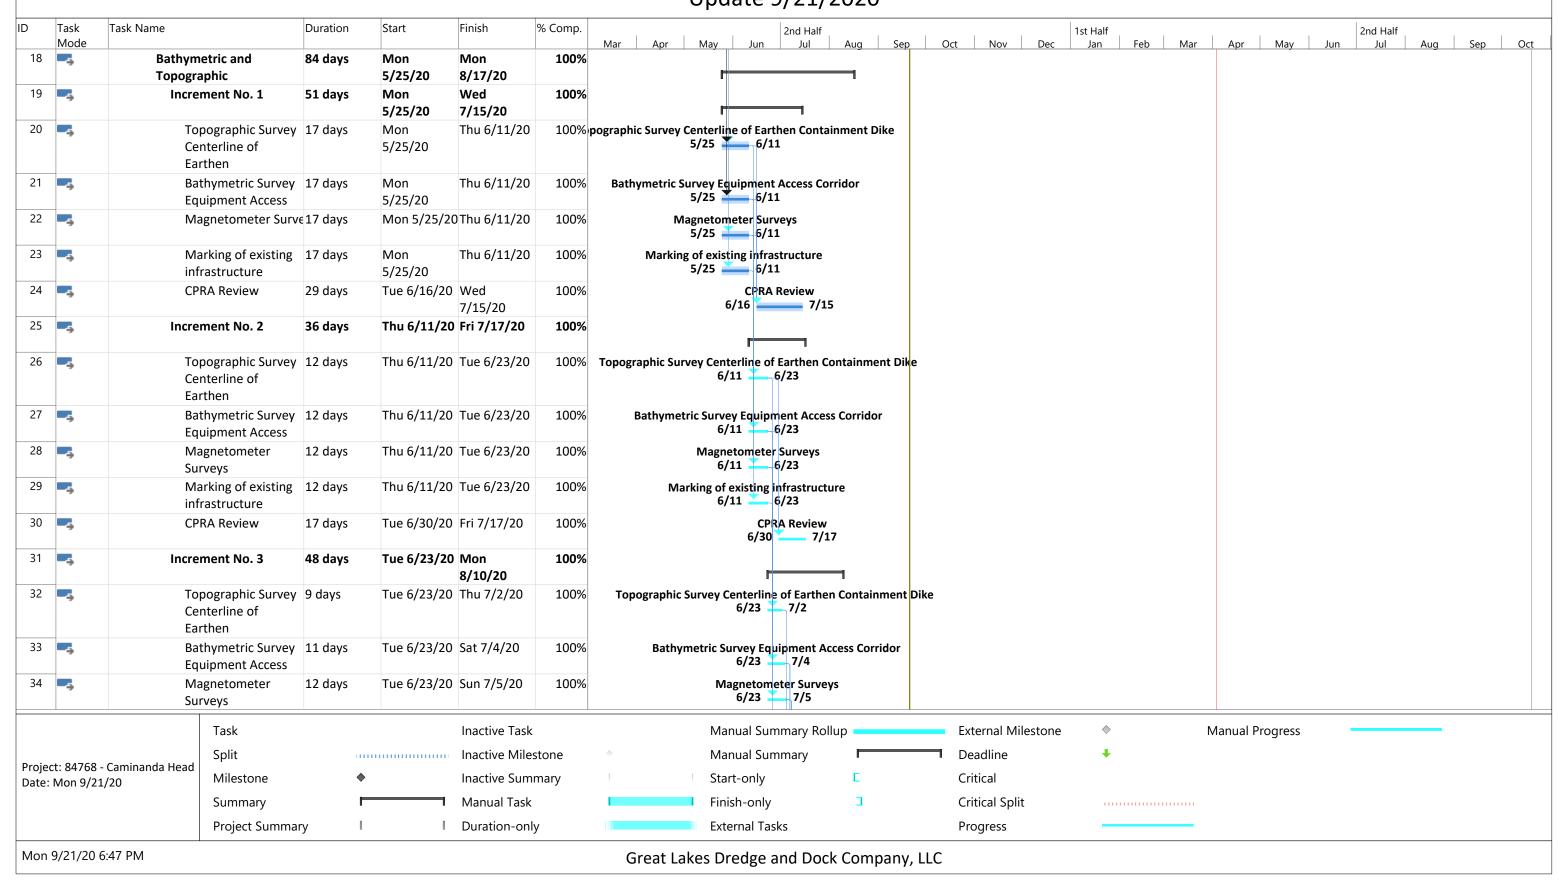


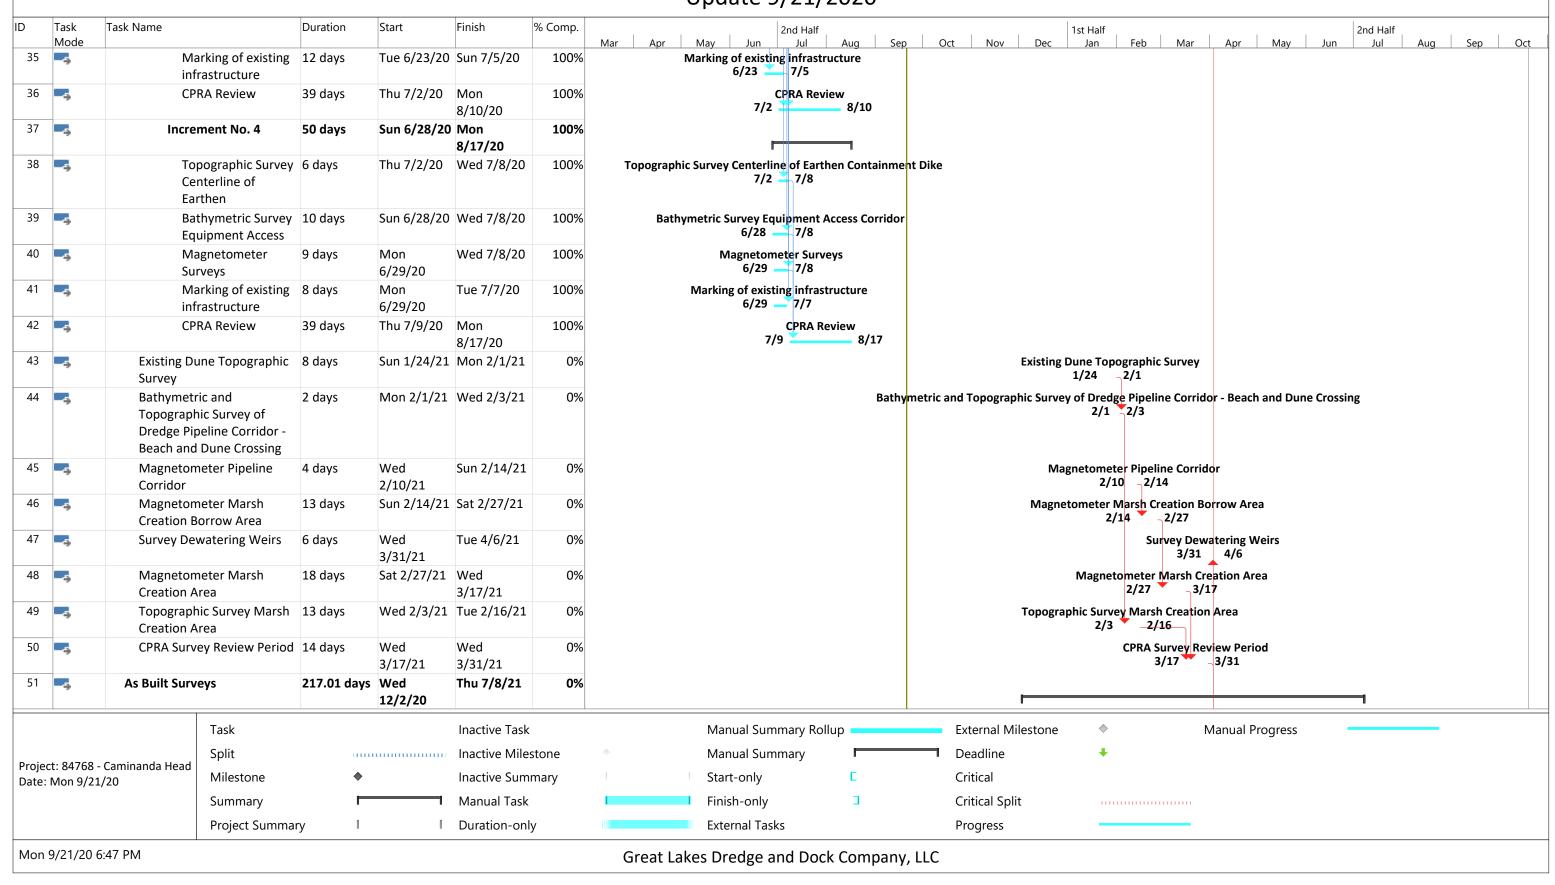


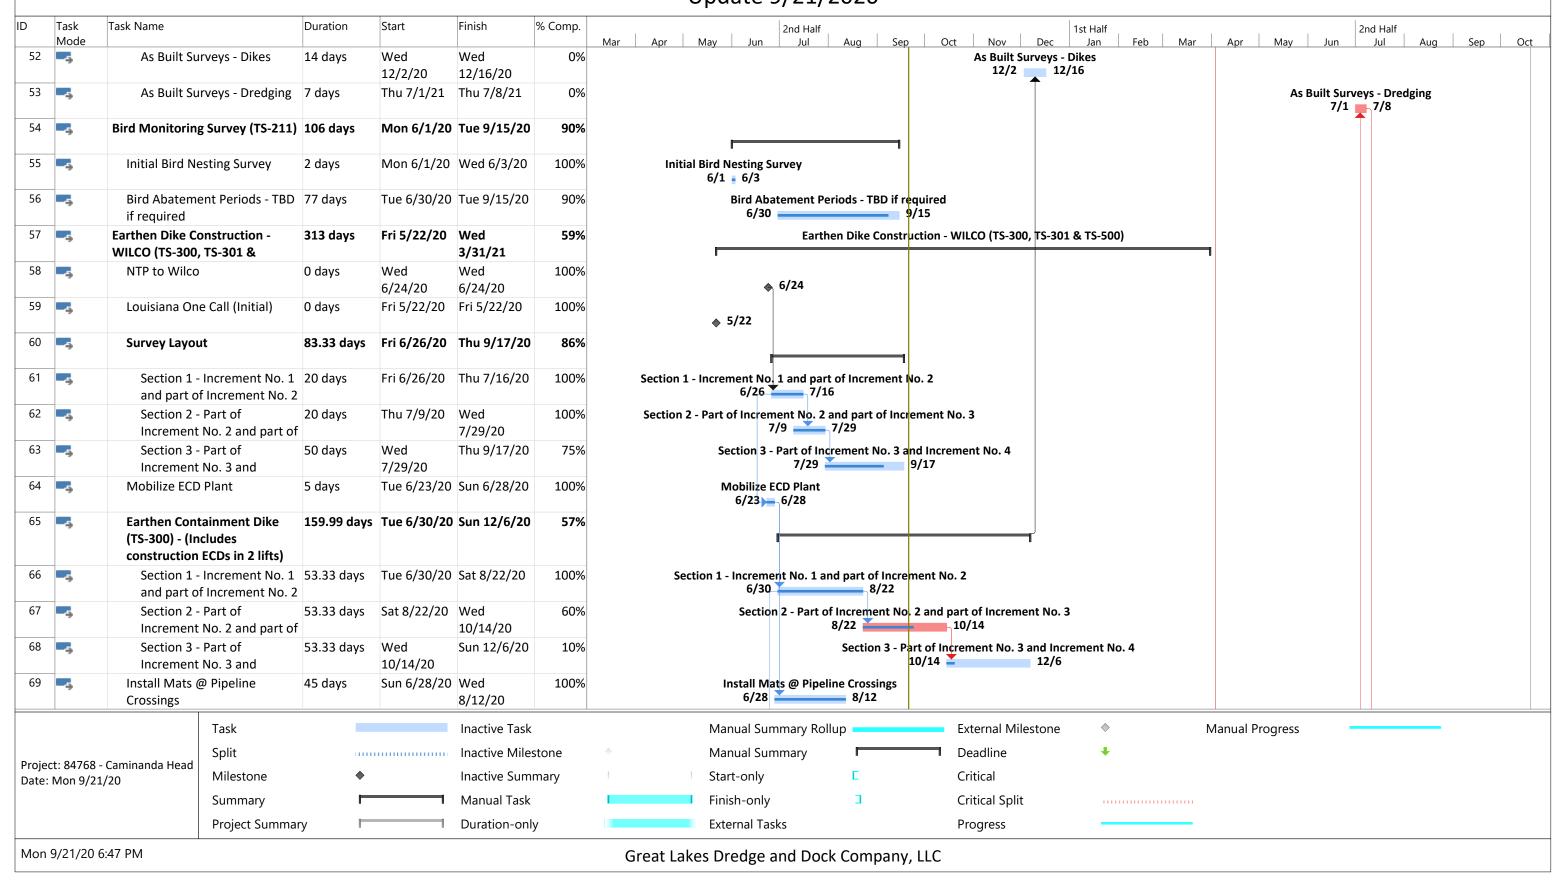


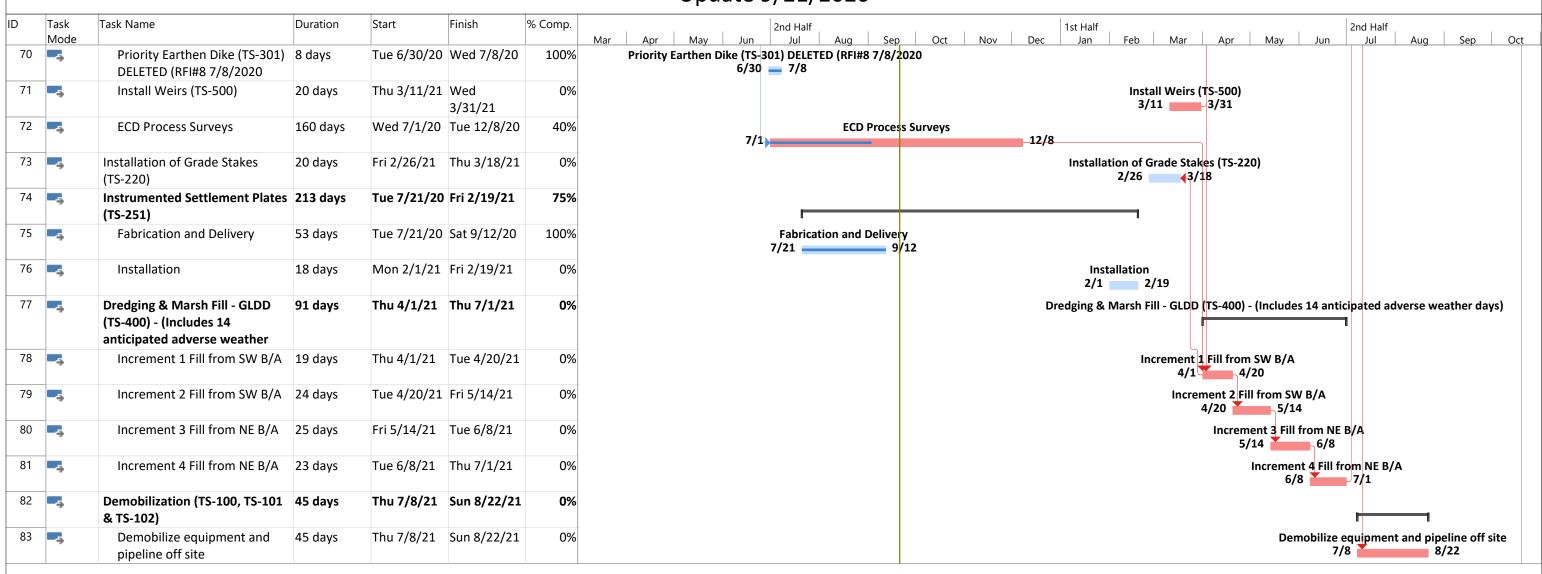





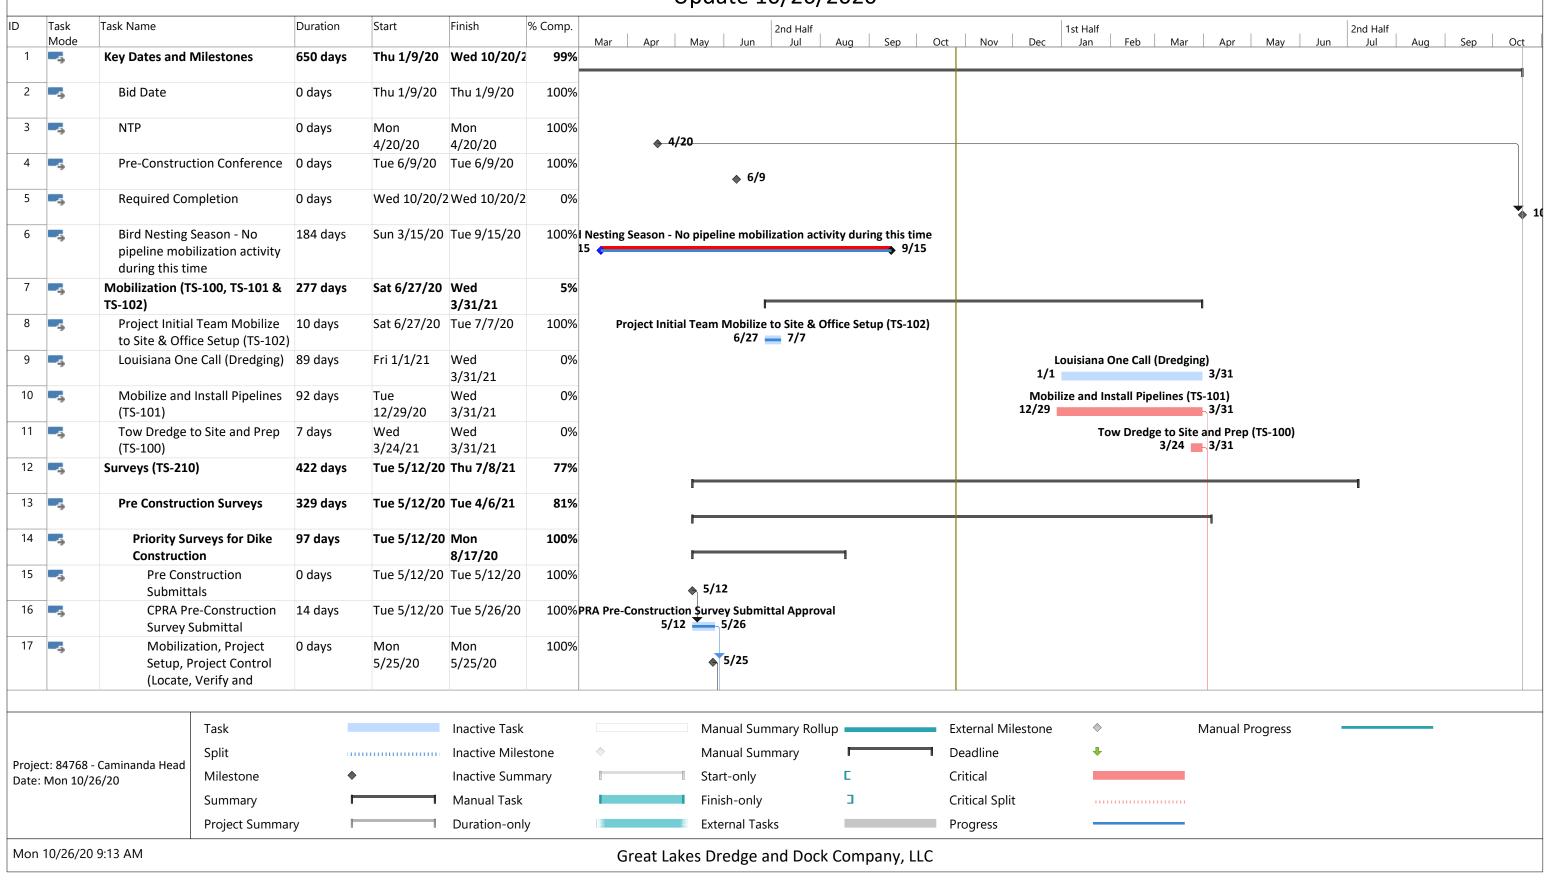


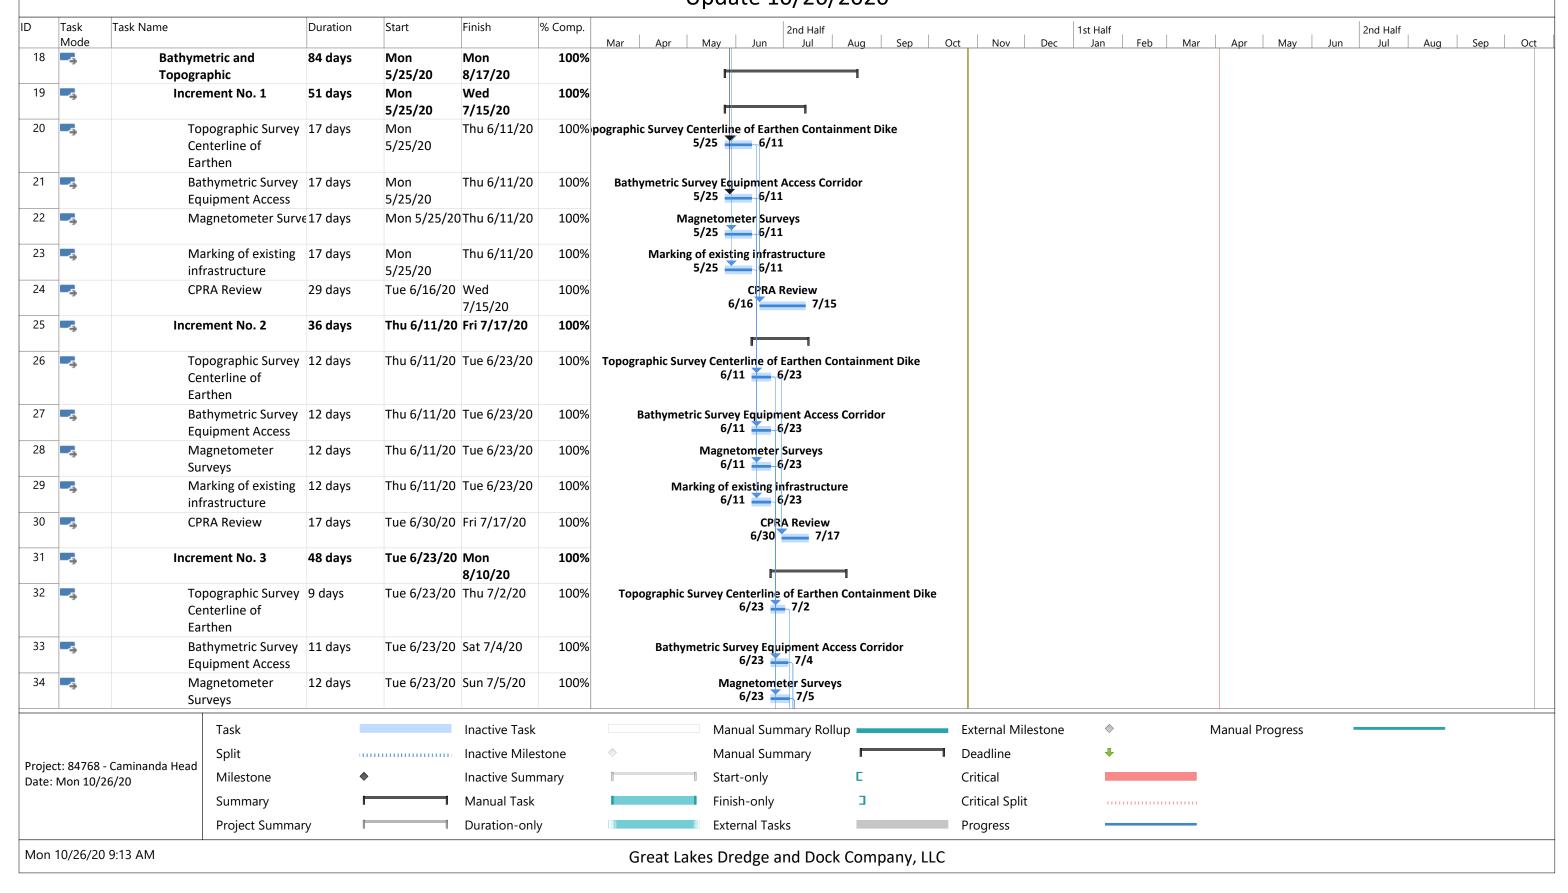

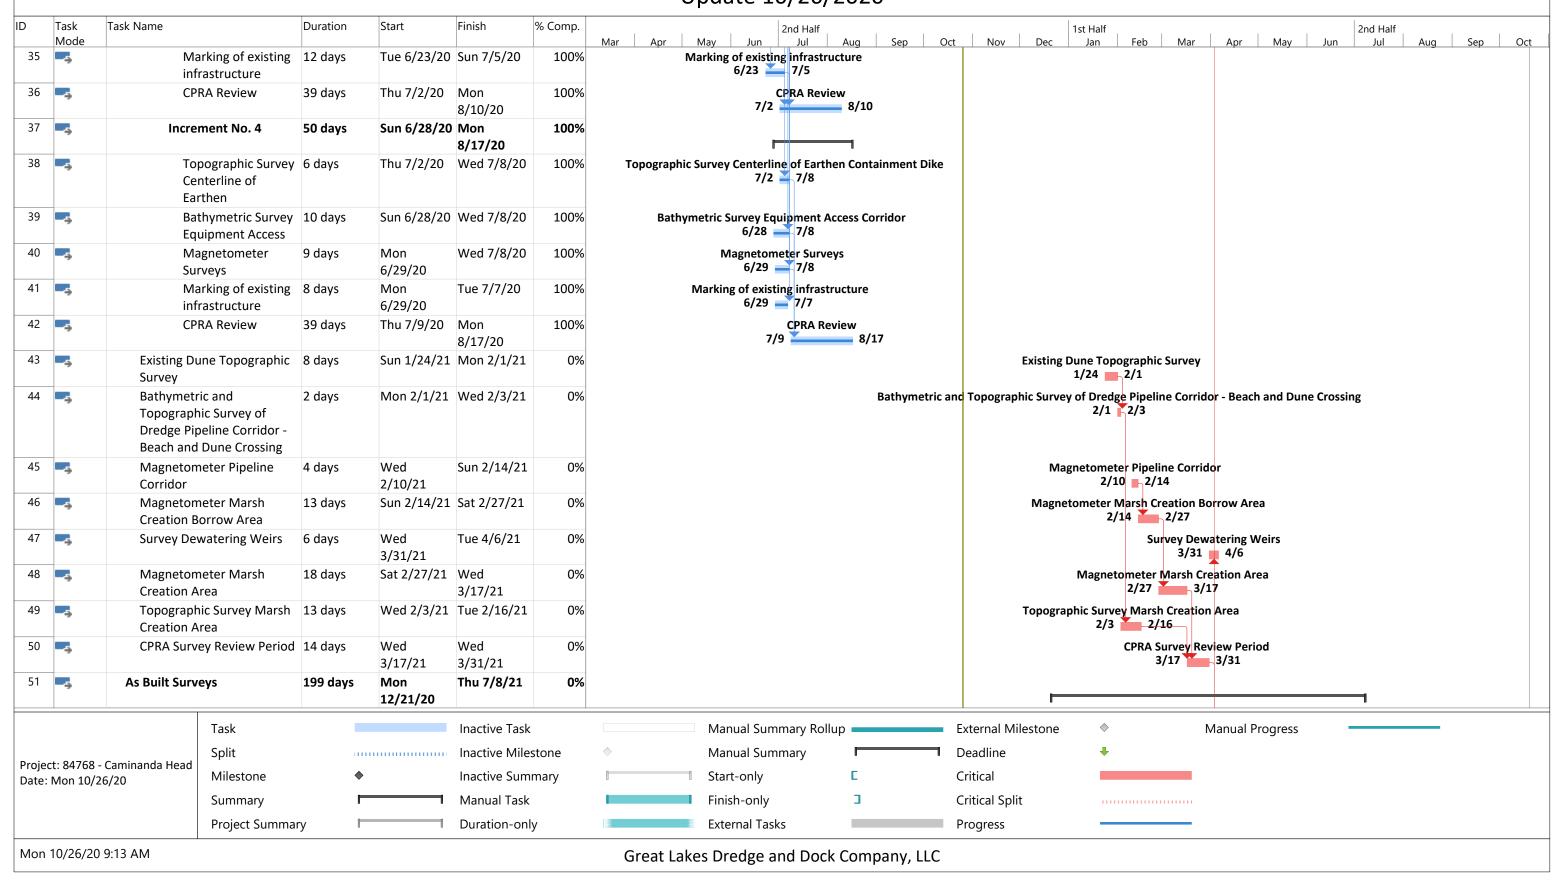

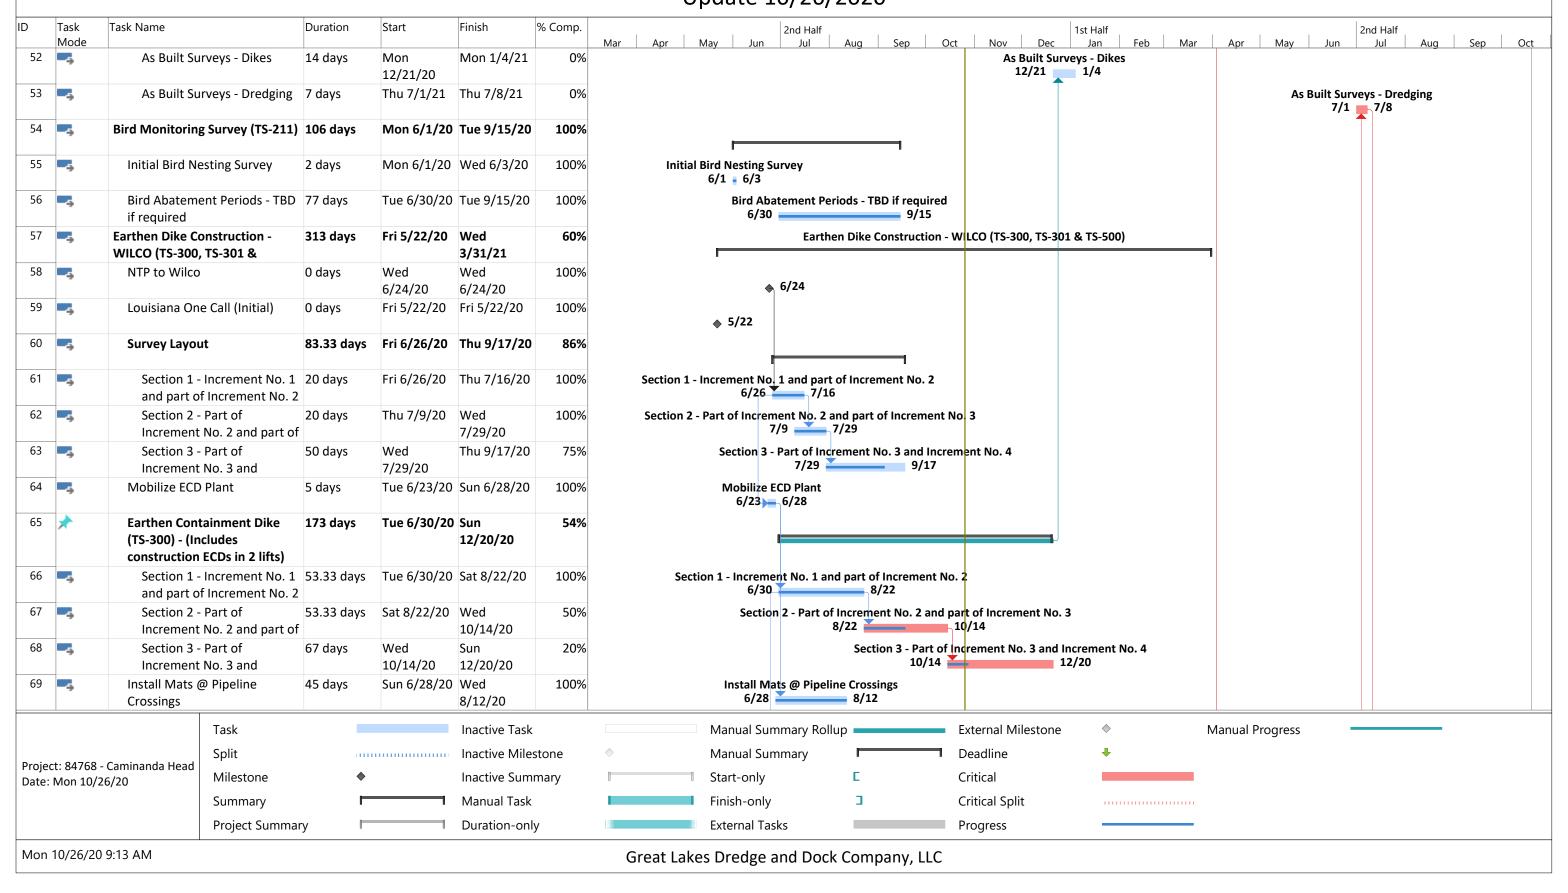

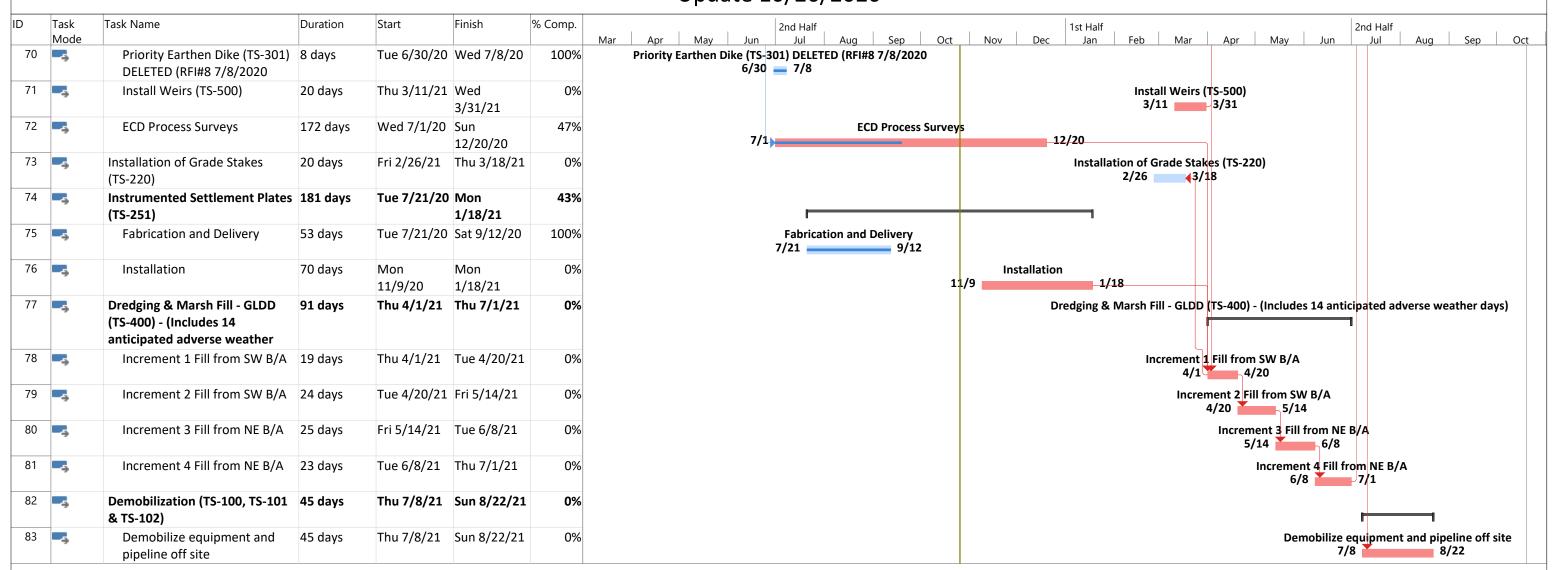






Mon 10/26/20 9:13 AM


Great Lakes Dredge and Dock Company, LLC




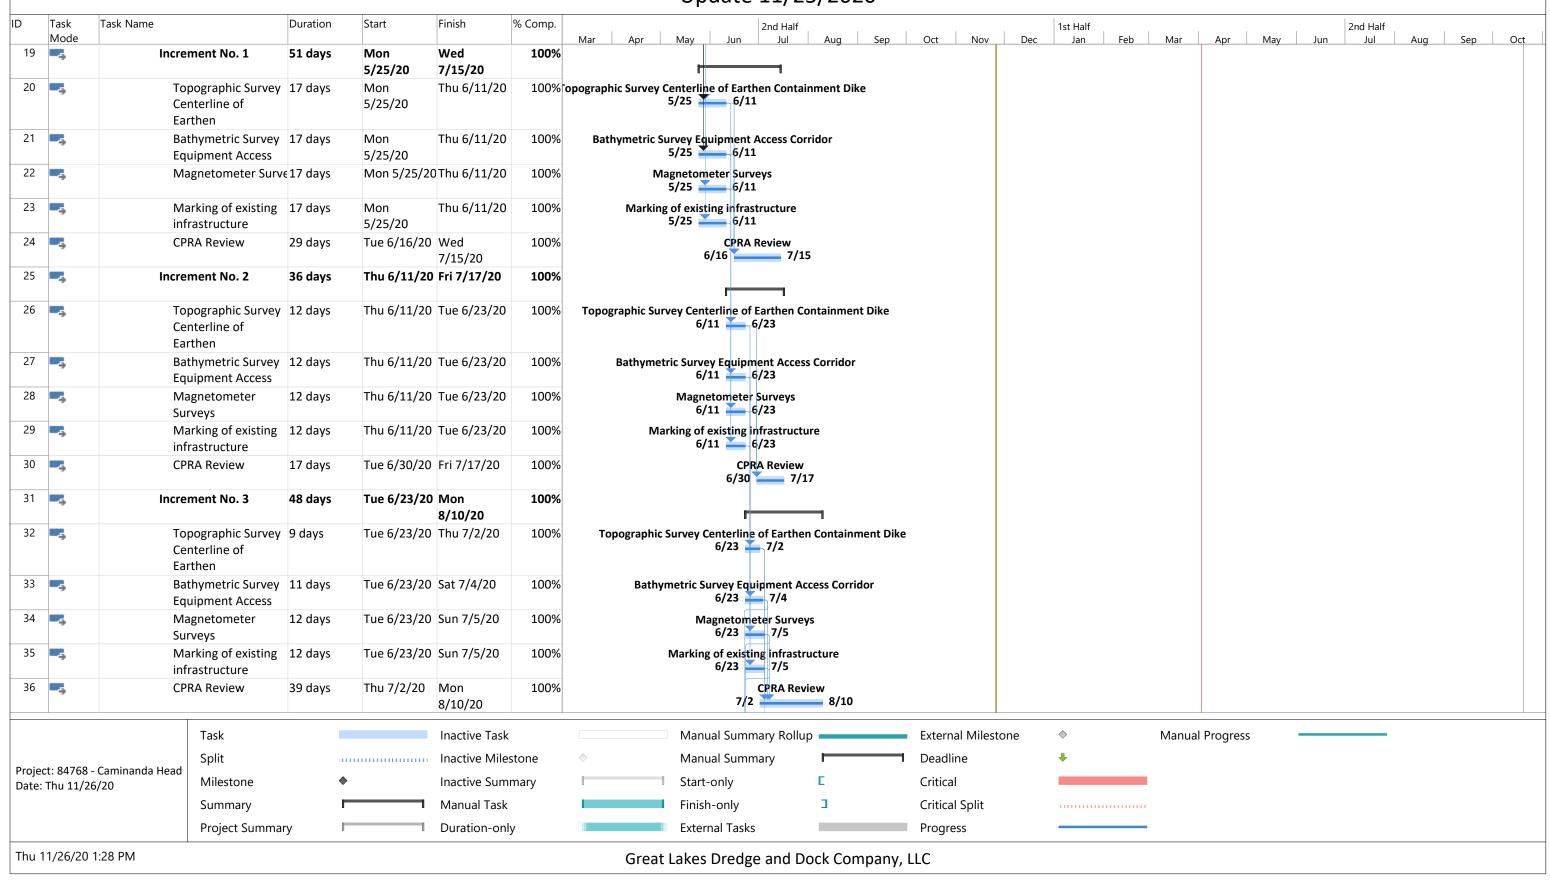

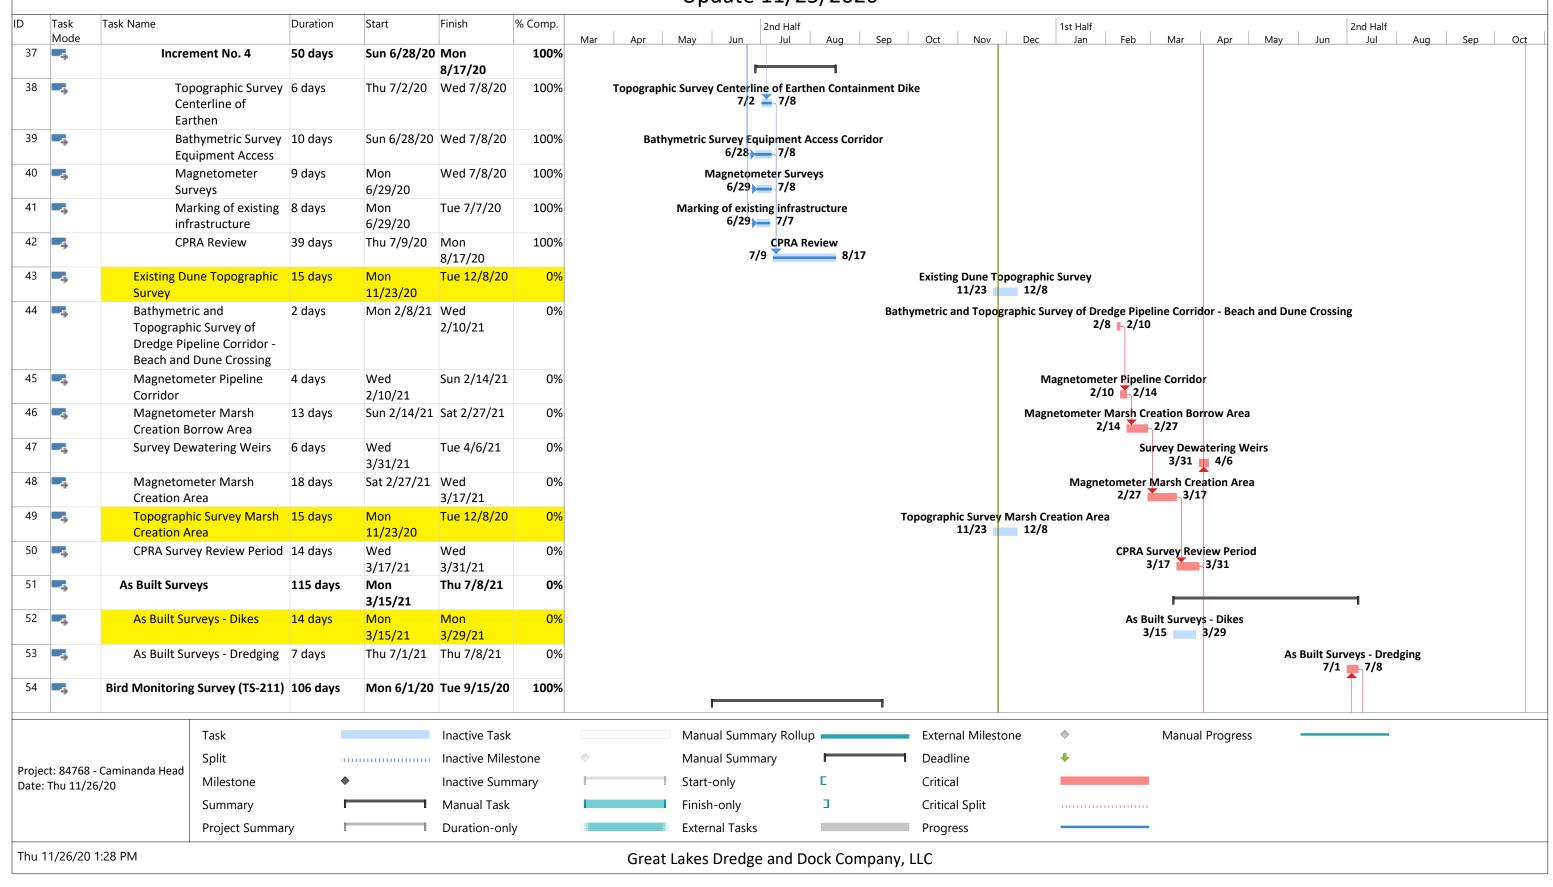

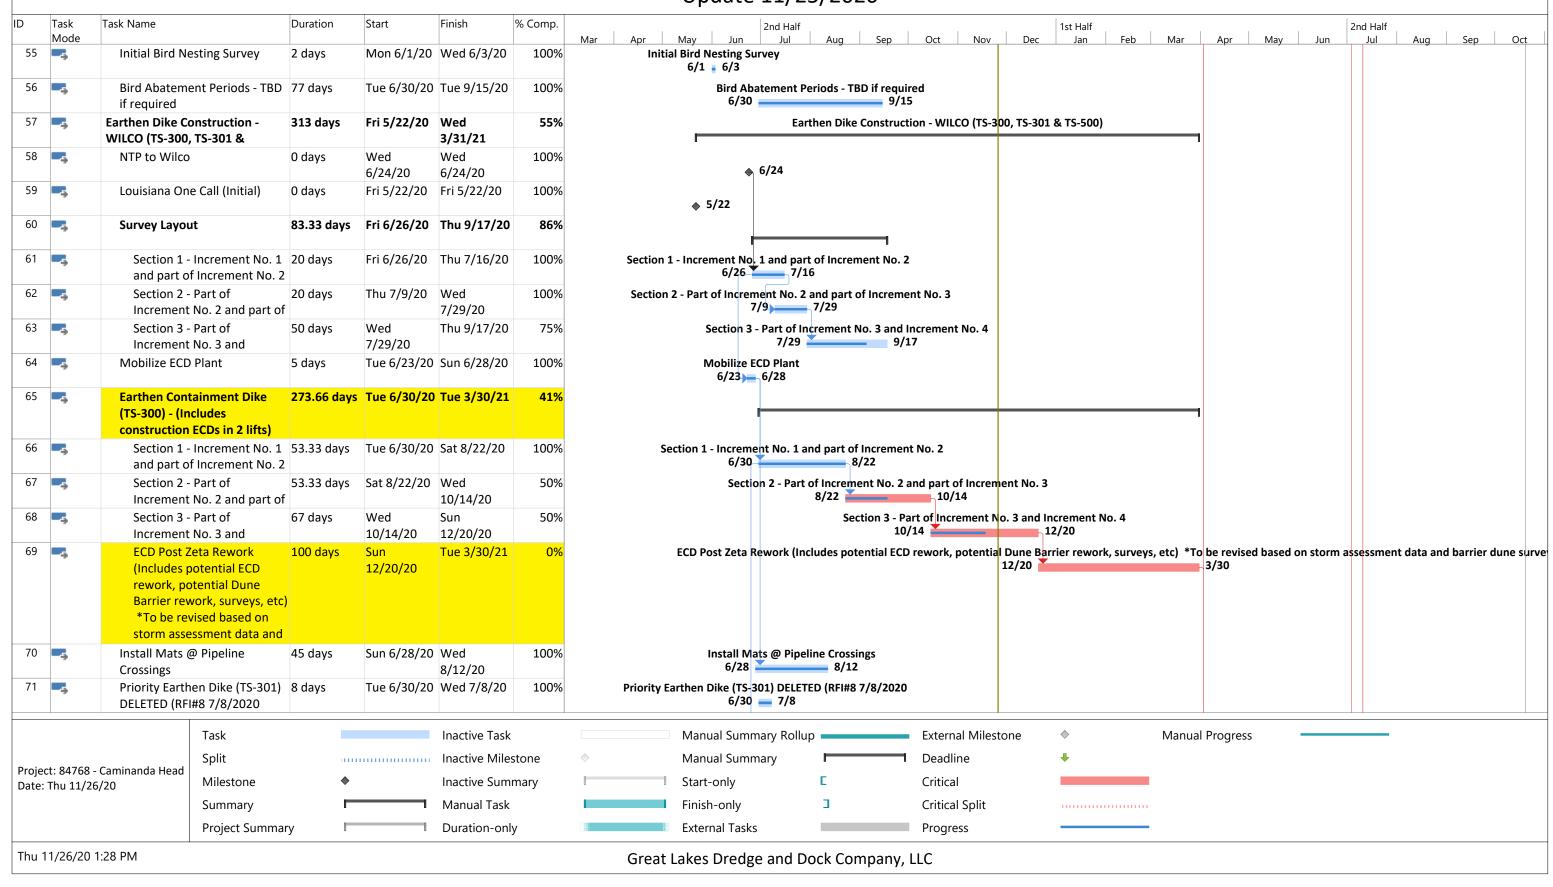

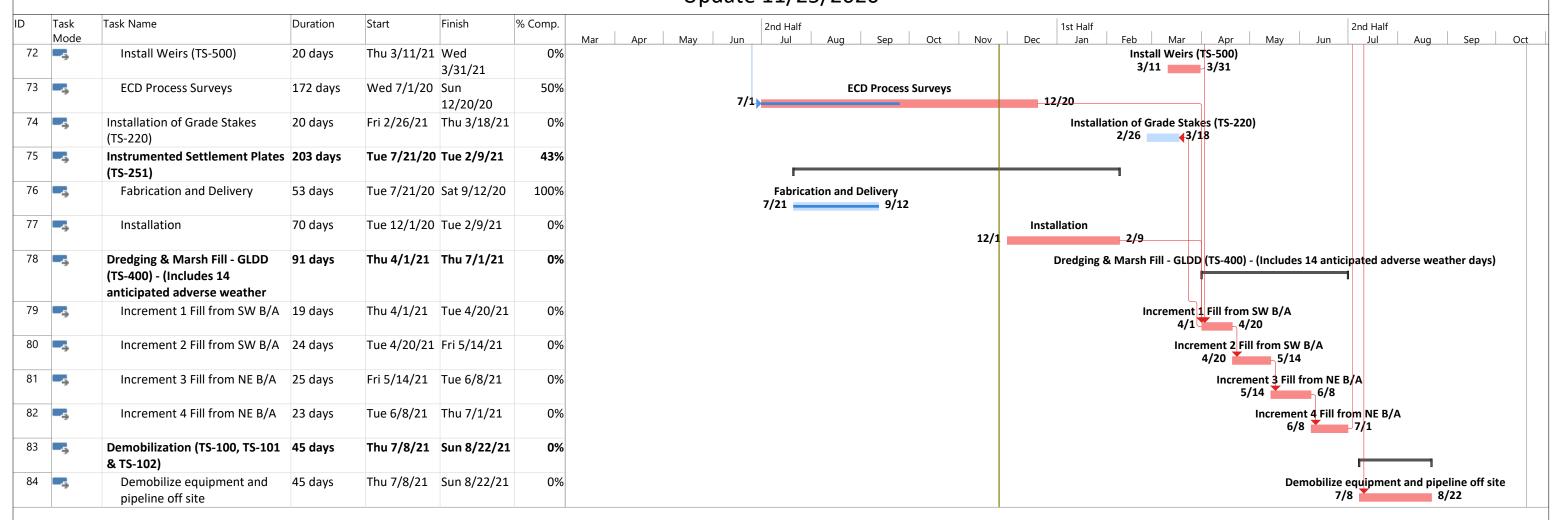





Thu 11/26/20 1:28 PM


Great Lakes Dredge and Dock Company, LLC






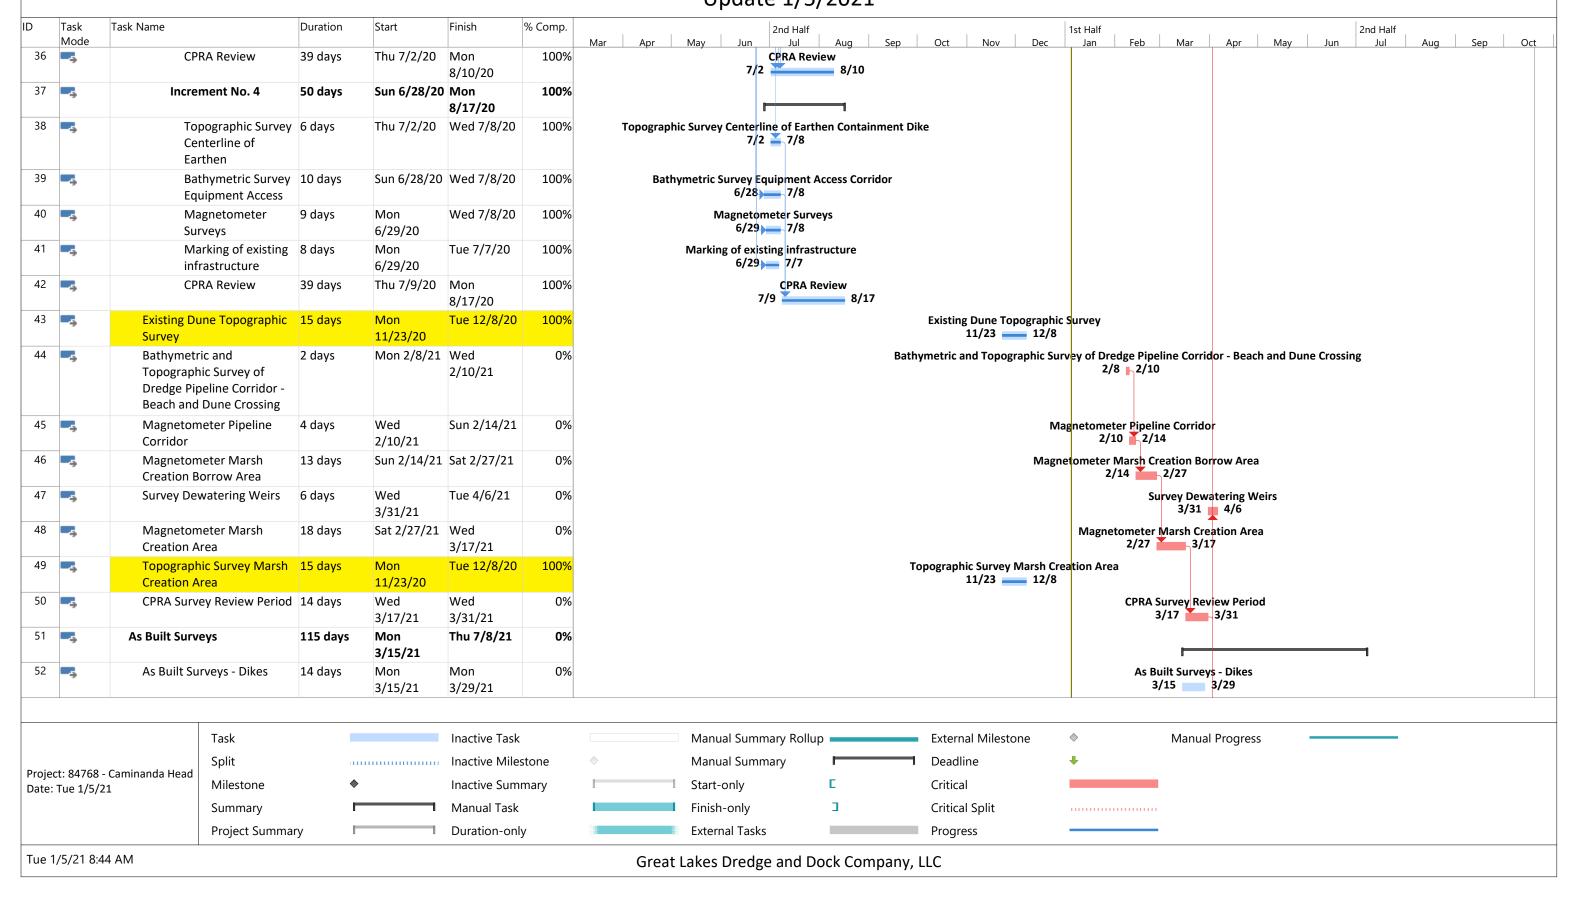


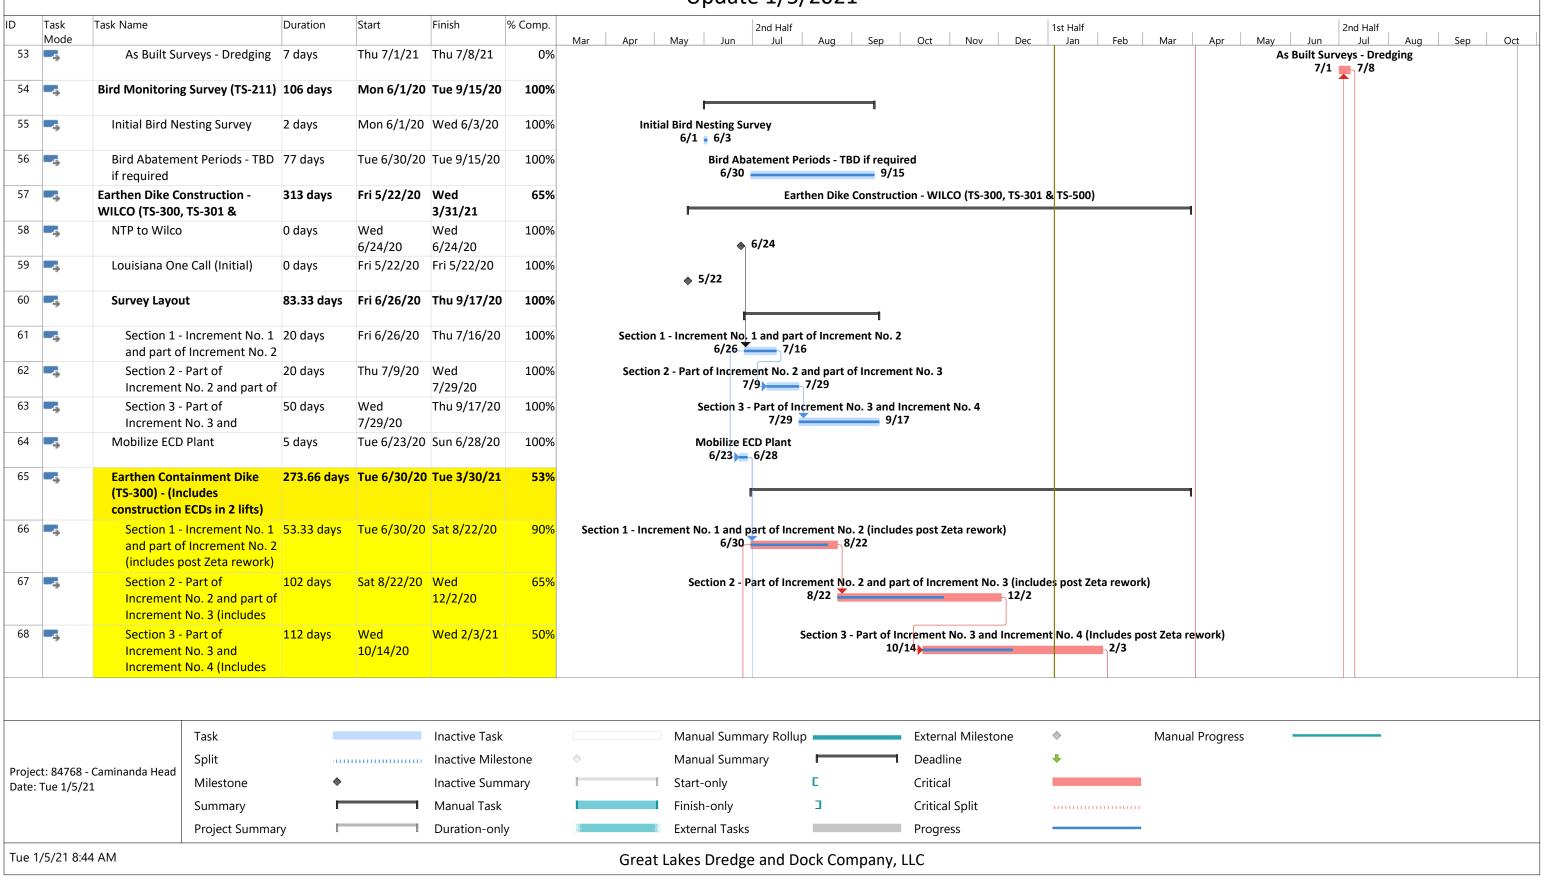


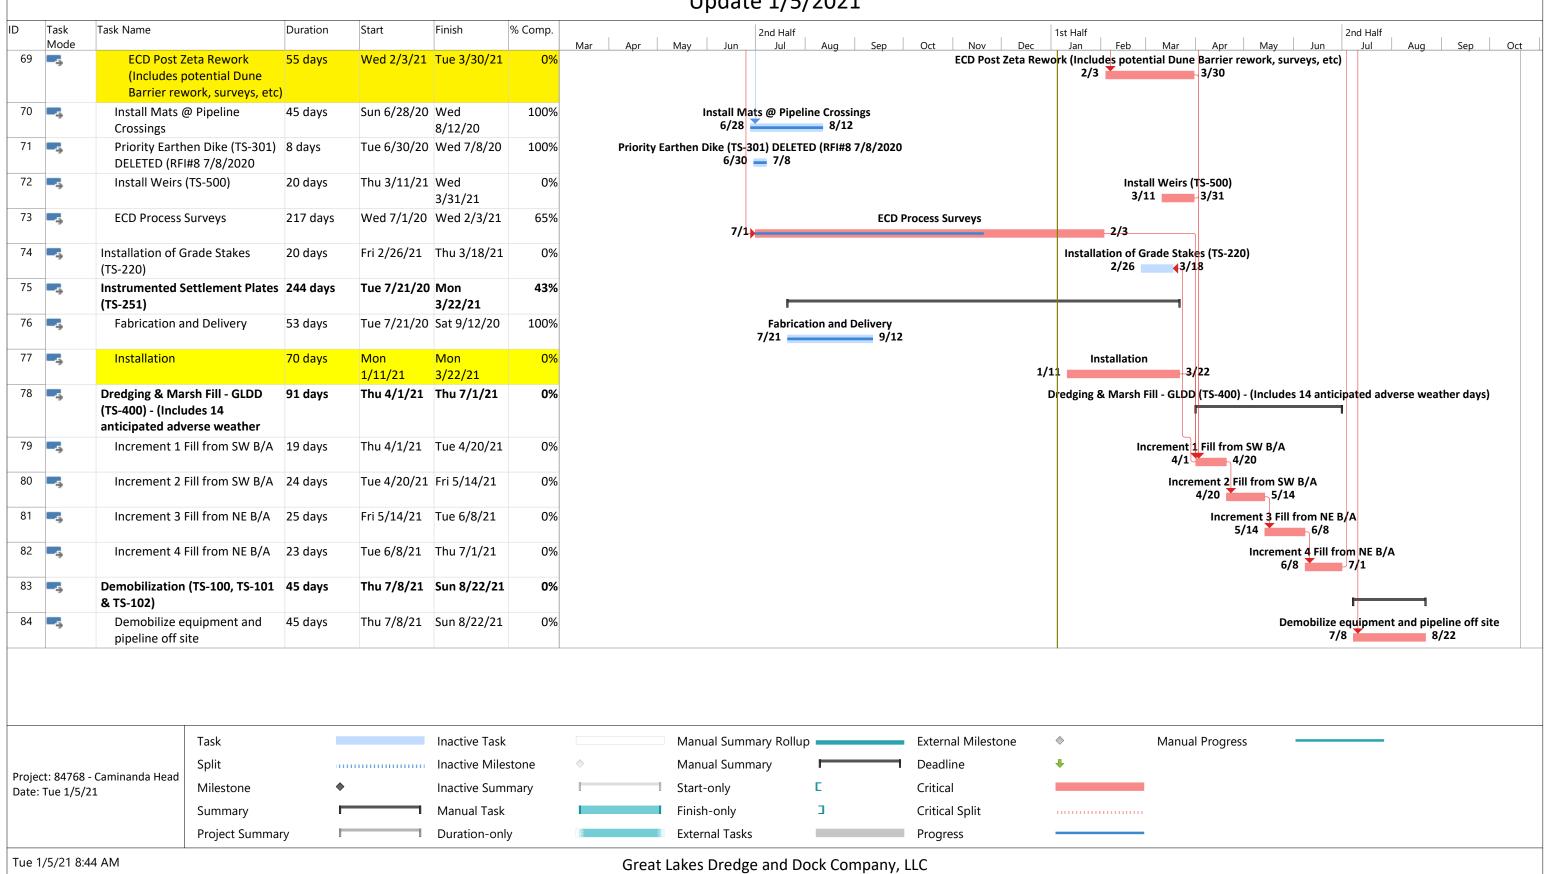





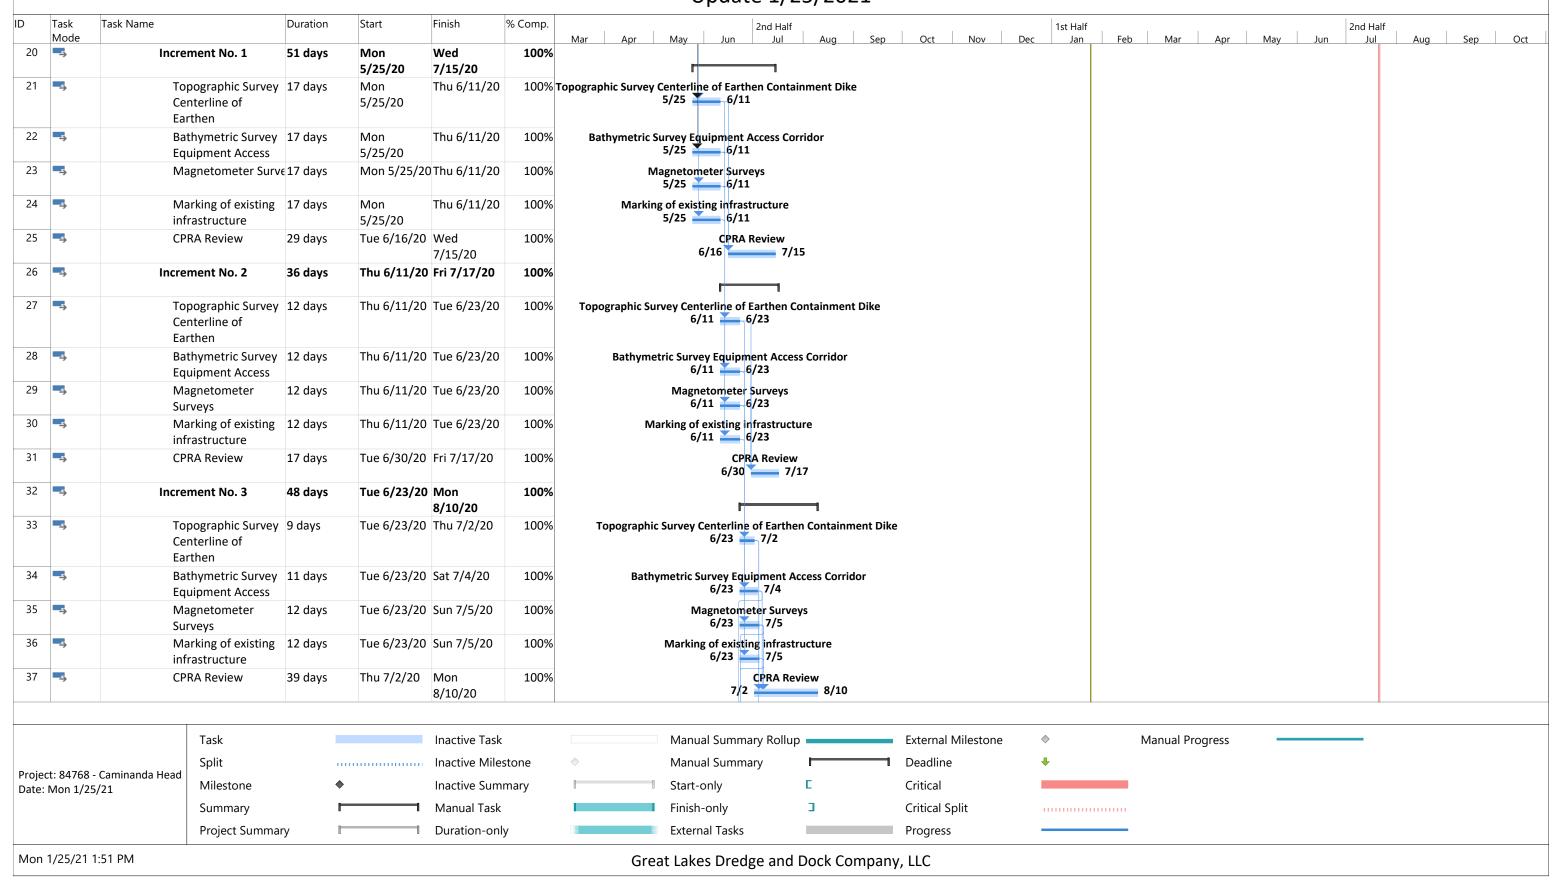

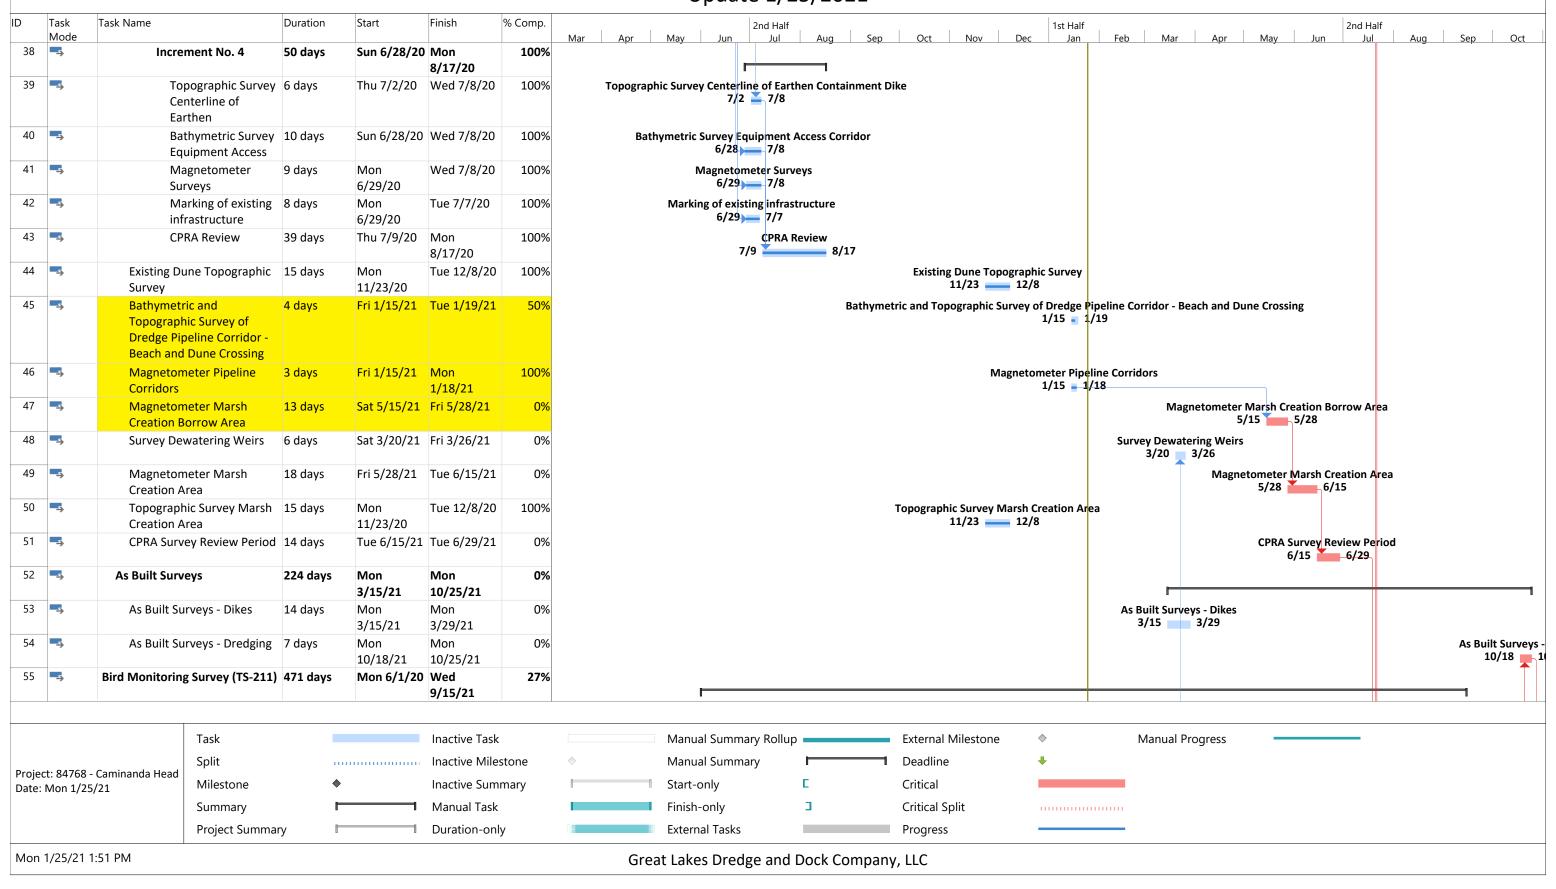


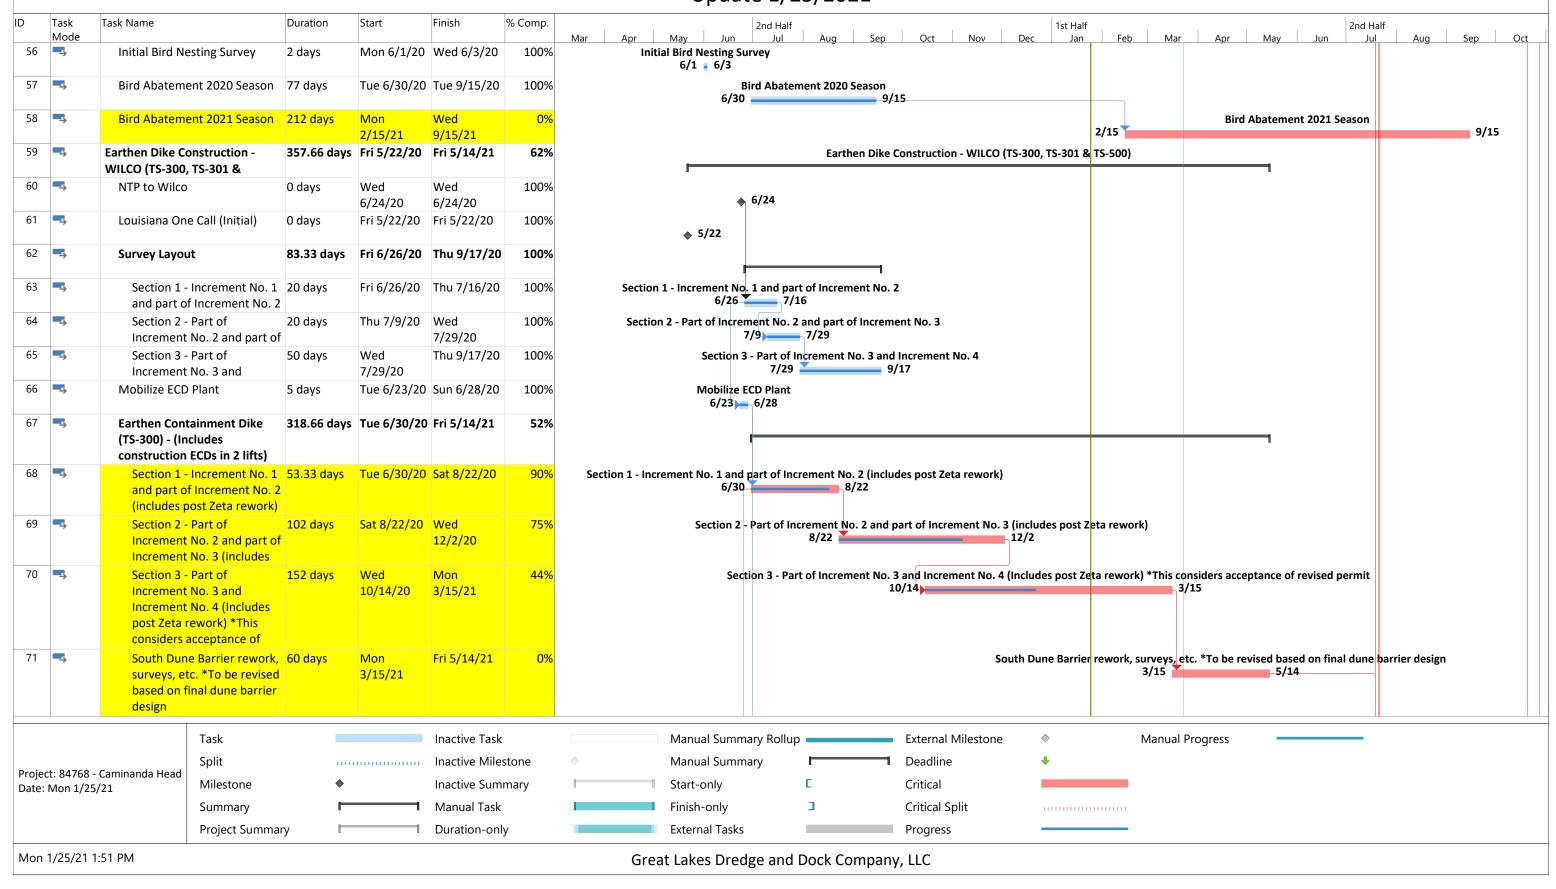


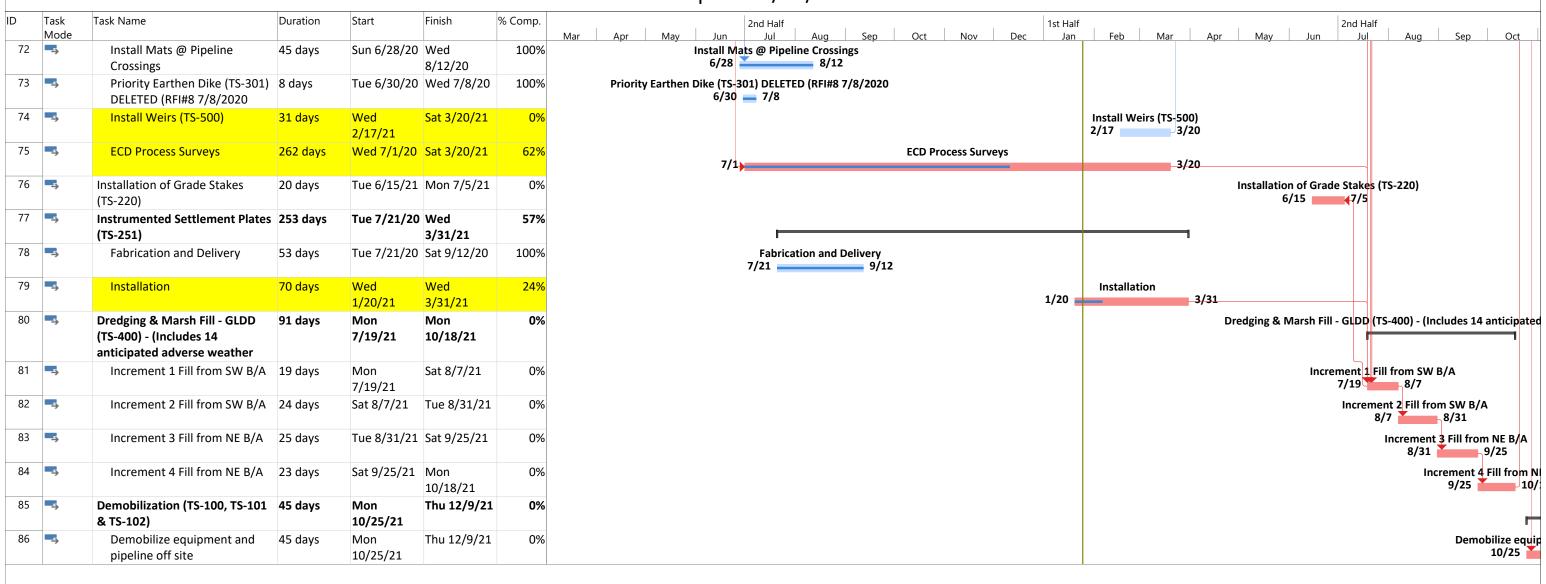







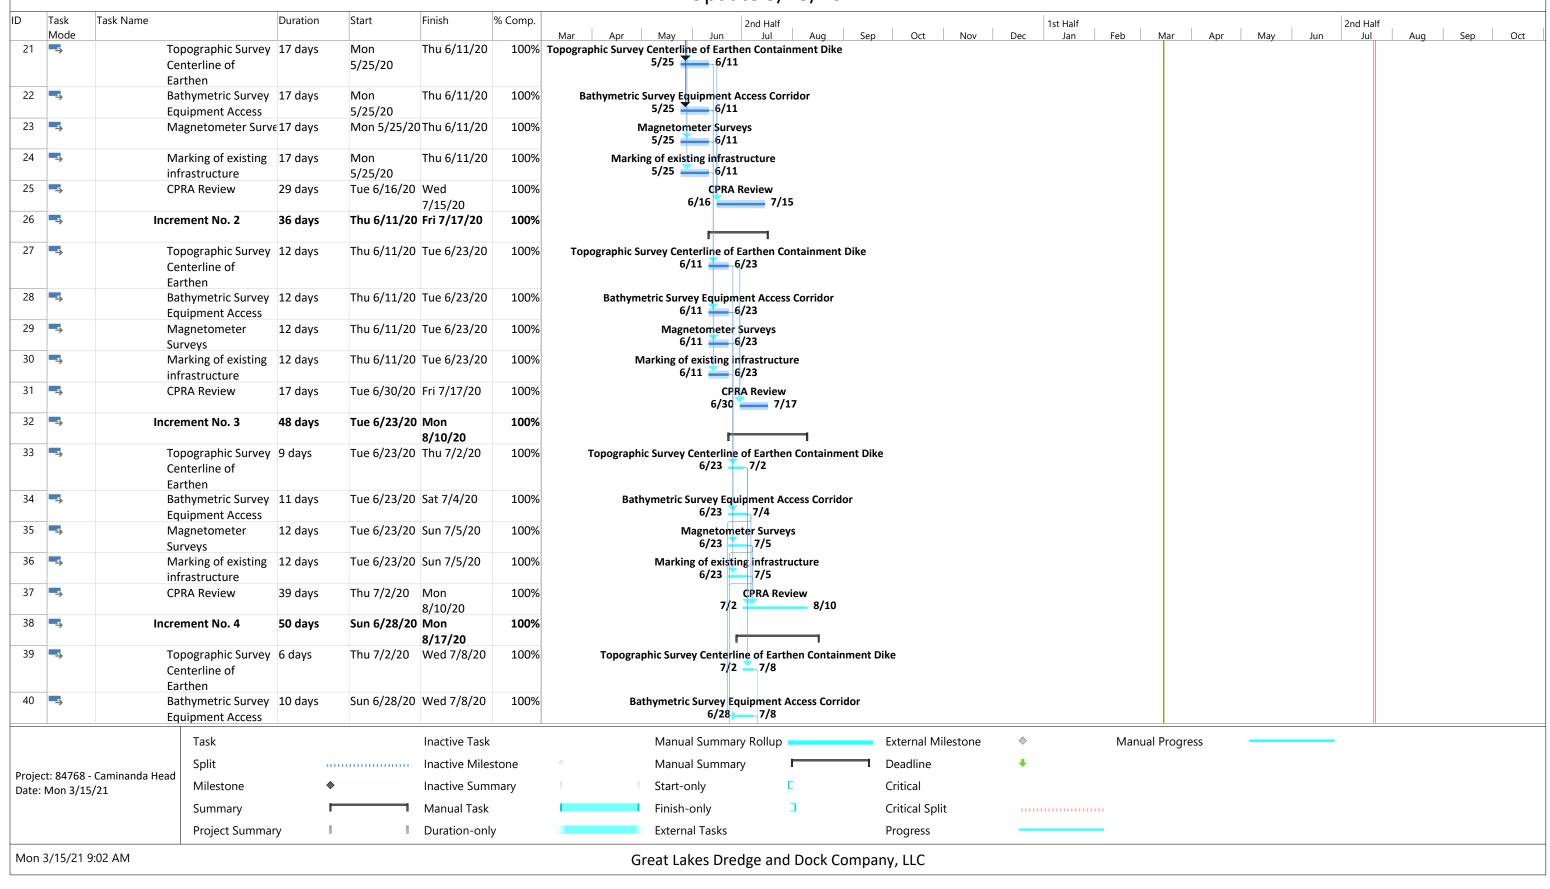


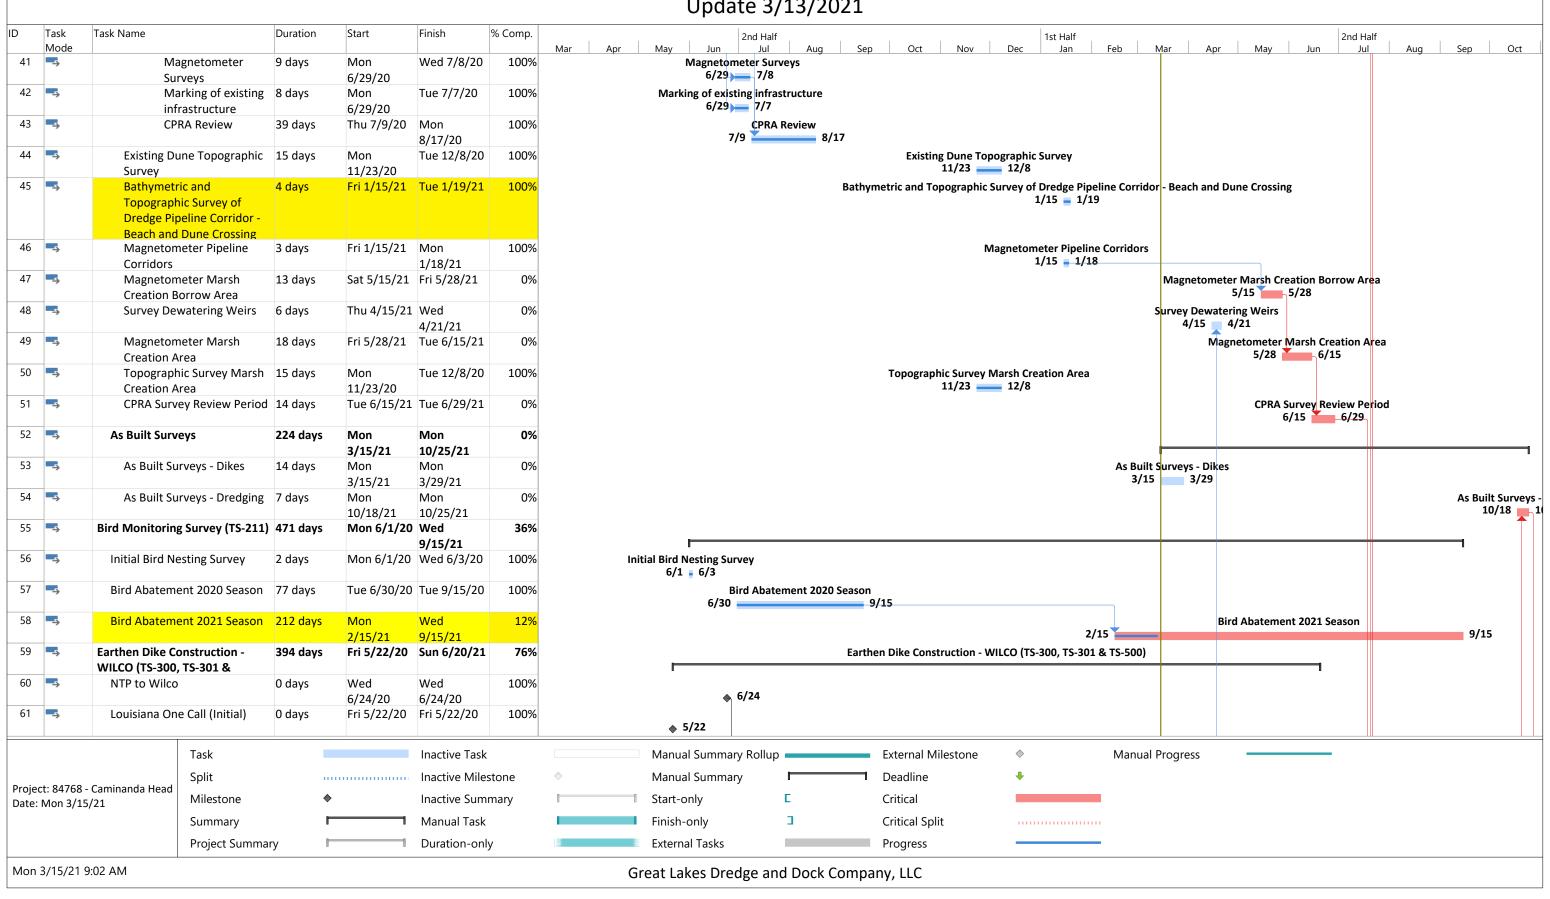


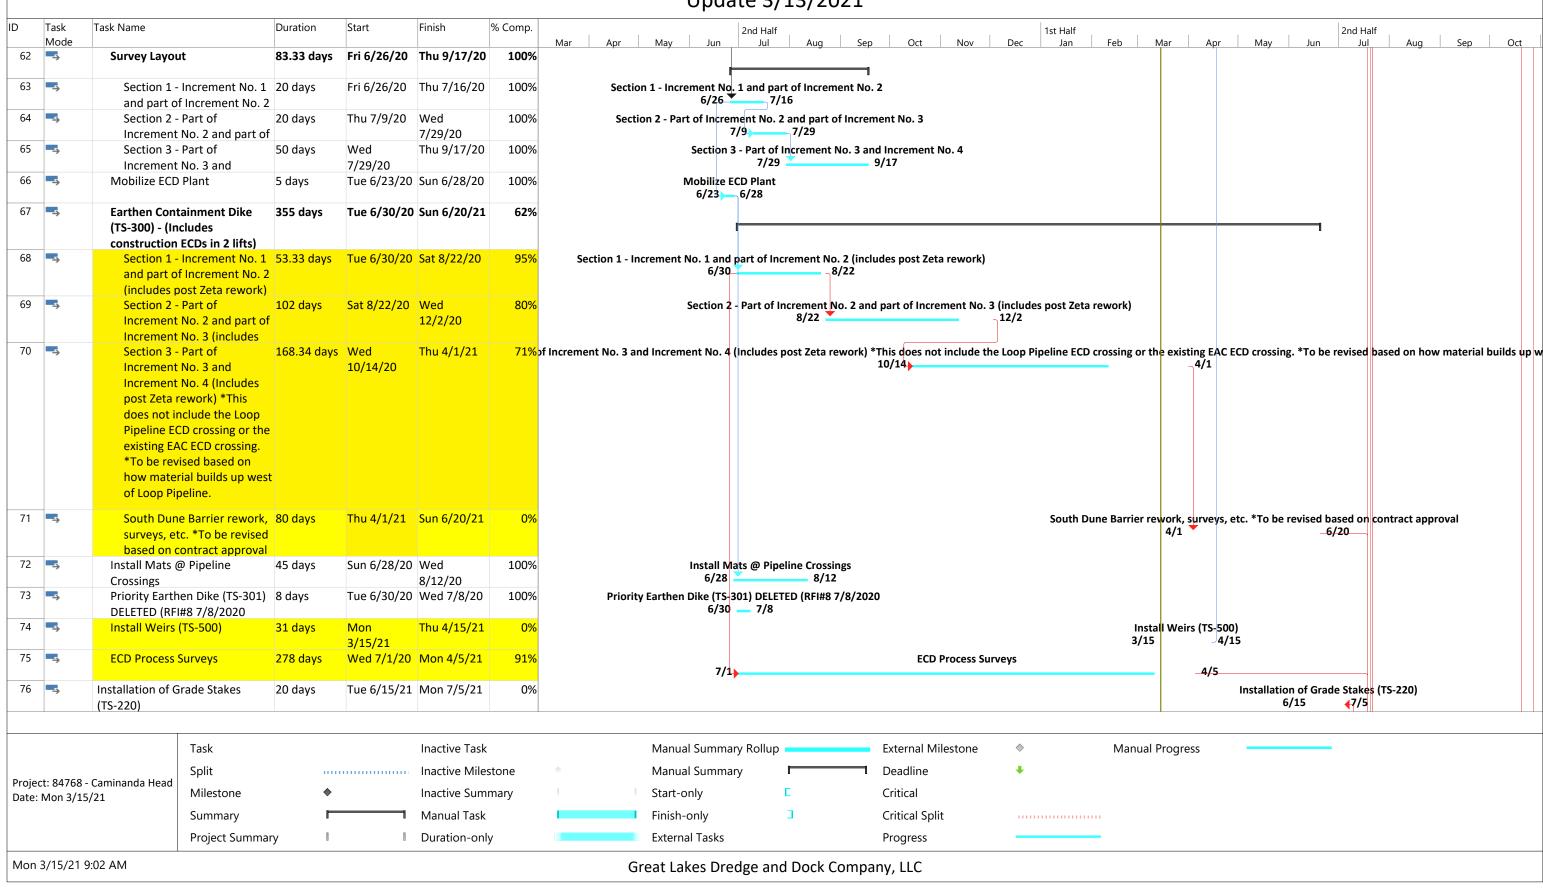








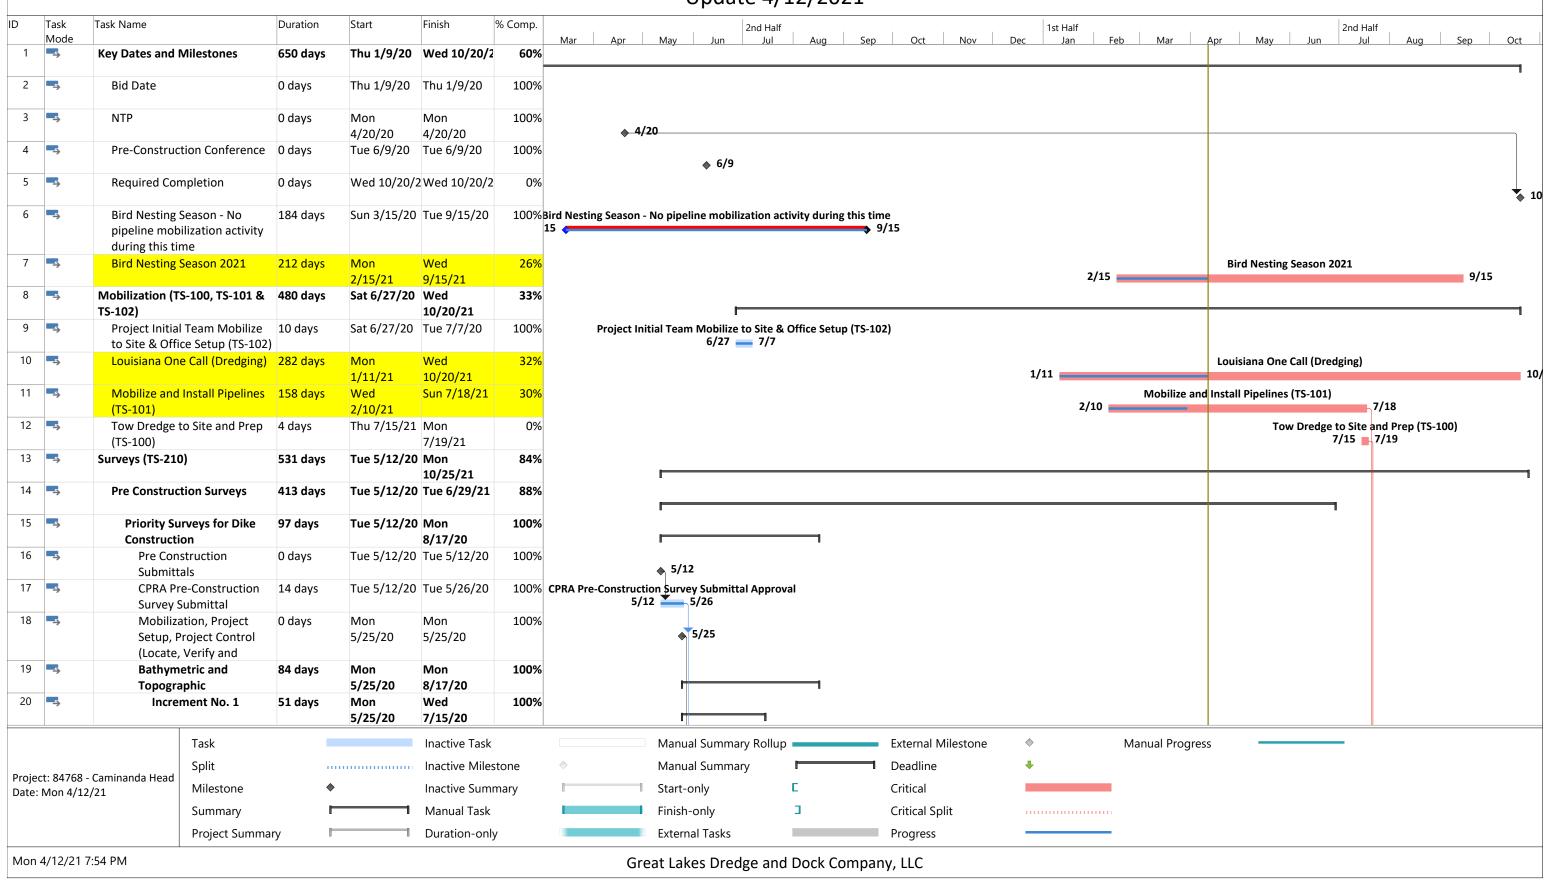


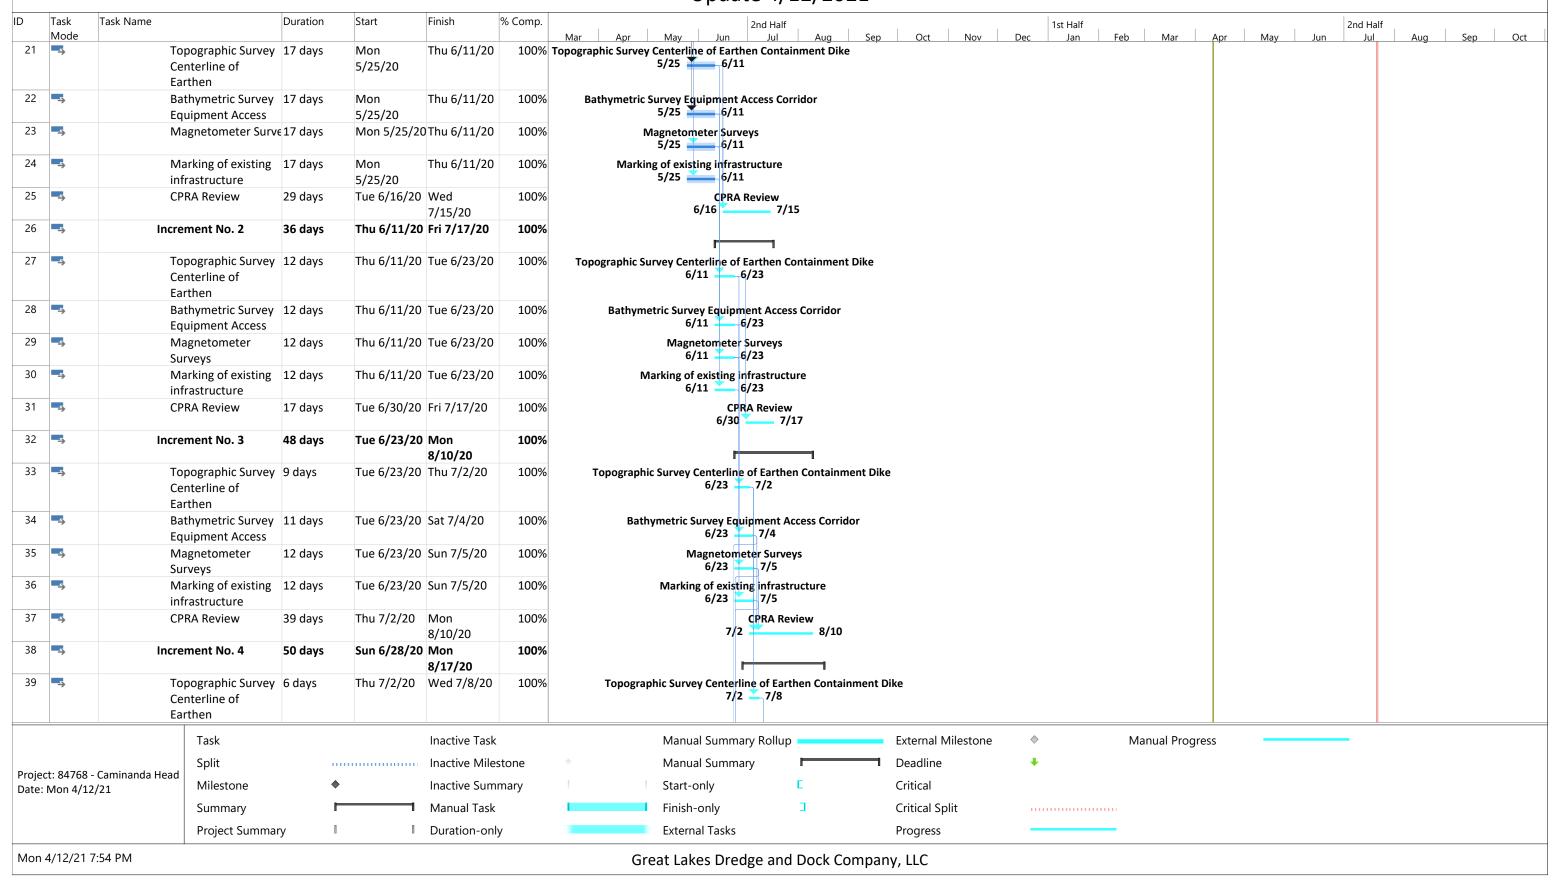


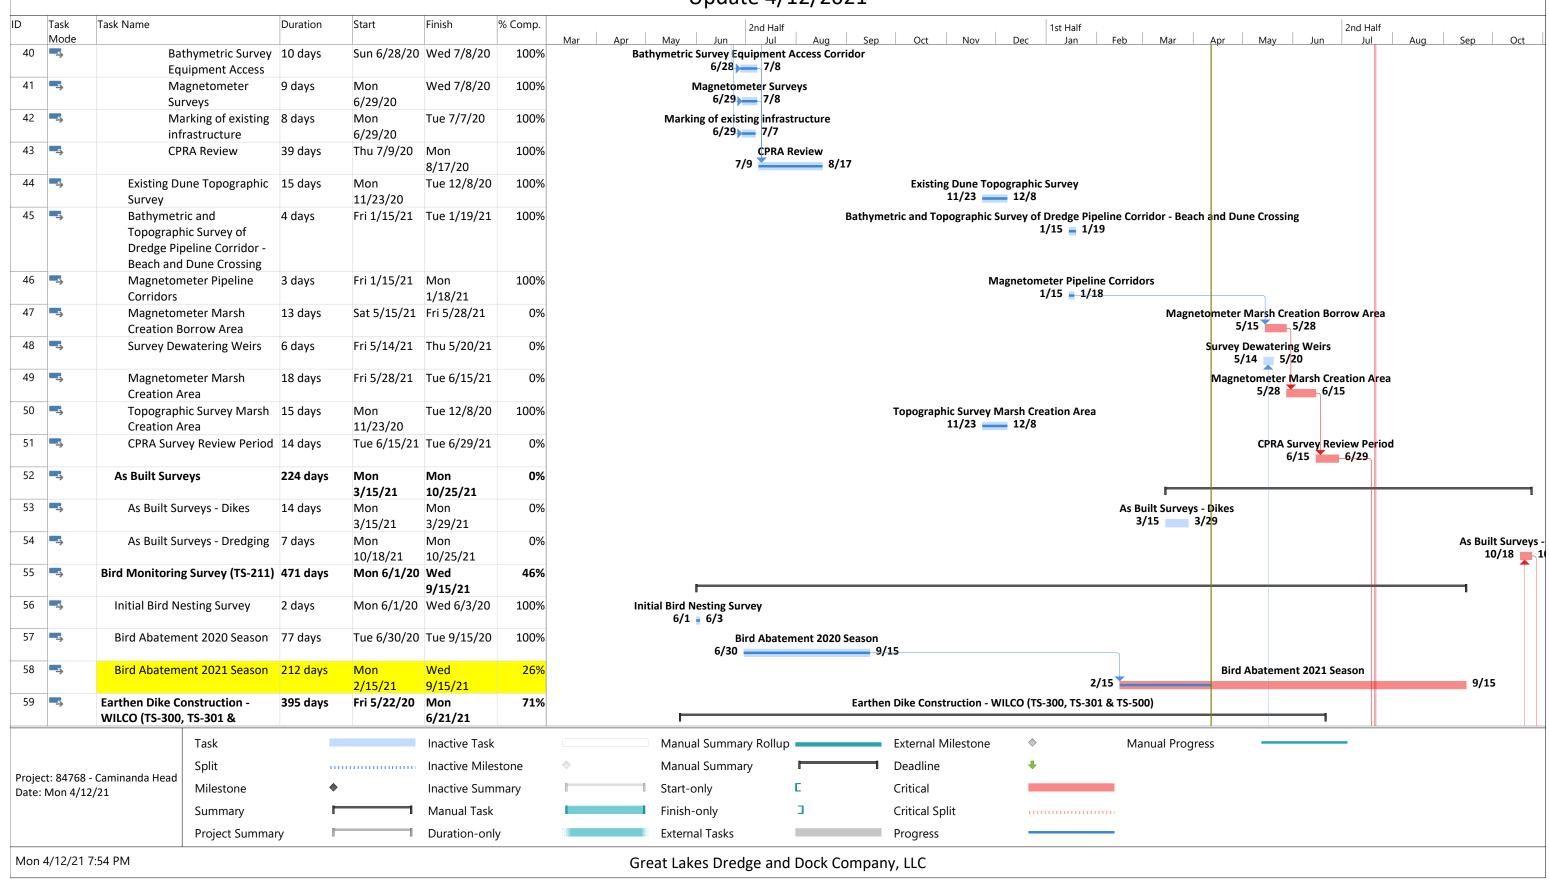

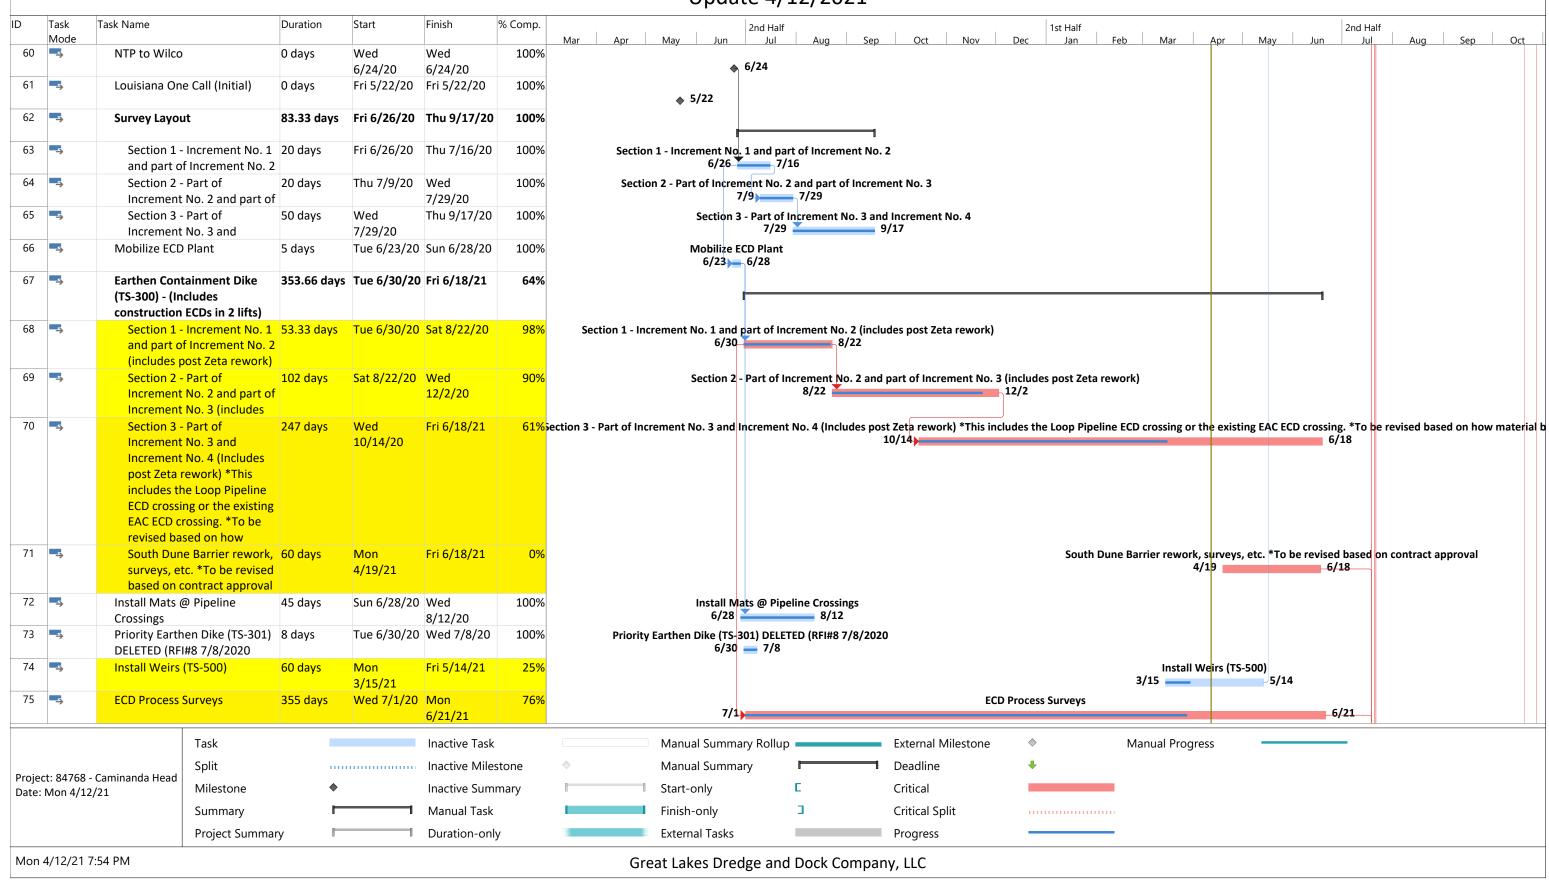


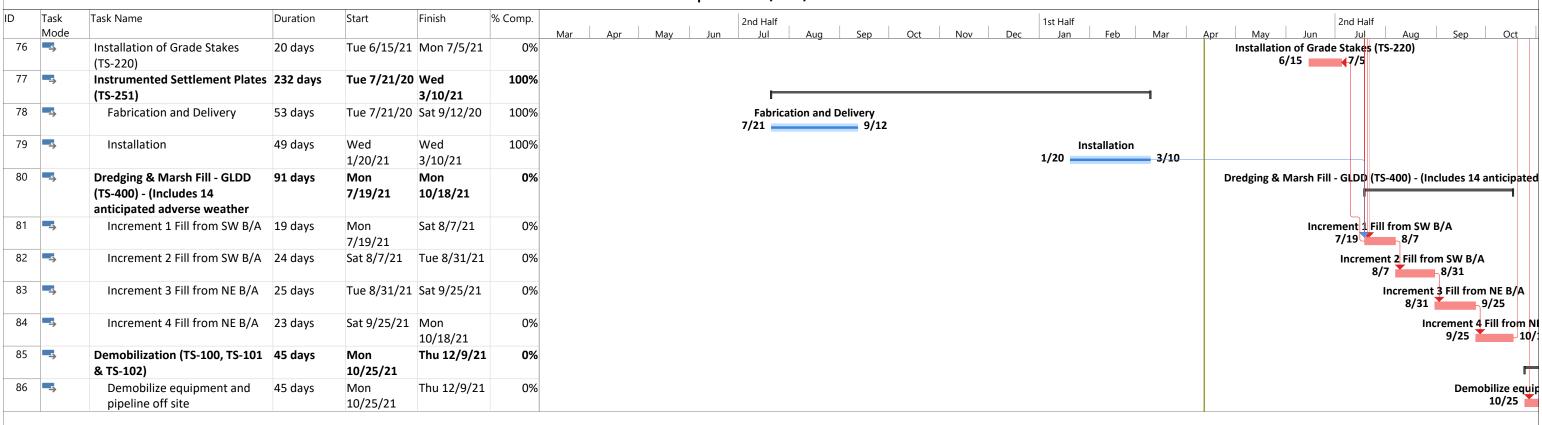





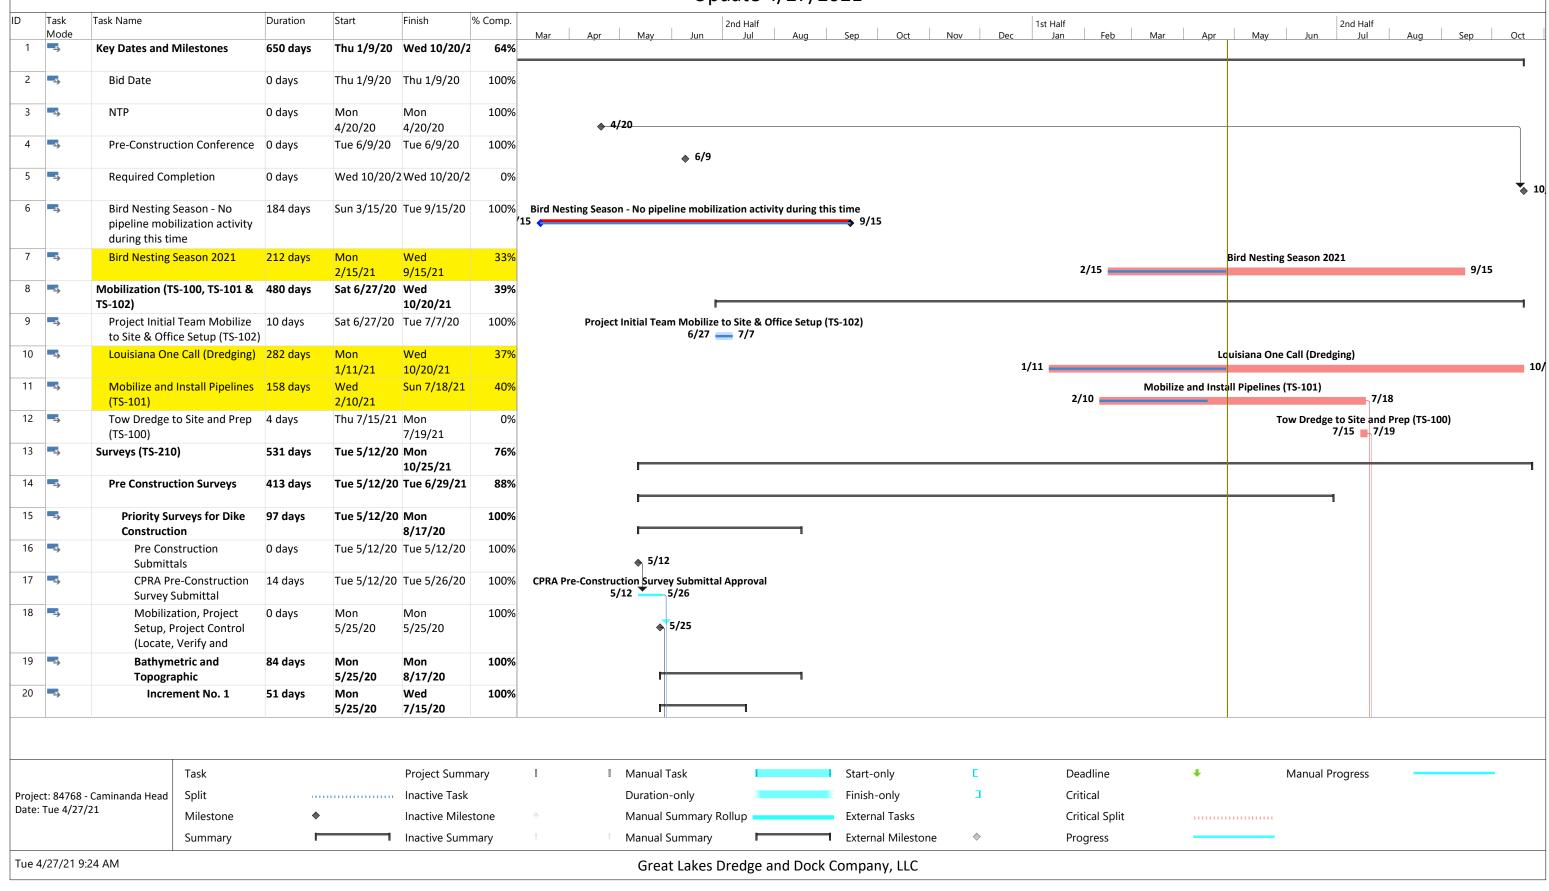




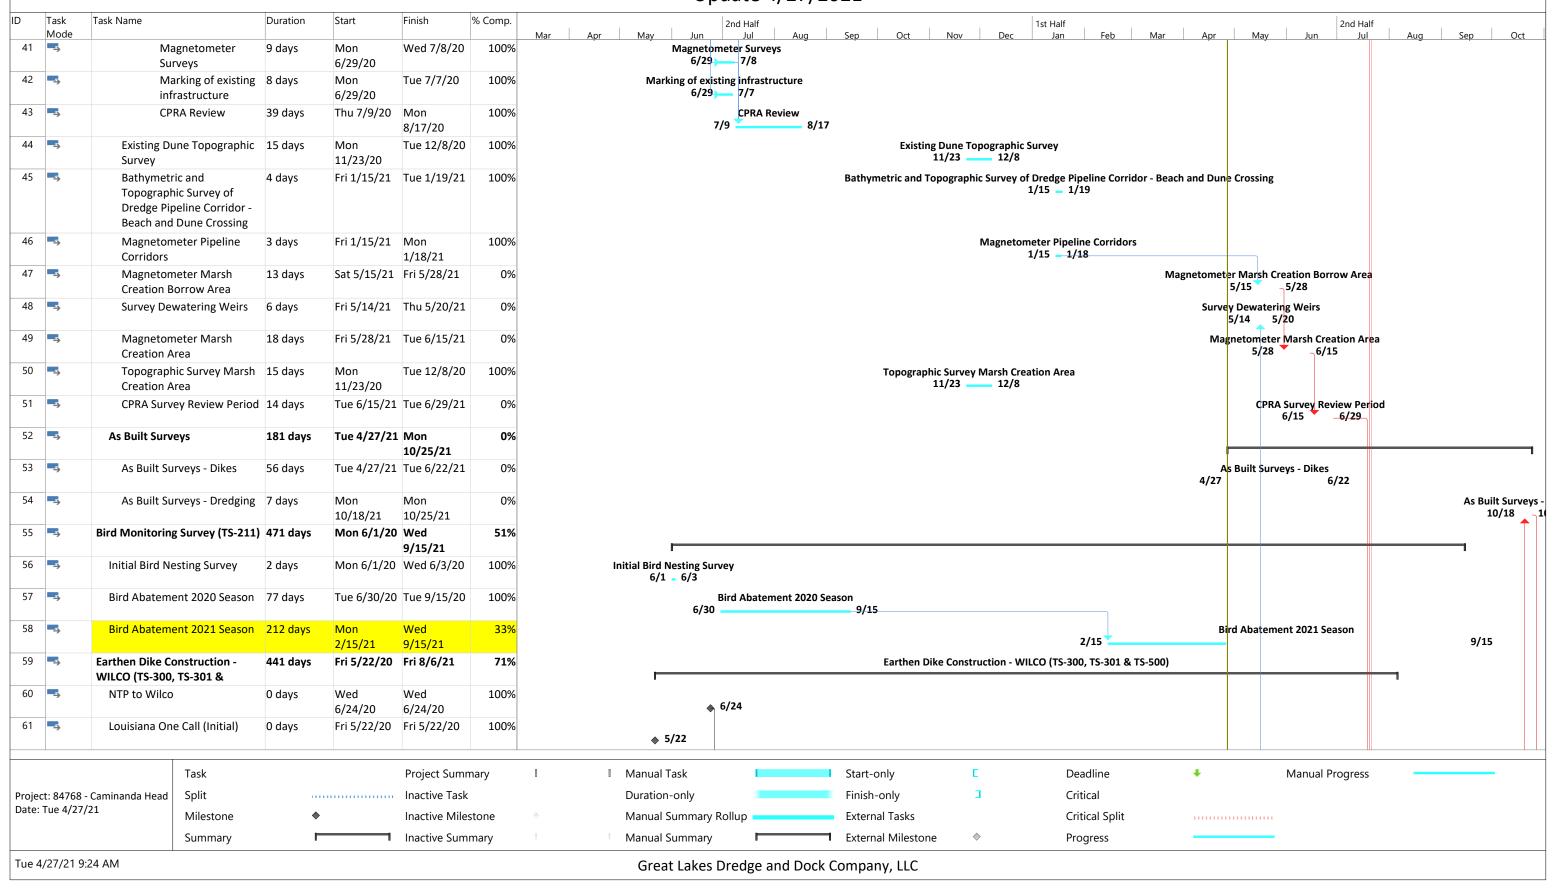


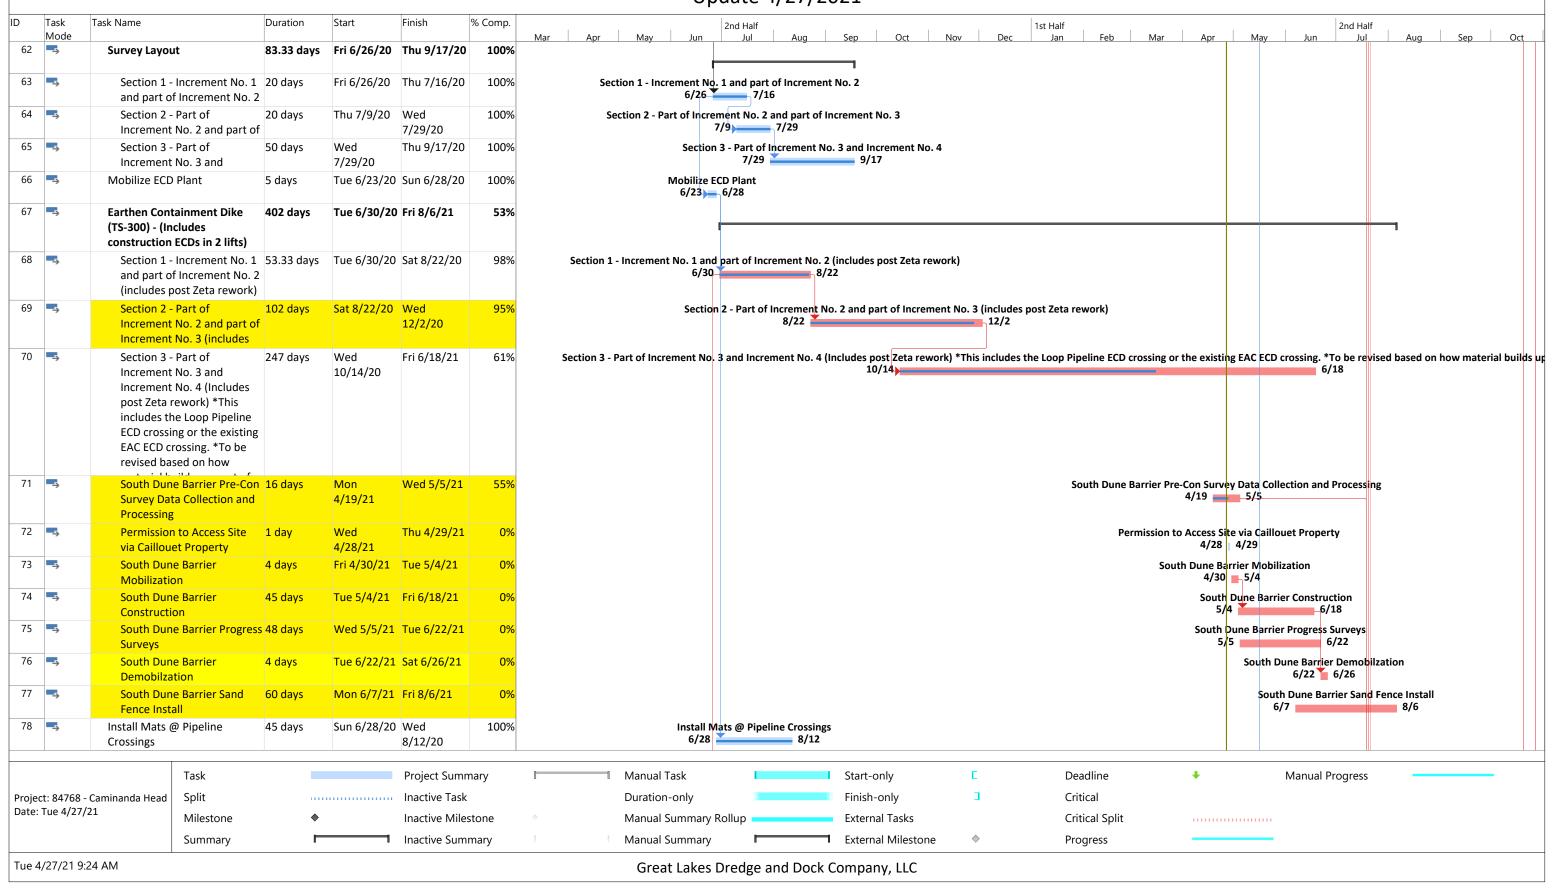


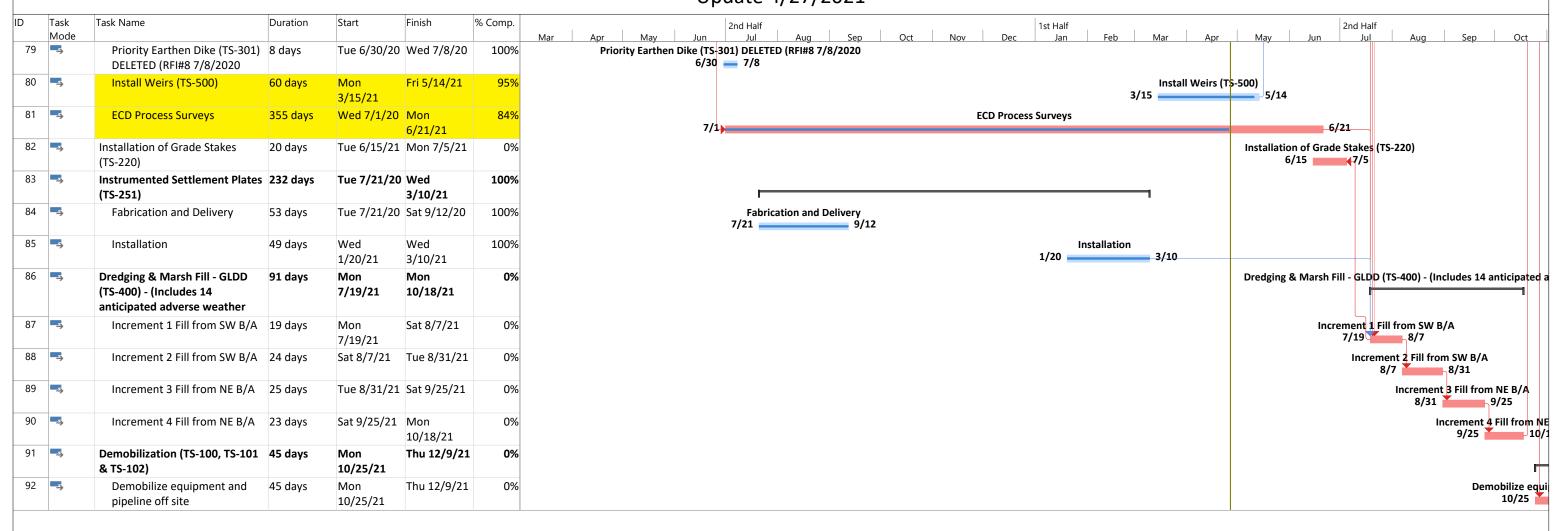








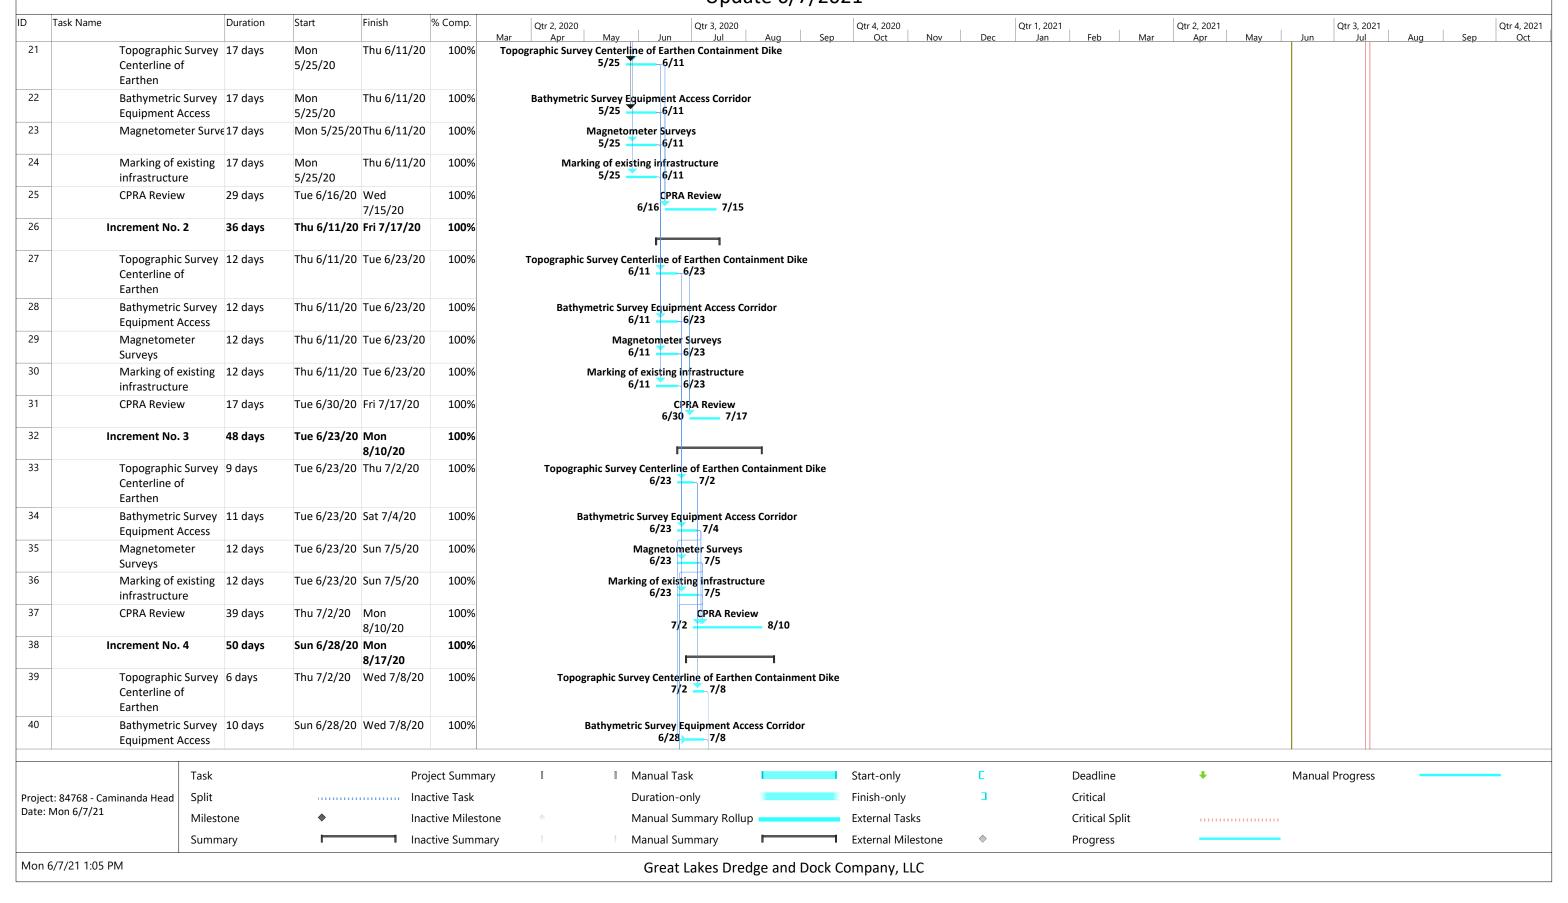


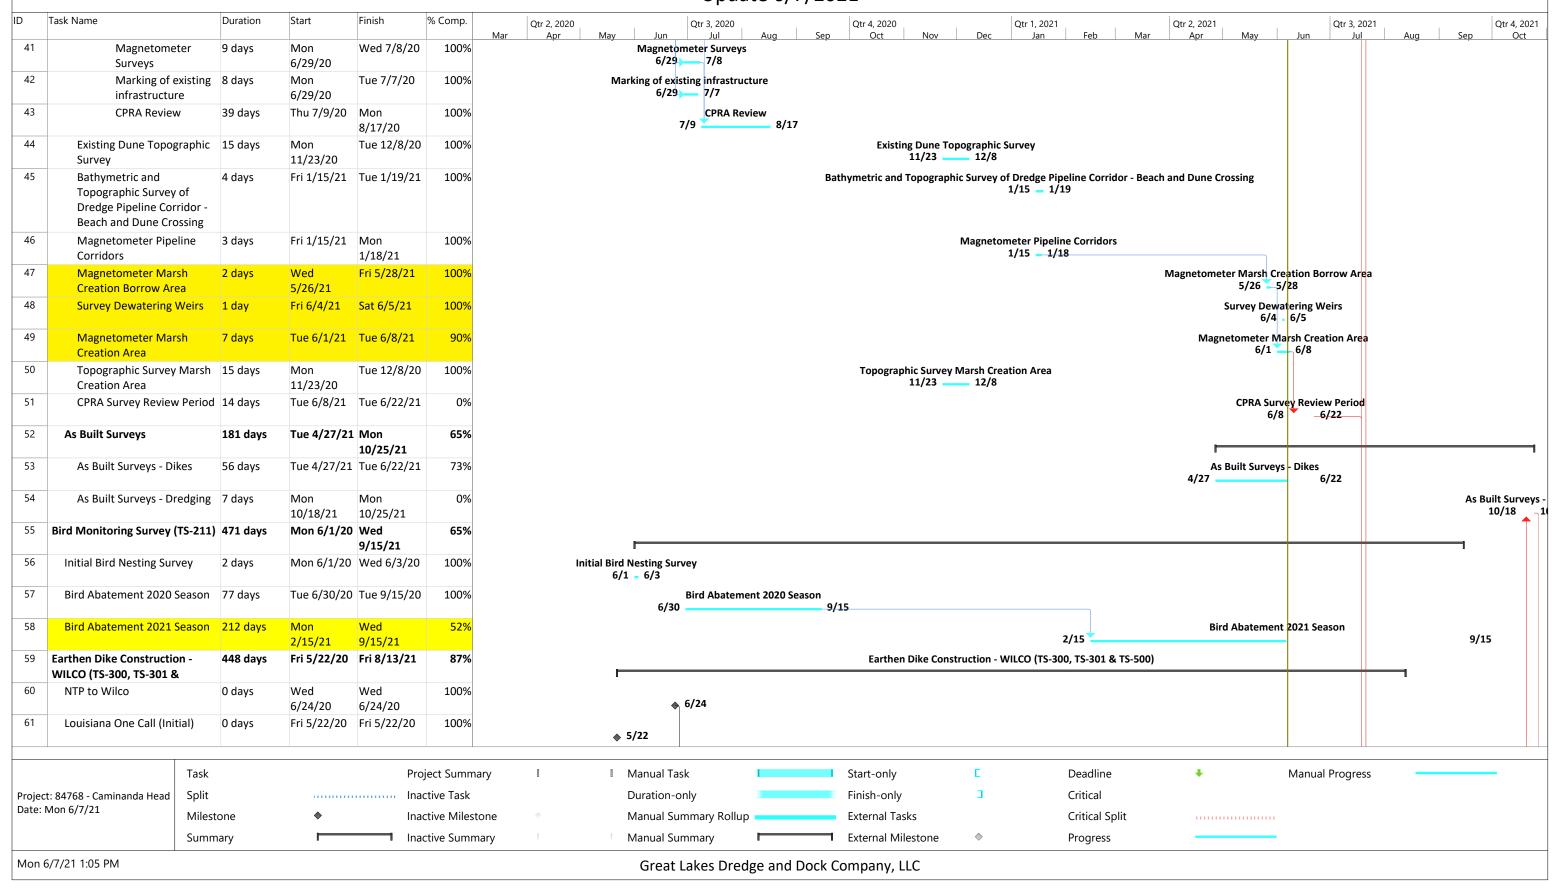


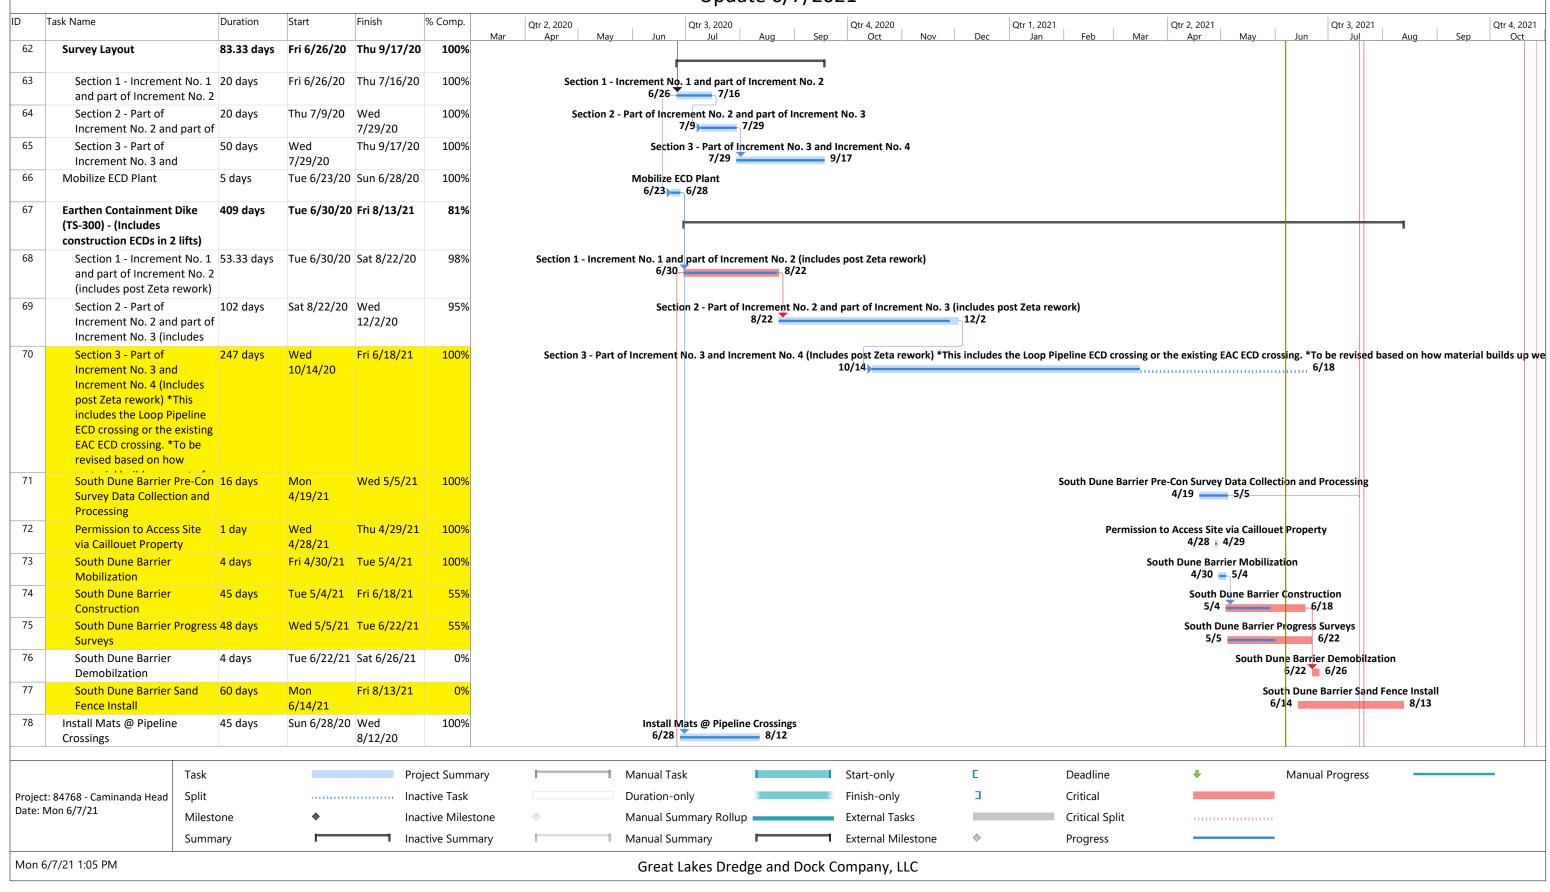


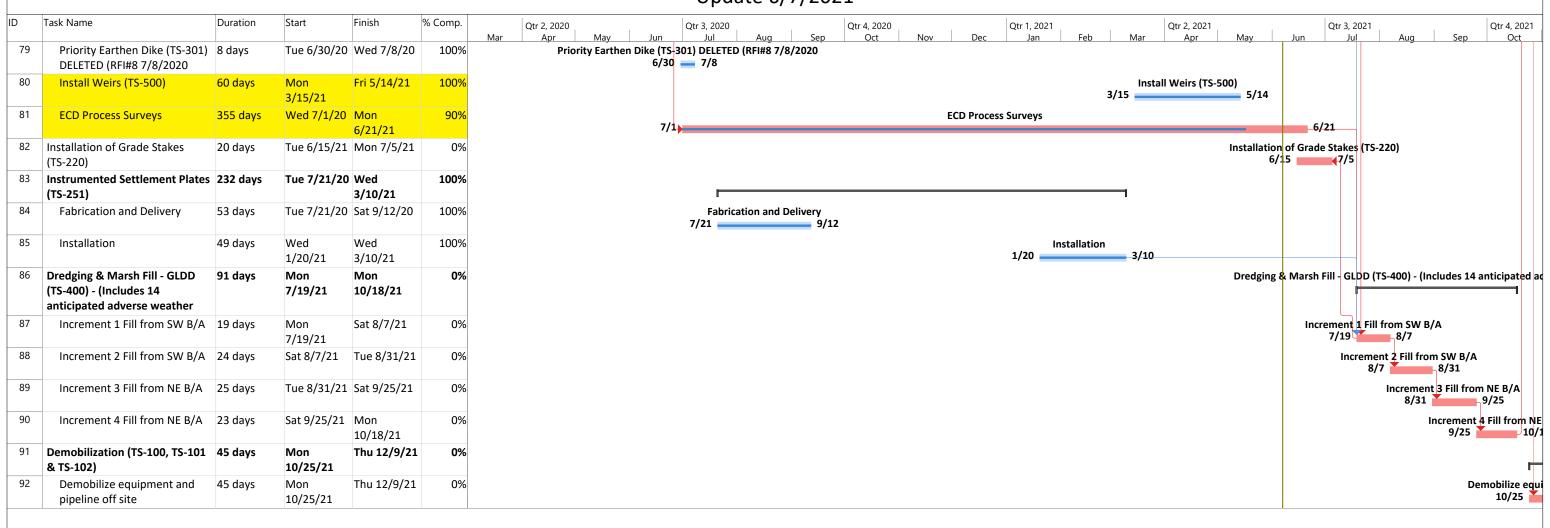





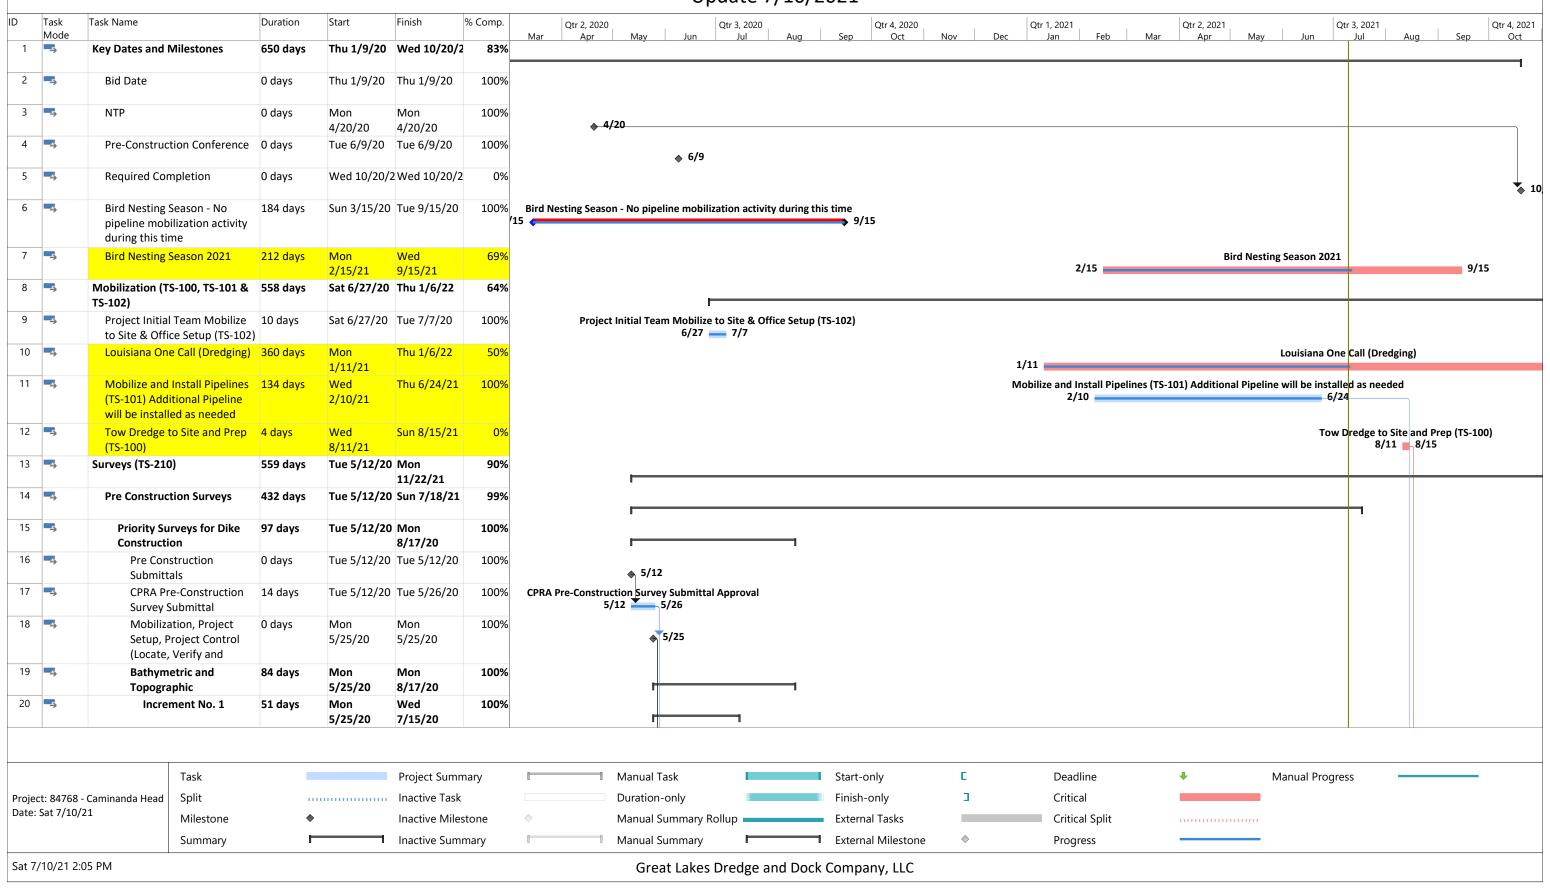


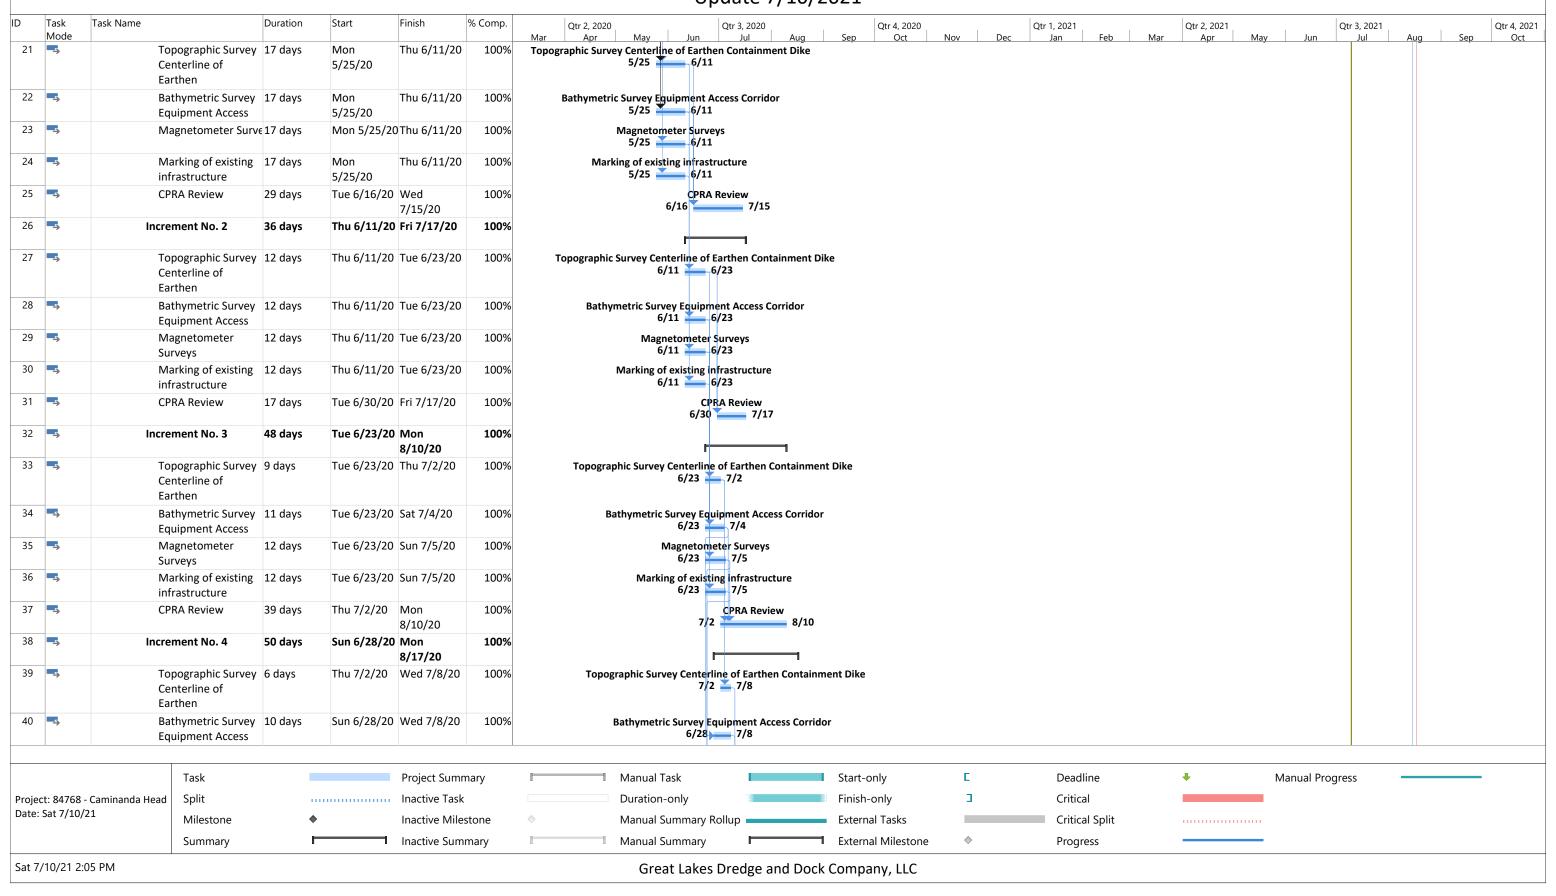


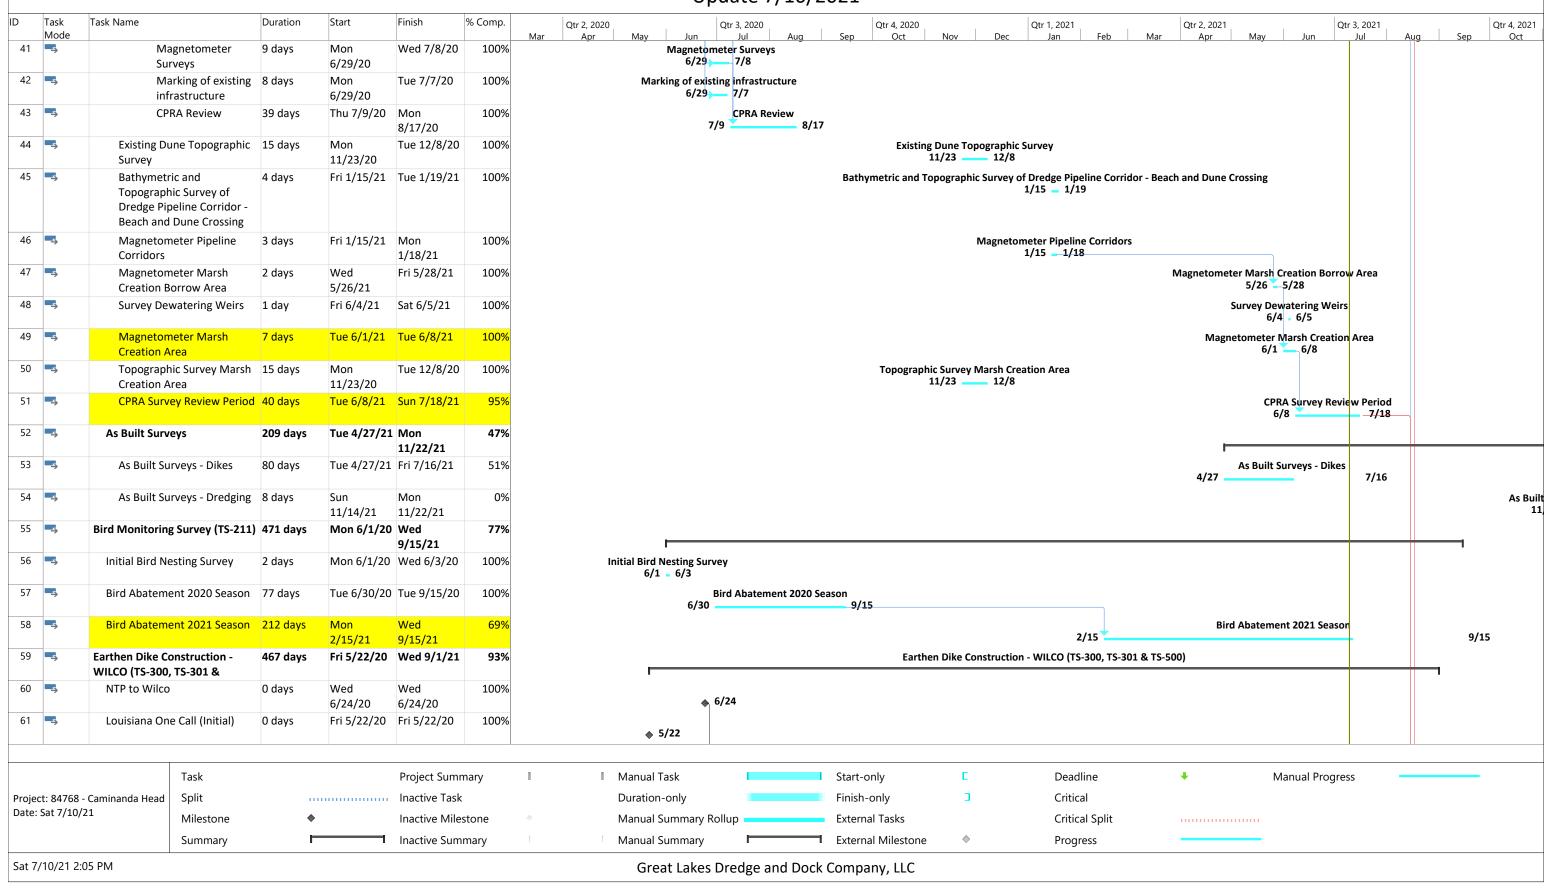


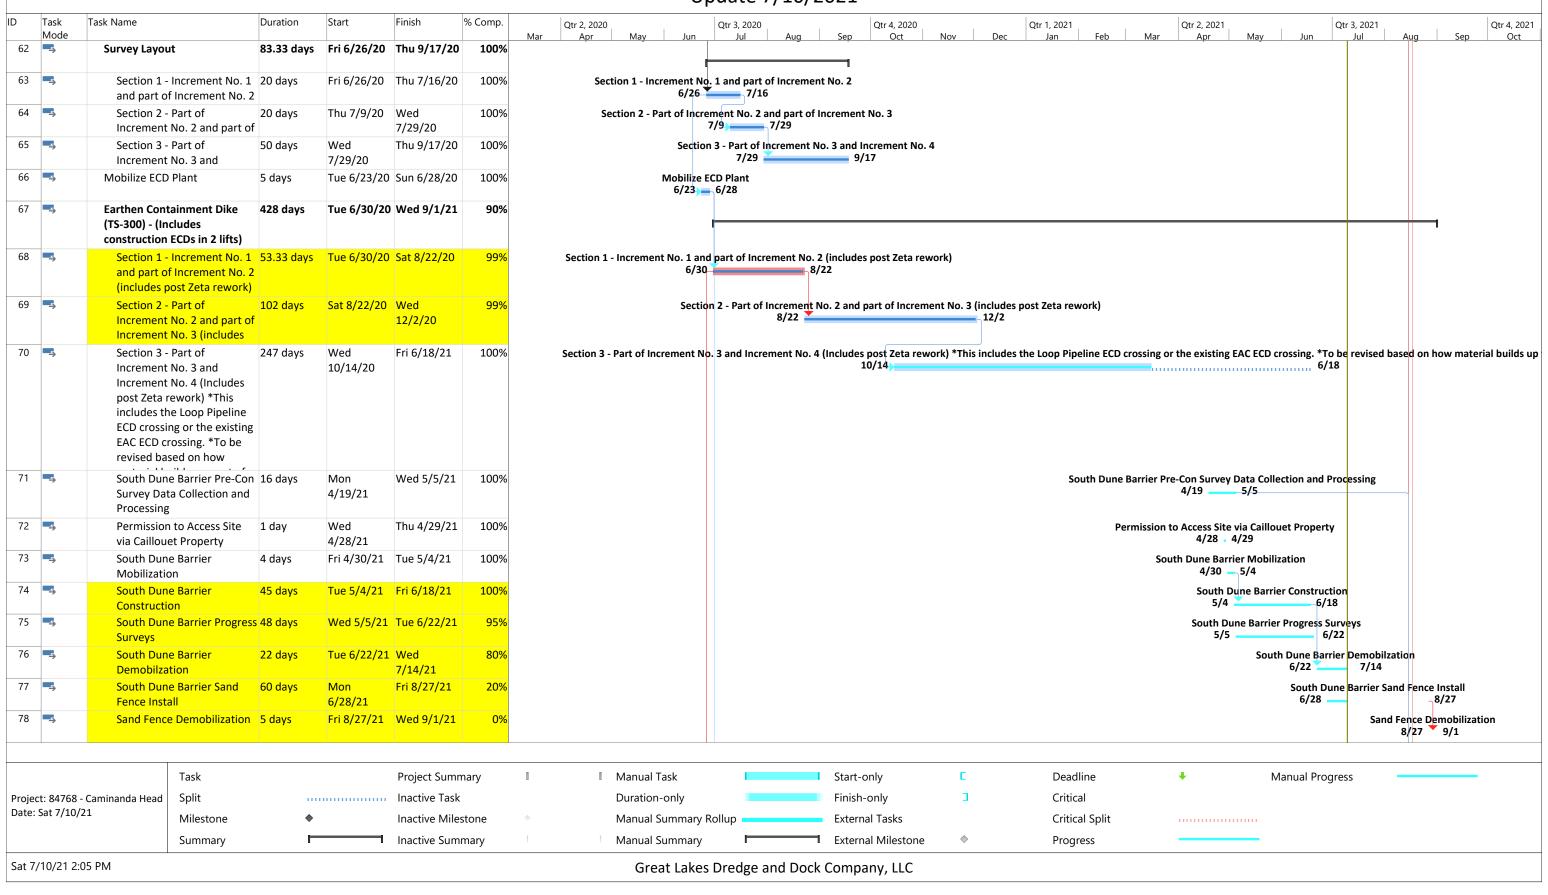


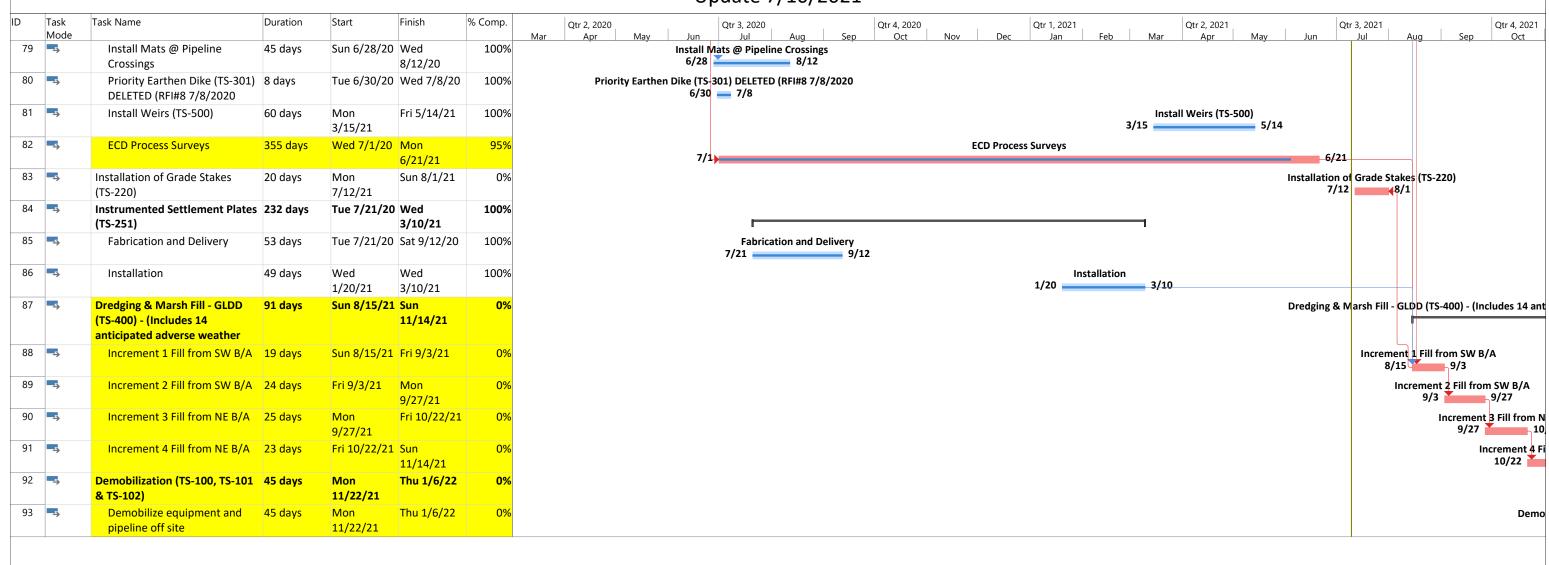





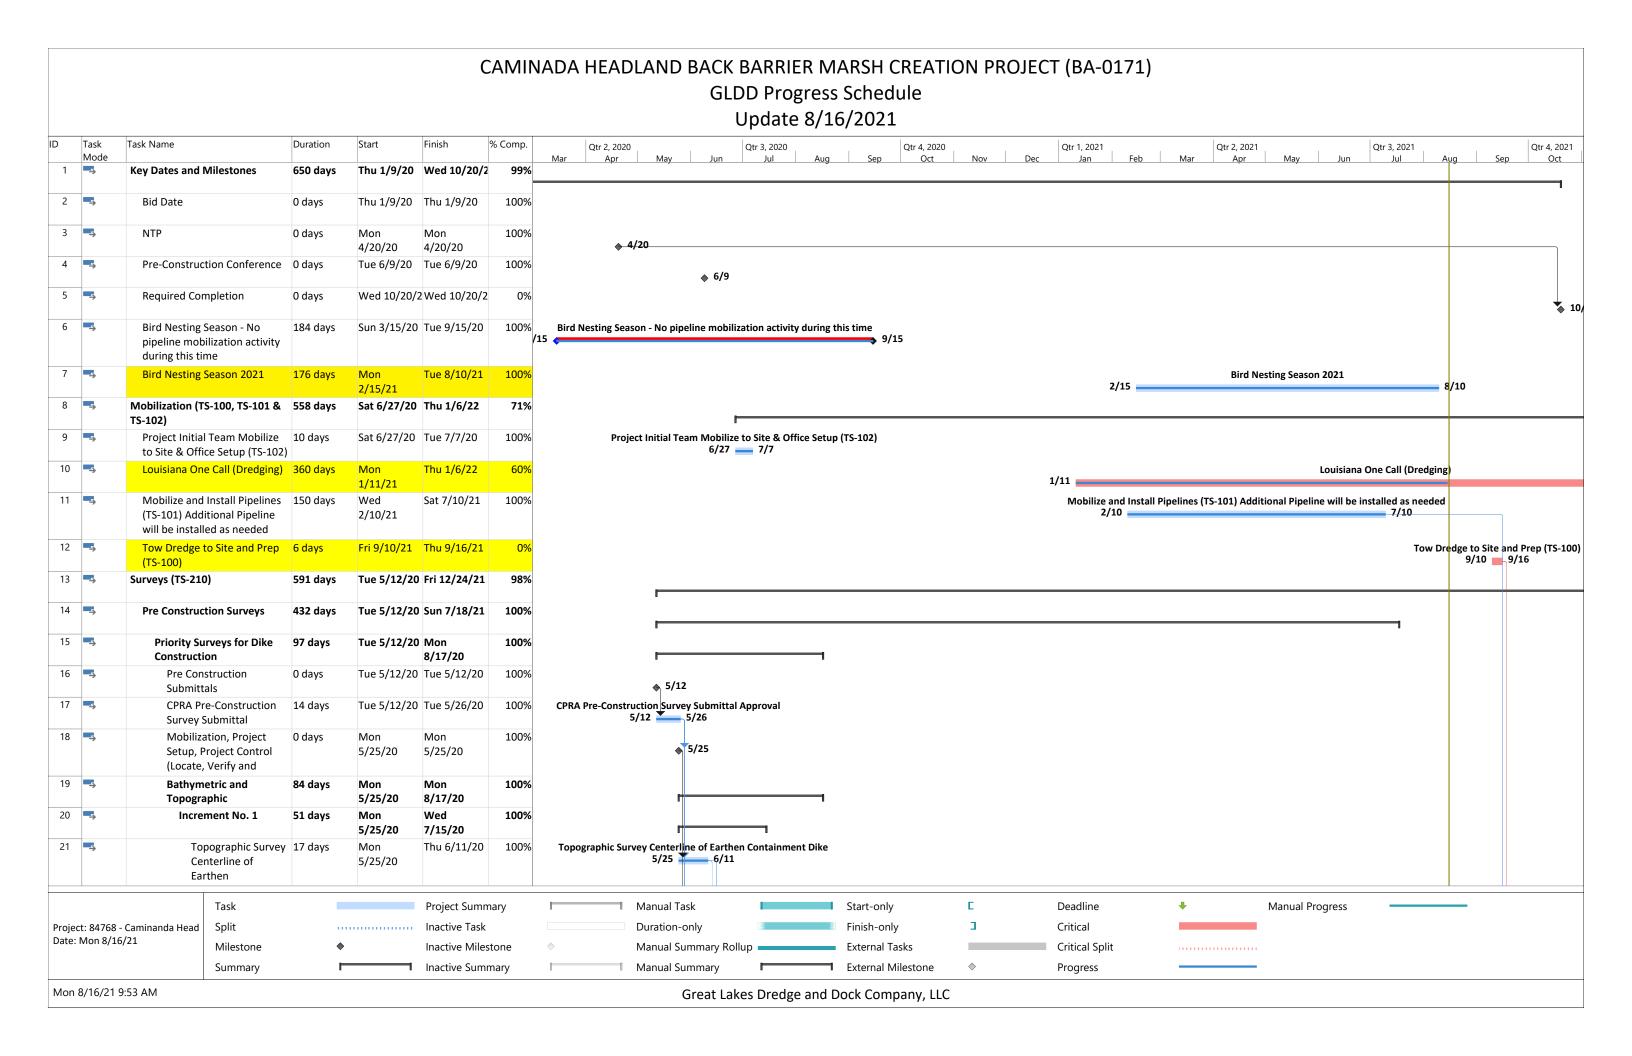

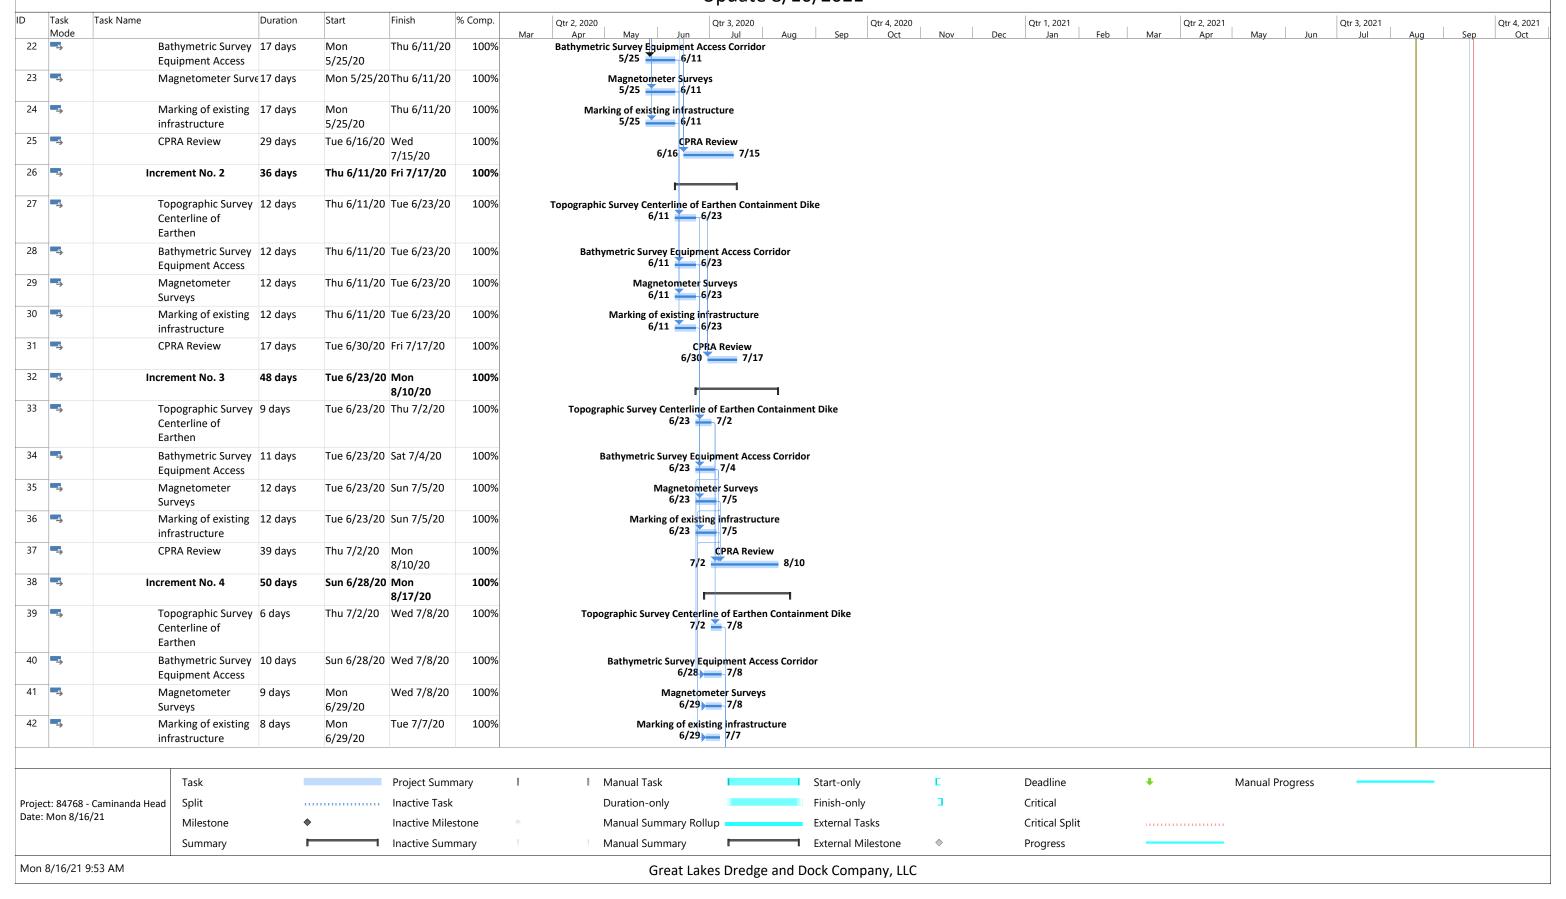

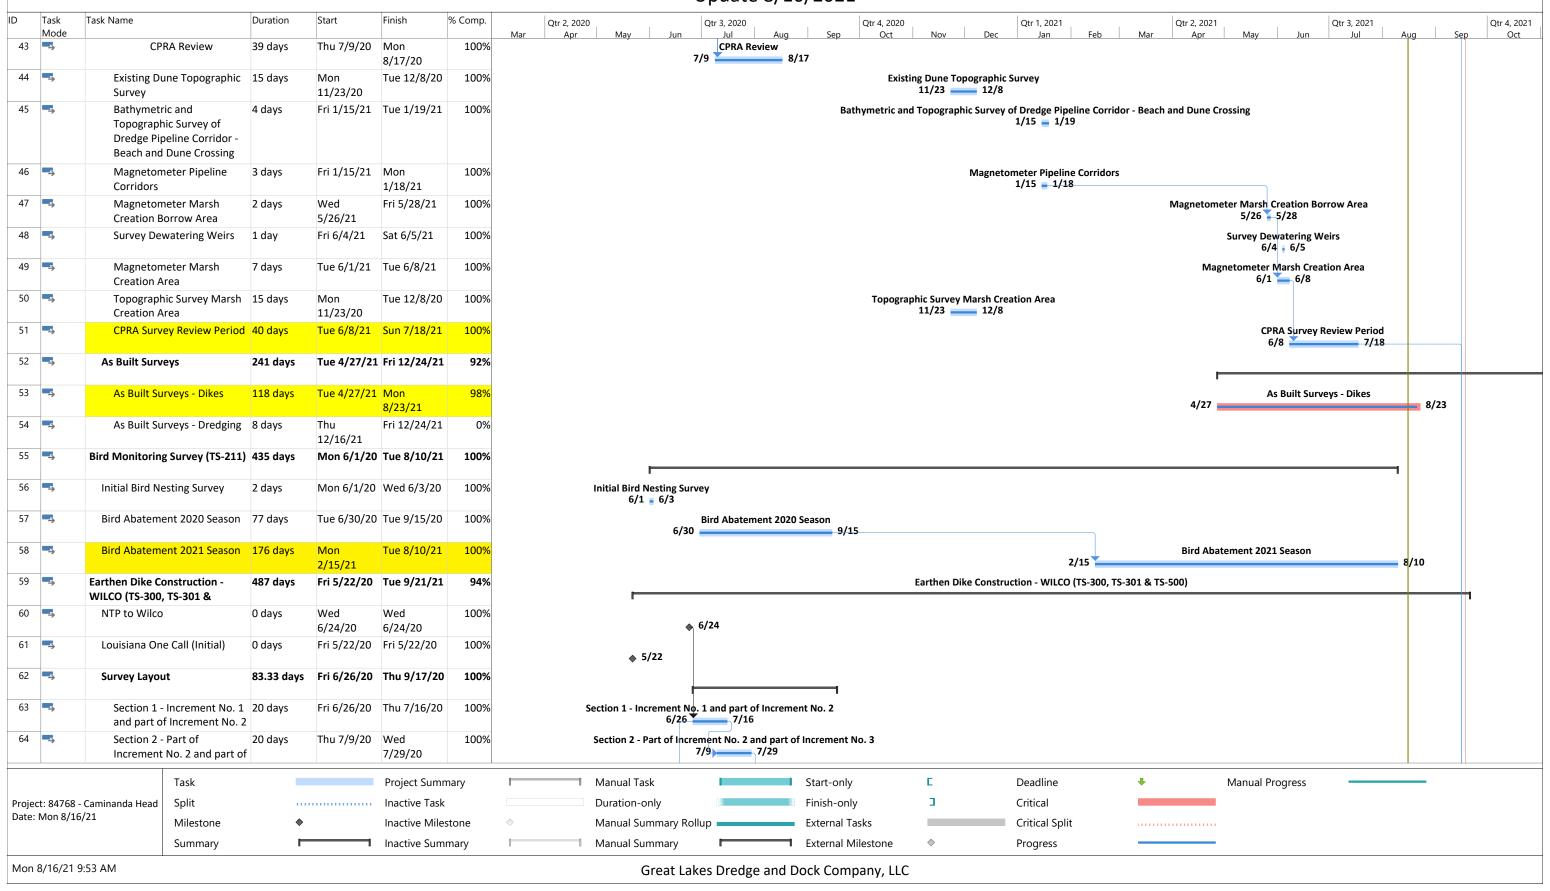

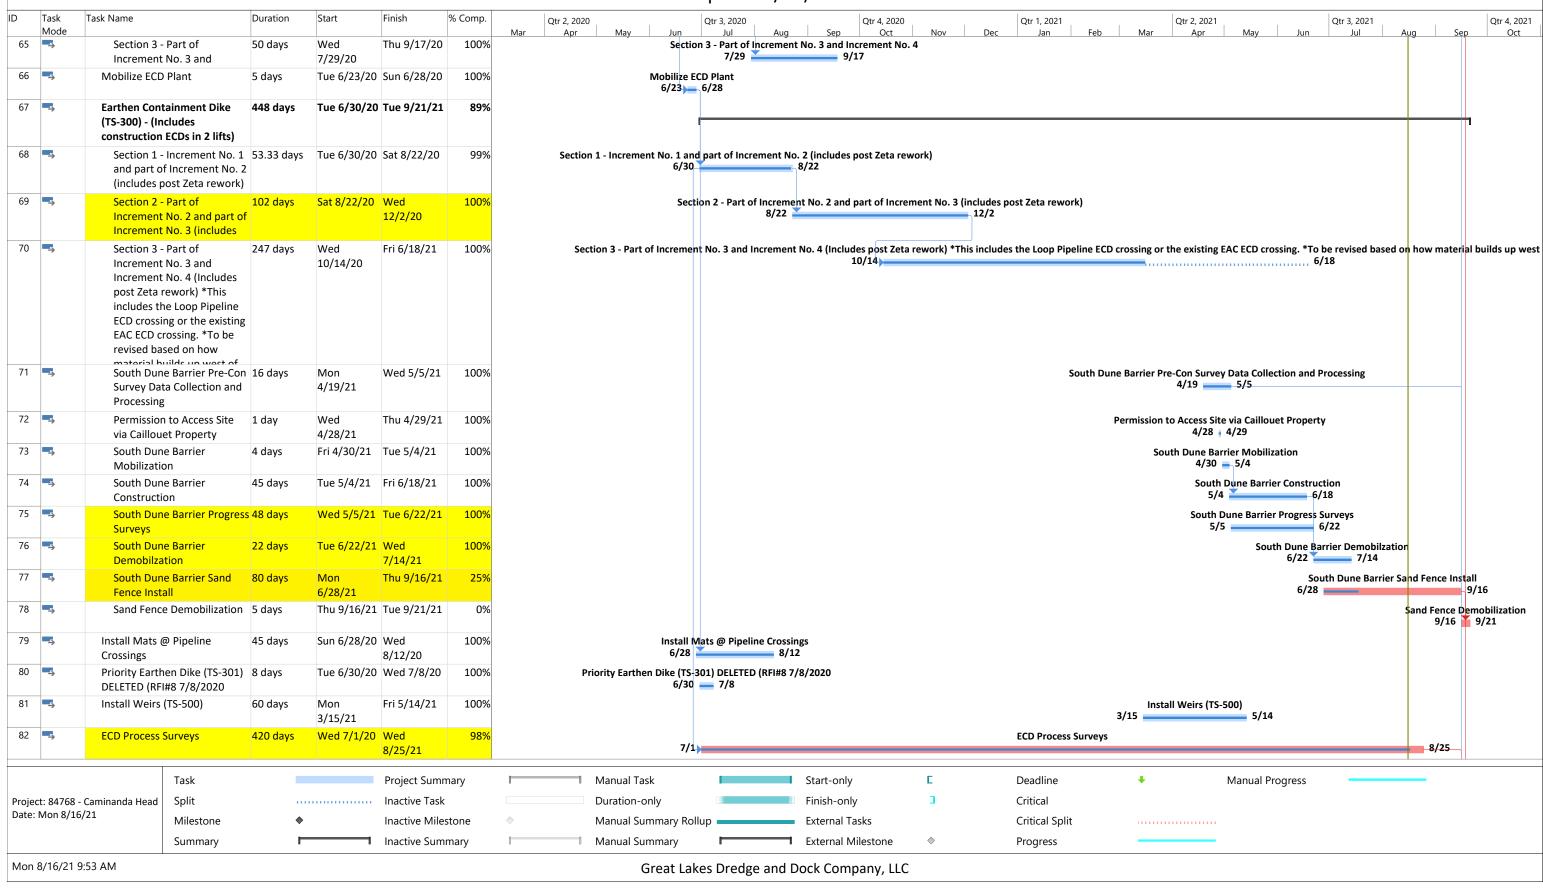


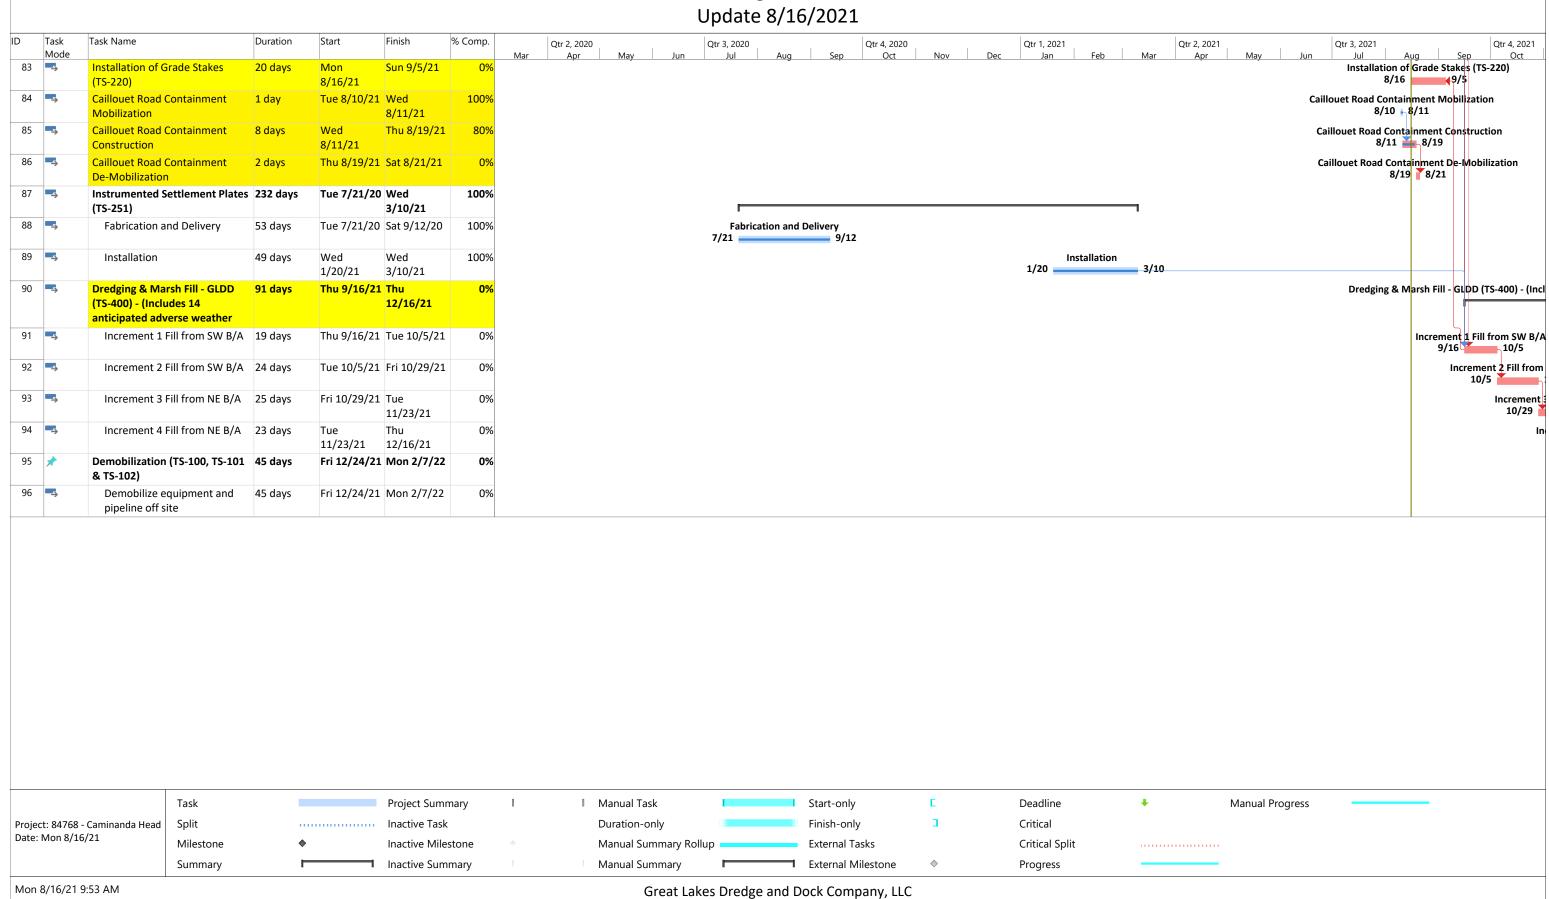








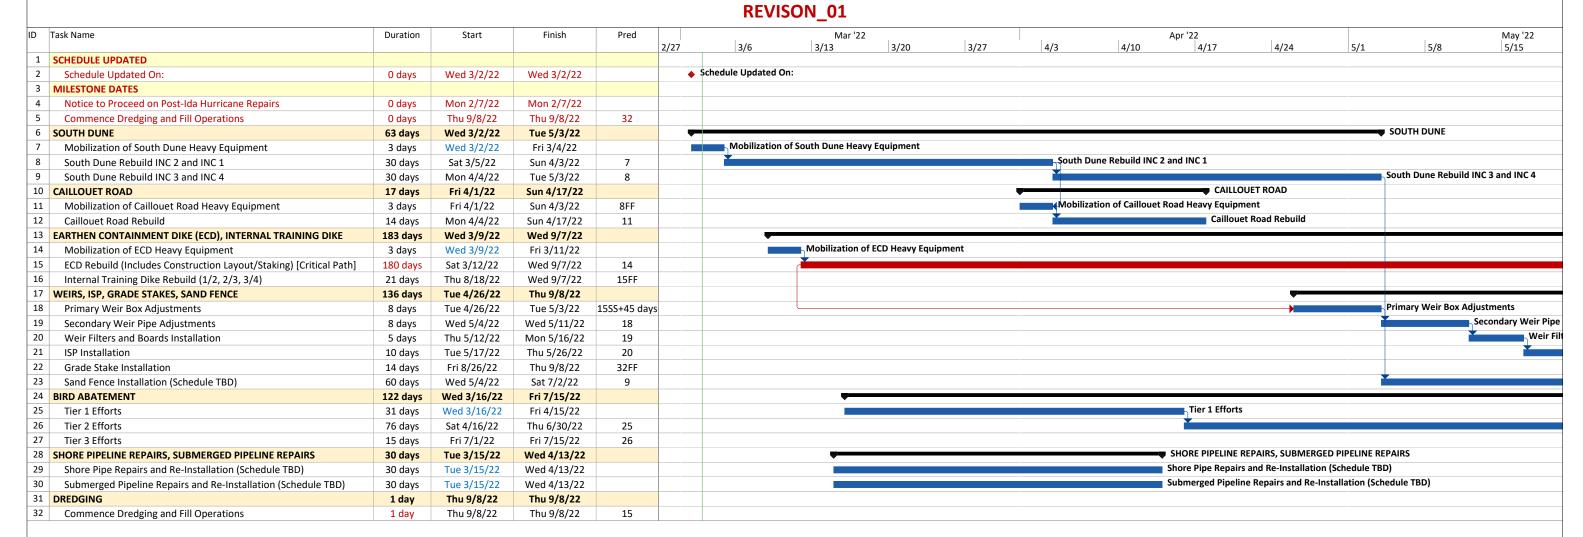








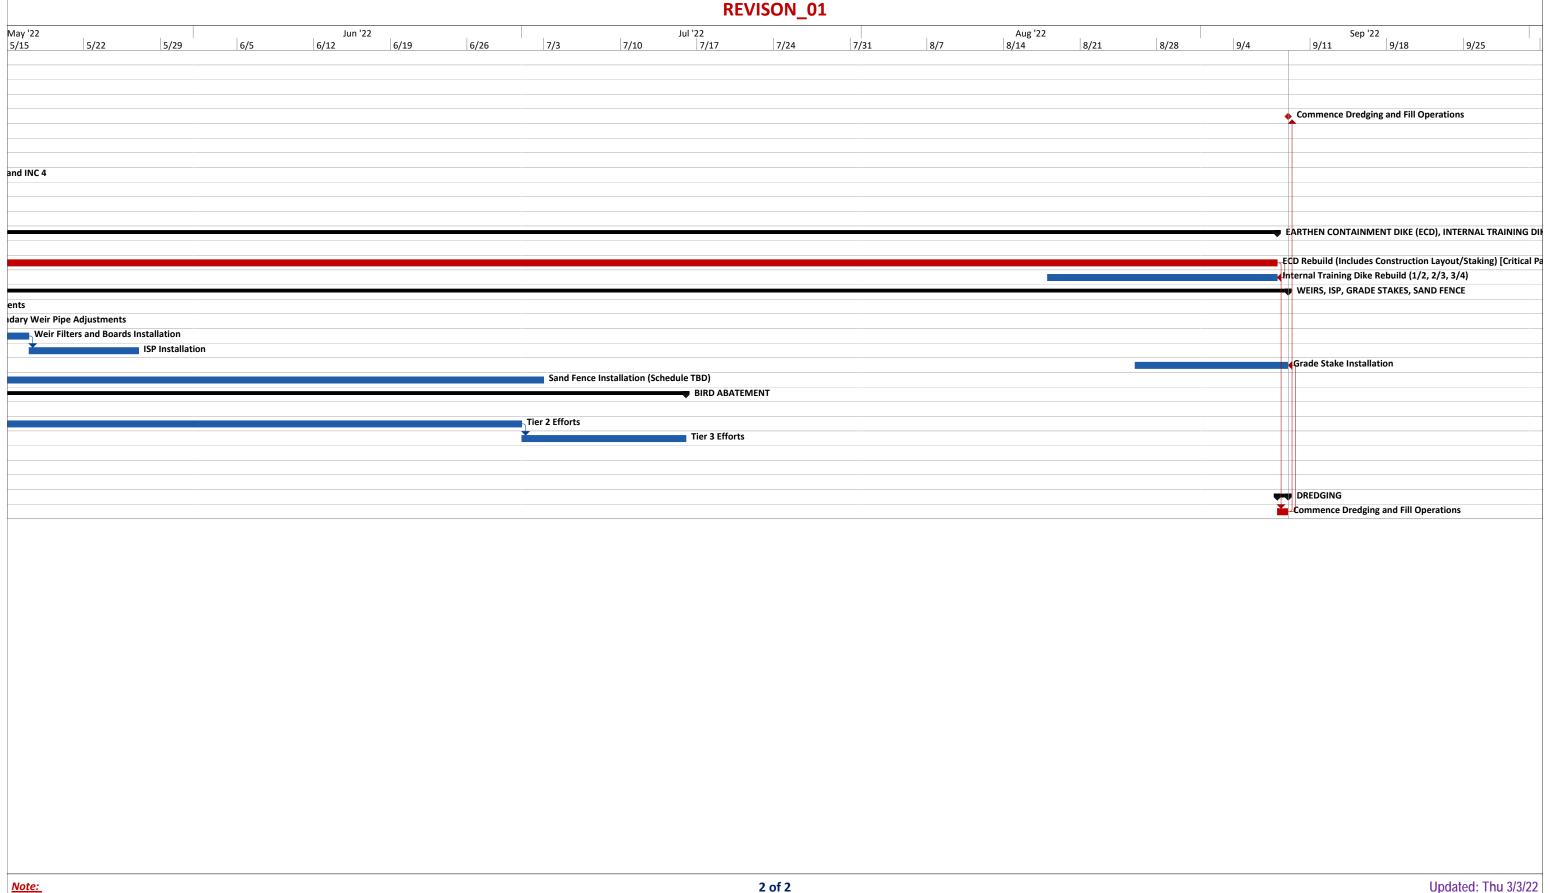








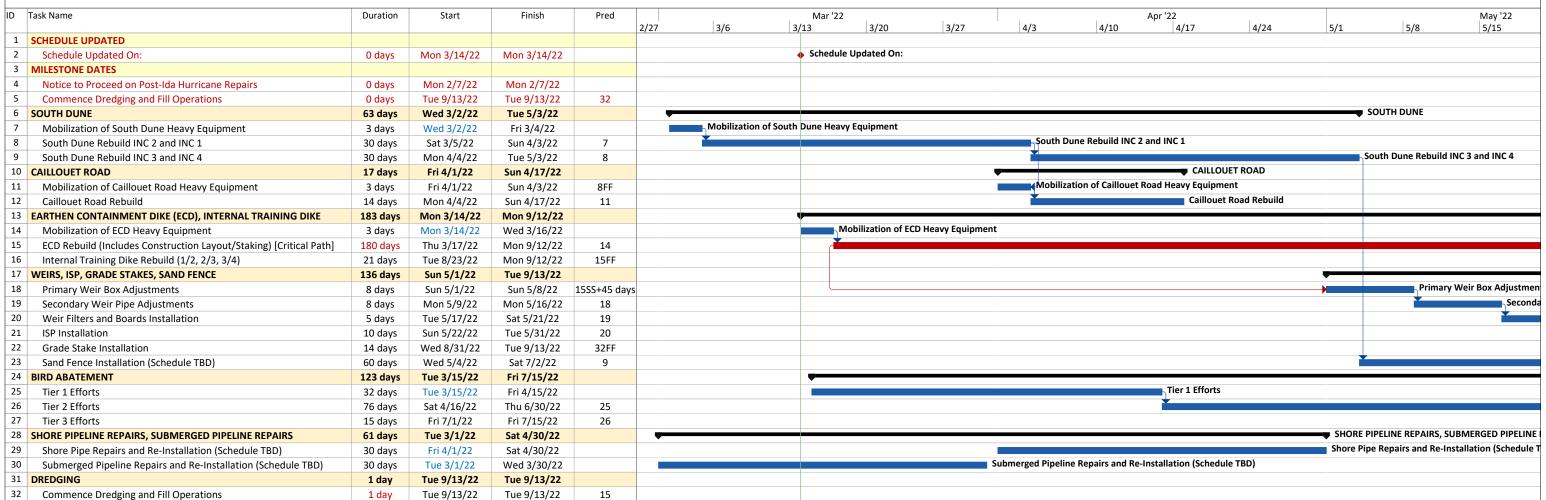








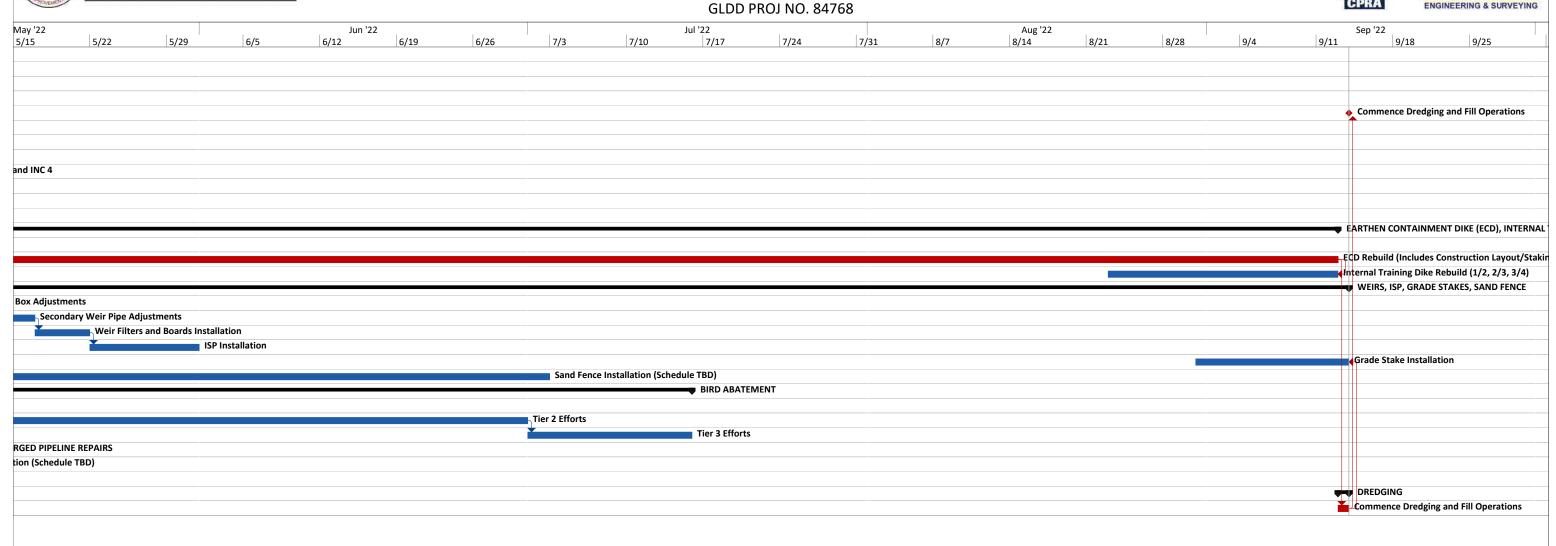








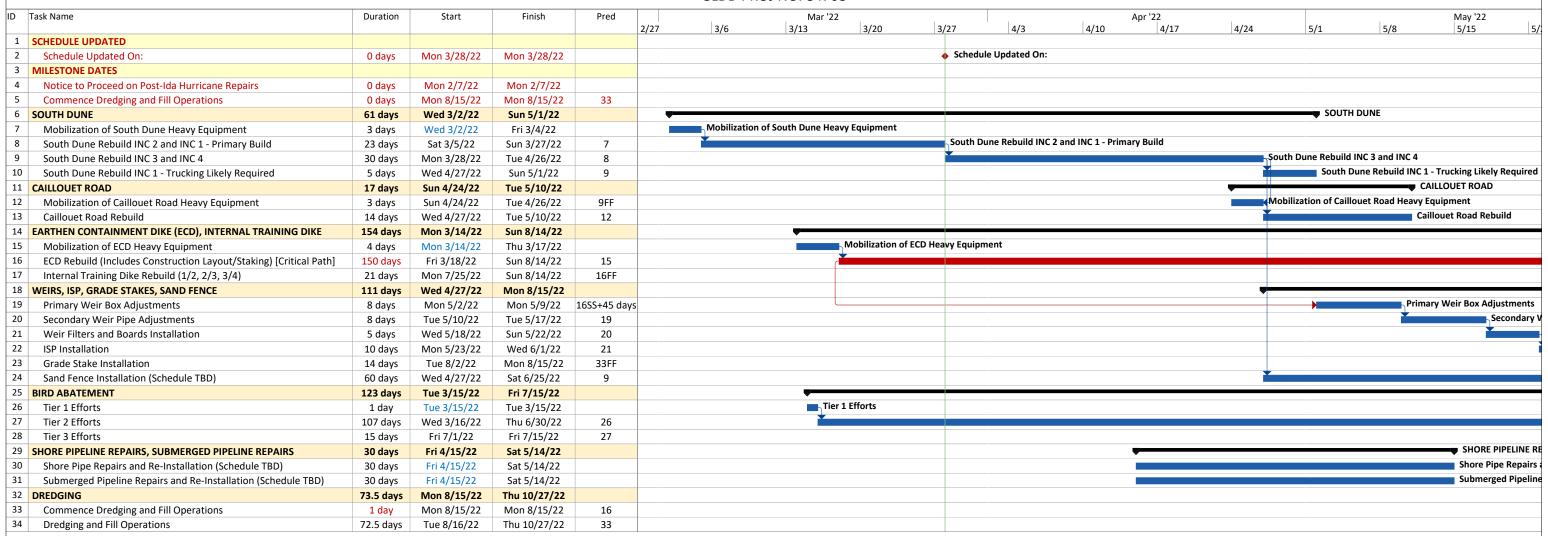







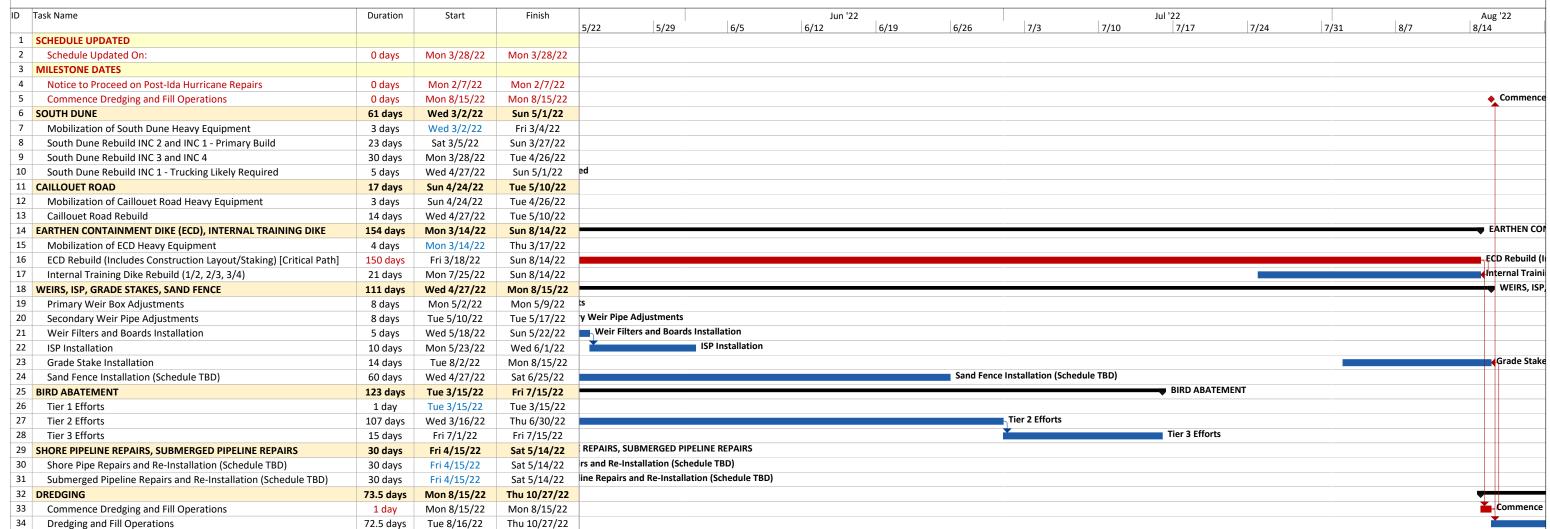



GLDD PROJ NO. 84768



Dredging and Fill Operations



ID	Task Name	Duration	Start	Finish					Sep '22				Oct '22				Nov '22
					8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13
1	SCHEDULE UPDATED																
2	Schedule Updated On:	0 days	Mon 3/28/22	Mon 3/28/22													
3	MILESTONE DATES																
4	Notice to Proceed on Post-Ida Hurricane Repairs	0 days	Mon 2/7/22	Mon 2/7/22													
5	Commence Dredging and Fill Operations	0 days	Mon 8/15/22	Mon 8/15/22	Dredging a	and Fill Operations	i										
6	SOUTH DUNE	61 days	Wed 3/2/22	Sun 5/1/22													
7	Mobilization of South Dune Heavy Equipment	3 days	Wed 3/2/22	Fri 3/4/22													
8	South Dune Rebuild INC 2 and INC 1 - Primary Build	23 days	Sat 3/5/22	Sun 3/27/22													
9	South Dune Rebuild INC 3 and INC 4	30 days	Mon 3/28/22	Tue 4/26/22													
10	South Dune Rebuild INC 1 - Trucking Likely Required	5 days	Wed 4/27/22	Sun 5/1/22													
11	CAILLOUET ROAD	17 days	Sun 4/24/22	Tue 5/10/22													
12	Mobilization of Caillouet Road Heavy Equipment	3 days	Sun 4/24/22	Tue 4/26/22													
13	Caillouet Road Rebuild	14 days	Wed 4/27/22	Tue 5/10/22													
14	EARTHEN CONTAINMENT DIKE (ECD), INTERNAL TRAINING DIKE	154 days	Mon 3/14/22	Sun 8/14/22	NTAINMENT	T DIKE (ECD), INTE	RNAL TRAINING DIK	Œ									
15	Mobilization of ECD Heavy Equipment	4 days	Mon 3/14/22	Thu 3/17/22													
16	ECD Rebuild (Includes Construction Layout/Staking) [Critical Path]	150 days	Fri 3/18/22	Sun 8/14/22	ncludes Cor	struction Layout/	Staking) [Critical Par	th]									
17	Internal Training Dike Rebuild (1/2, 2/3, 3/4)	21 days	Mon 7/25/22	Sun 8/14/22	ng Dike Rek	ouild (1/2, 2/3, 3/4	1)										
18	WEIRS, ISP, GRADE STAKES, SAND FENCE	111 days	Wed 4/27/22	Mon 8/15/22	, GRADE ST	AKES, SAND FENCE											
19	Primary Weir Box Adjustments	8 days	Mon 5/2/22	Mon 5/9/22													
20	Secondary Weir Pipe Adjustments	8 days	Tue 5/10/22	Tue 5/17/22													
21	Weir Filters and Boards Installation	5 days	Wed 5/18/22	Sun 5/22/22													
22	ISP Installation	10 days	Mon 5/23/22	Wed 6/1/22													
23	Grade Stake Installation	14 days	Tue 8/2/22	Mon 8/15/22	Installatio	n											
24	Sand Fence Installation (Schedule TBD)	60 days	Wed 4/27/22	Sat 6/25/22													
25	BIRD ABATEMENT	123 days	Tue 3/15/22	Fri 7/15/22													
26	Tier 1 Efforts	1 day	Tue 3/15/22	Tue 3/15/22													
27	Tier 2 Efforts	107 days	Wed 3/16/22	Thu 6/30/22													
28	Tier 3 Efforts	15 days	Fri 7/1/22	Fri 7/15/22													
29	SHORE PIPELINE REPAIRS, SUBMERGED PIPELINE REPAIRS	30 days	Fri 4/15/22	Sat 5/14/22													
30	Shore Pipe Repairs and Re-Installation (Schedule TBD)	30 days	Fri 4/15/22	Sat 5/14/22													
31	Submerged Pipeline Repairs and Re-Installation (Schedule TBD)	30 days	Fri 4/15/22	Sat 5/14/22													
32	DREDGING	73.5 days	Mon 8/15/22	Thu 10/27/22											DREDGING		
33	Commence Dredging and Fill Operations	1 day	Mon 8/15/22		Dredging a	nd Fill Operations											
															D deline en d 510 4		

Tue 8/16/22 Thu 10/27/22

72.5 days


34 Dredging and Fill Operations



GLDD PROJ NO. 84768





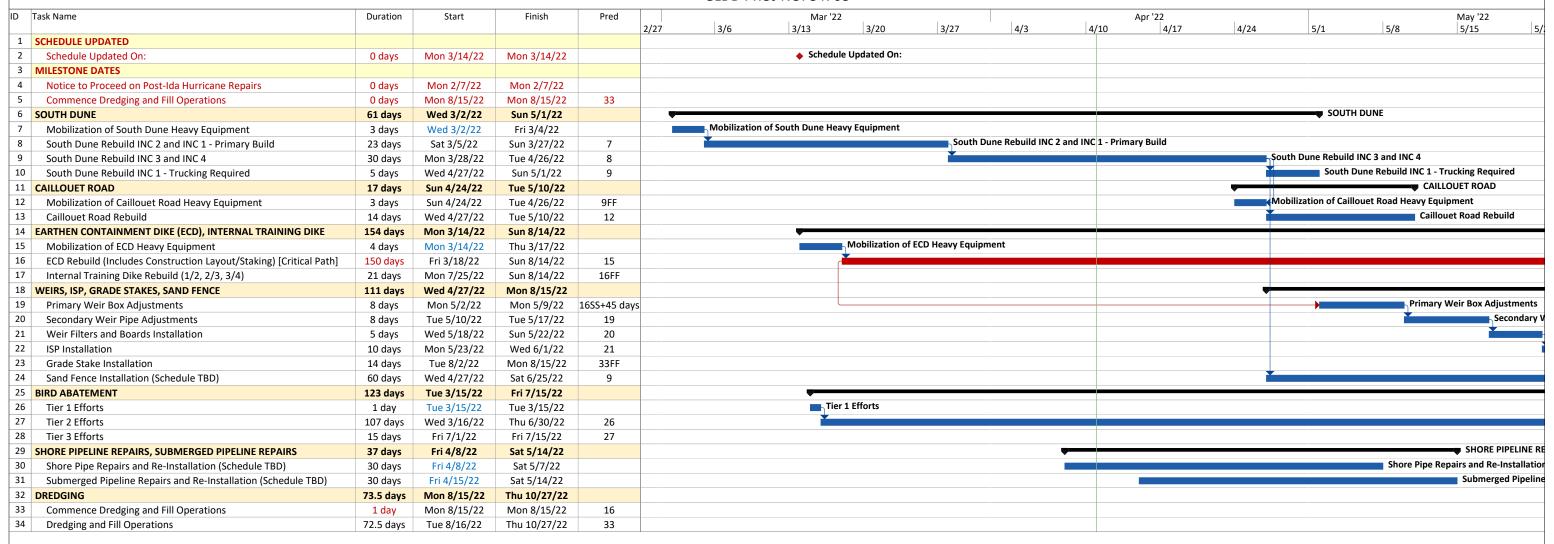


1 of 3







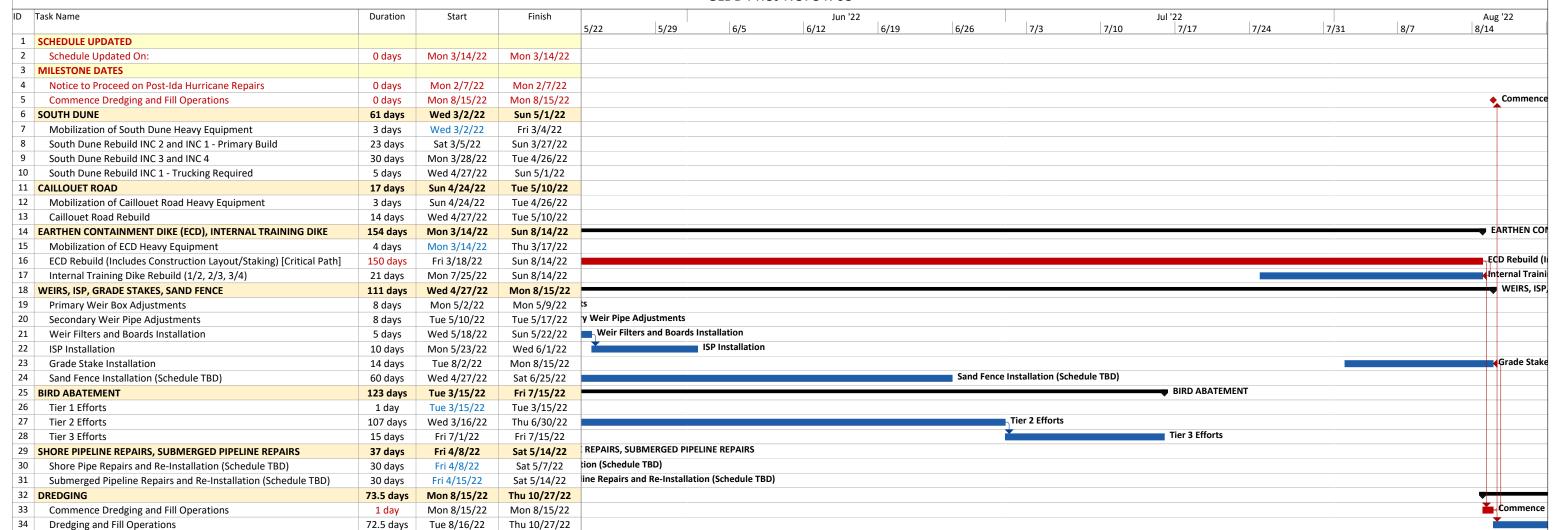



GLDD PROJ NO. 84768



Dredging and Fill Operations



ID	Task Name	Duration	Start	Finish				S	ep '22				Oct '22				Nov '22
					8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13
1	SCHEDULE UPDATED																
2	Schedule Updated On:	0 days	Mon 3/14/22	Mon 3/14/22													
3	MILESTONE DATES																
4	Notice to Proceed on Post-Ida Hurricane Repairs	0 days	Mon 2/7/22	Mon 2/7/22													
5	Commence Dredging and Fill Operations	0 days	Mon 8/15/22	Mon 8/15/22	Dredging and I	ill Operatio	ons										
6	SOUTH DUNE	61 days	Wed 3/2/22	Sun 5/1/22													
7	Mobilization of South Dune Heavy Equipment	3 days	Wed 3/2/22	Fri 3/4/22													
8	South Dune Rebuild INC 2 and INC 1 - Primary Build	23 days	Sat 3/5/22	Sun 3/27/22													
9	South Dune Rebuild INC 3 and INC 4	30 days	Mon 3/28/22	Tue 4/26/22													
10	South Dune Rebuild INC 1 - Trucking Required	5 days	Wed 4/27/22	Sun 5/1/22													
11	CAILLOUET ROAD	17 days	Sun 4/24/22	Tue 5/10/22													
12	Mobilization of Caillouet Road Heavy Equipment	3 days	Sun 4/24/22	Tue 4/26/22													
13	Caillouet Road Rebuild	14 days	Wed 4/27/22	Tue 5/10/22													
14	EARTHEN CONTAINMENT DIKE (ECD), INTERNAL TRAINING DIKE	154 days	Mon 3/14/22	Sun 8/14/22	NTAINMENT DI	E (ECD), IN	TERNAL TRAINING	DIKE									
15	Mobilization of ECD Heavy Equipment	4 days	Mon 3/14/22	Thu 3/17/22													
16	ECD Rebuild (Includes Construction Layout/Staking) [Critical Path]	150 days	Fri 3/18/22	Sun 8/14/22	ncludes Constru	ction Layou	ıt/Staking) [Critical	Path]									
17	Internal Training Dike Rebuild (1/2, 2/3, 3/4)	21 days	Mon 7/25/22	Sun 8/14/22	ng Dike Rebuild	(1/2, 2/3, 3	3/4)										
18	WEIRS, ISP, GRADE STAKES, SAND FENCE	111 days	Wed 4/27/22	Mon 8/15/22	, GRADE STAKES	, SAND FEN	ICE										
19	Primary Weir Box Adjustments	8 days	Mon 5/2/22	Mon 5/9/22													
20	Secondary Weir Pipe Adjustments	8 days	Tue 5/10/22	Tue 5/17/22													
21	Weir Filters and Boards Installation	5 days	Wed 5/18/22	Sun 5/22/22													
22	ISP Installation	10 days	Mon 5/23/22	Wed 6/1/22													
23	Grade Stake Installation	14 days	Tue 8/2/22	Mon 8/15/22	Installation												
24	Sand Fence Installation (Schedule TBD)	60 days	Wed 4/27/22	Sat 6/25/22													
25	BIRD ABATEMENT	123 days	Tue 3/15/22	Fri 7/15/22													
26	Tier 1 Efforts	1 day	Tue 3/15/22	Tue 3/15/22													
27	Tier 2 Efforts	107 days	Wed 3/16/22	Thu 6/30/22													
28	Tier 3 Efforts	15 days	Fri 7/1/22	Fri 7/15/22													
29	SHORE PIPELINE REPAIRS, SUBMERGED PIPELINE REPAIRS	37 days	Fri 4/8/22	Sat 5/14/22													
30	Shore Pipe Repairs and Re-Installation (Schedule TBD)	30 days	Fri 4/8/22	Sat 5/7/22													
31	Submerged Pipeline Repairs and Re-Installation (Schedule TBD)	30 days	Fri 4/15/22	Sat 5/14/22													
32	DREDGING	73.5 days	Mon 8/15/22	Thu 10/27/22											DREDGING		
33	Commence Dredging and Fill Operations	1 day	Mon 8/15/22	Mon 8/15/22	Dredging and F	II Operation	ıs										

34 Dredging and Fill Operations


72.5 days Tue 8/16/22 Thu 10/27/22



GLDD PROJ NO. 84768





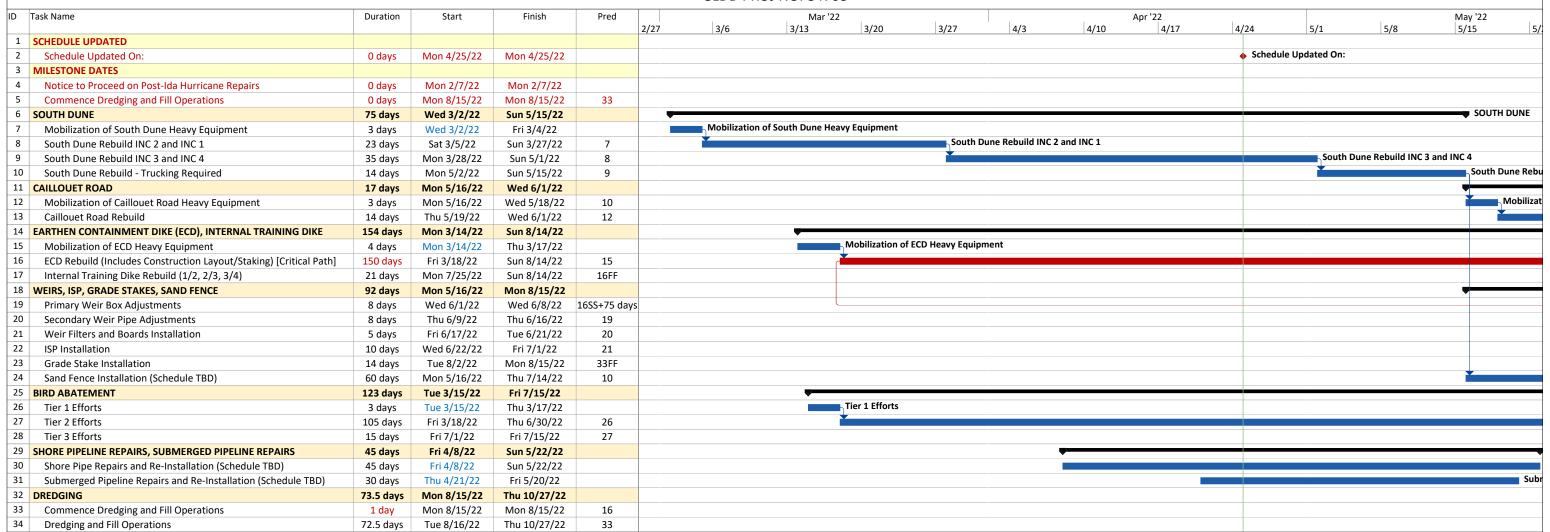


1 of 3







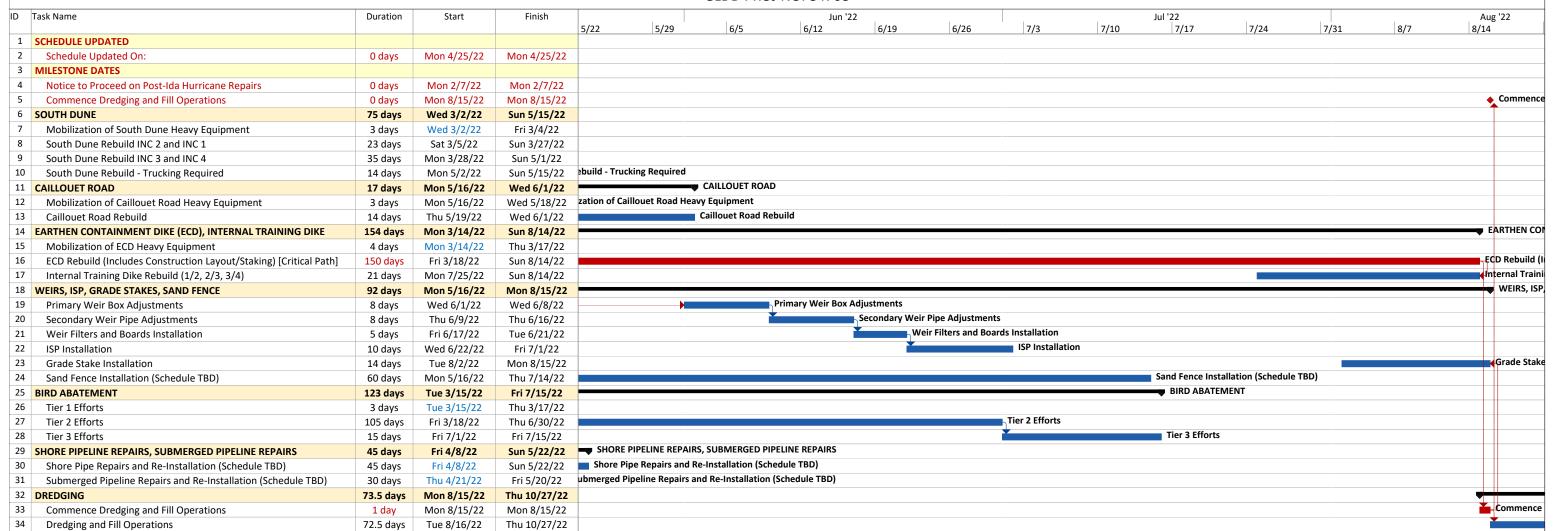



GLDD PROJ NO. 84768



Dredging and Fill Operations



ID	Task Name	Duration	Start	Finish				S	ep '22				Oct '22				Nov '22
					8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13
1	SCHEDULE UPDATED																
2	Schedule Updated On:	0 days	Mon 4/25/22	Mon 4/25/22													
3	MILESTONE DATES																
4	Notice to Proceed on Post-Ida Hurricane Repairs	0 days	Mon 2/7/22	Mon 2/7/22													
5	Commence Dredging and Fill Operations	0 days	Mon 8/15/22	Mon 8/15/22	Dredging and F	ill Operatio	ons										
6	SOUTH DUNE	75 days	Wed 3/2/22	Sun 5/15/22													
7	Mobilization of South Dune Heavy Equipment	3 days	Wed 3/2/22	Fri 3/4/22													
8	South Dune Rebuild INC 2 and INC 1	23 days	Sat 3/5/22	Sun 3/27/22													
9	South Dune Rebuild INC 3 and INC 4	35 days	Mon 3/28/22	Sun 5/1/22													
10	South Dune Rebuild - Trucking Required	14 days	Mon 5/2/22	Sun 5/15/22													
11	CAILLOUET ROAD	17 days	Mon 5/16/22	Wed 6/1/22													
12	Mobilization of Caillouet Road Heavy Equipment	3 days	Mon 5/16/22	Wed 5/18/22													
13	Caillouet Road Rebuild	14 days	Thu 5/19/22	Wed 6/1/22													
14	EARTHEN CONTAINMENT DIKE (ECD), INTERNAL TRAINING DIKE	154 days	Mon 3/14/22	Sun 8/14/22	NTAINMENT DIK	E (ECD), IN	TERNAL TRAINING	DIKE									
15	Mobilization of ECD Heavy Equipment	4 days	Mon 3/14/22	Thu 3/17/22													
16	ECD Rebuild (Includes Construction Layout/Staking) [Critical Path]	150 days	Fri 3/18/22	Sun 8/14/22	ncludes Constru	ction Layou	ıt/Staking) [Critical	Path]									
17	Internal Training Dike Rebuild (1/2, 2/3, 3/4)	21 days	Mon 7/25/22	Sun 8/14/22	ng Dike Rebuild	(1/2, 2/3, 3	3/4)										
18	WEIRS, ISP, GRADE STAKES, SAND FENCE	92 days	Mon 5/16/22	Mon 8/15/22	, GRADE STAKES	, SAND FEN	ICE										
19	Primary Weir Box Adjustments	8 days	Wed 6/1/22	Wed 6/8/22													
20	Secondary Weir Pipe Adjustments	8 days	Thu 6/9/22	Thu 6/16/22													
21	Weir Filters and Boards Installation	5 days	Fri 6/17/22	Tue 6/21/22													
22	ISP Installation	10 days	Wed 6/22/22	Fri 7/1/22													
23	Grade Stake Installation	14 days	Tue 8/2/22	Mon 8/15/22	Installation												
24	Sand Fence Installation (Schedule TBD)	60 days	Mon 5/16/22	Thu 7/14/22													
25	BIRD ABATEMENT	123 days	Tue 3/15/22	Fri 7/15/22													
26	Tier 1 Efforts	3 days	Tue 3/15/22	Thu 3/17/22													
27	Tier 2 Efforts	105 days	Fri 3/18/22	Thu 6/30/22													
28	Tier 3 Efforts	15 days	Fri 7/1/22	Fri 7/15/22													
29	SHORE PIPELINE REPAIRS, SUBMERGED PIPELINE REPAIRS	45 days	Fri 4/8/22	Sun 5/22/22													
30	Shore Pipe Repairs and Re-Installation (Schedule TBD)	45 days	Fri 4/8/22	Sun 5/22/22													
31	Submerged Pipeline Repairs and Re-Installation (Schedule TBD)	30 days	Thu 4/21/22	Fri 5/20/22													
32	DREDGING	73.5 days	Mon 8/15/22	Thu 10/27/22											DREDGING		
33	Commence Dredging and Fill Operations	1 day	Mon 8/15/22	Mon 8/15/22	Dredging and Fi	ll Operation	ıs										


34 Dredging and Fill Operations

72.5 days Tue 8/16/22 Thu 10/27/22








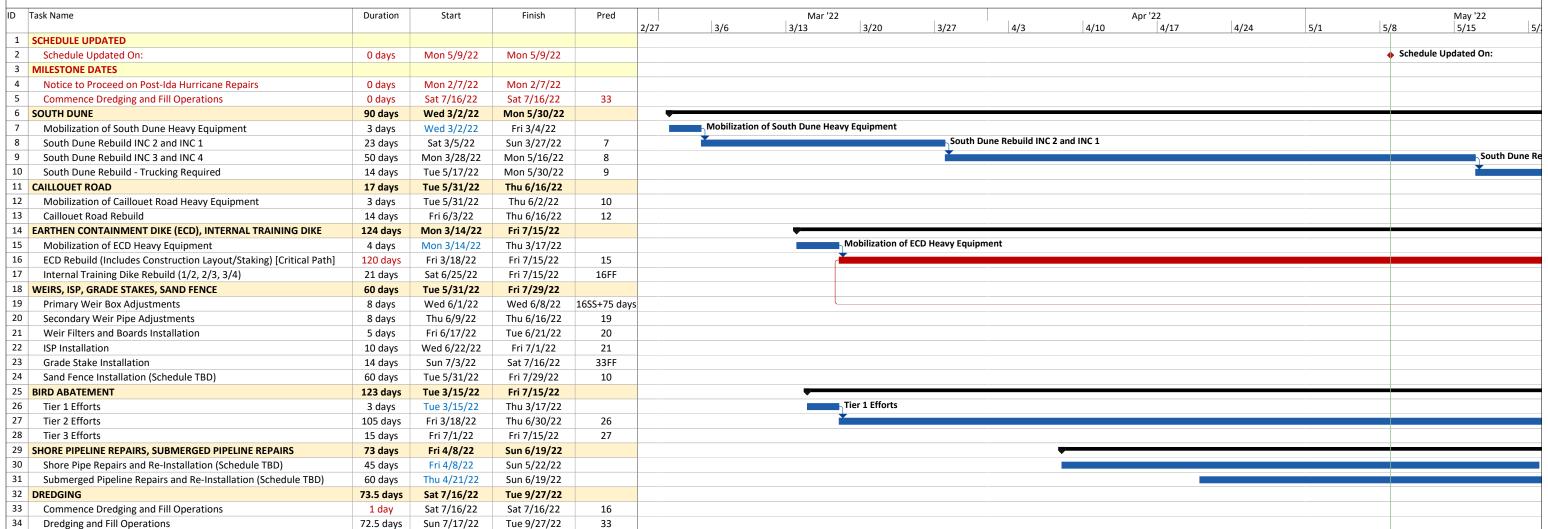







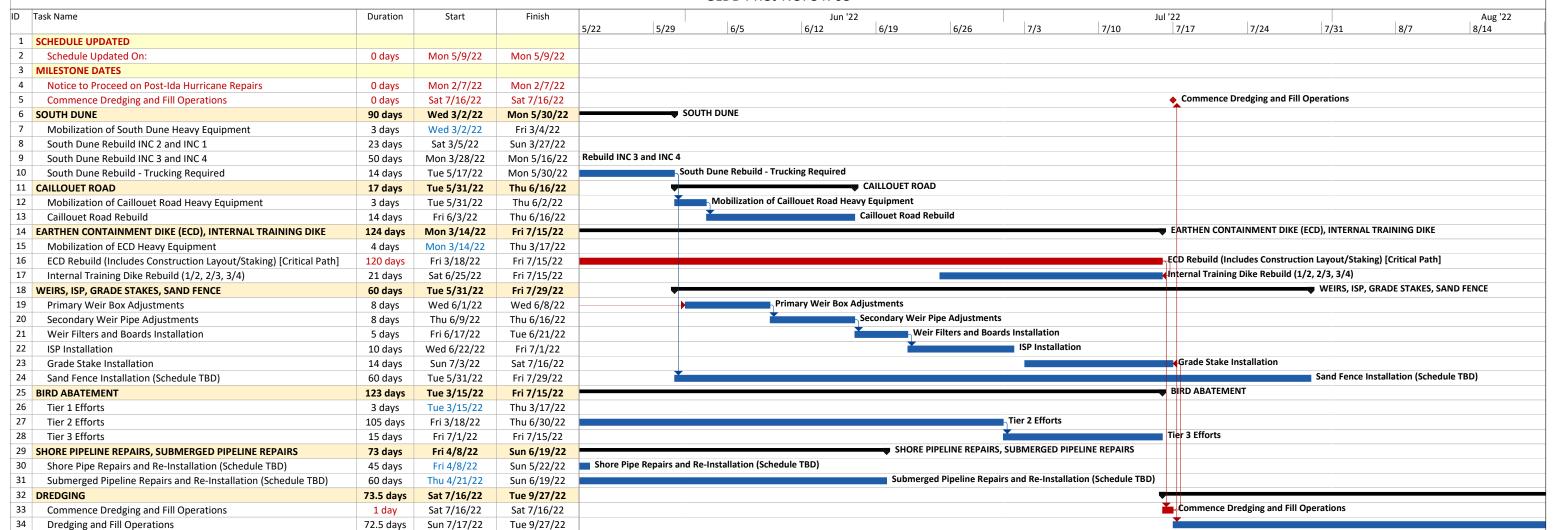



GLDD PROJ NO. 84768






ID	Task Name	Duration	Start	Finish				Se	ep '22				Oct '22				Nov '22
					8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13
1	SCHEDULE UPDATED																
2	Schedule Updated On:	0 days	Mon 5/9/22	Mon 5/9/22													
3	MILESTONE DATES																
4	Notice to Proceed on Post-Ida Hurricane Repairs	0 days	Mon 2/7/22	Mon 2/7/22													
5	Commence Dredging and Fill Operations	0 days	Sat 7/16/22	Sat 7/16/22													
6	SOUTH DUNE	90 days	Wed 3/2/22	Mon 5/30/22													
7	Mobilization of South Dune Heavy Equipment	3 days	Wed 3/2/22	Fri 3/4/22													
8	South Dune Rebuild INC 2 and INC 1	23 days	Sat 3/5/22	Sun 3/27/22													
9	South Dune Rebuild INC 3 and INC 4	50 days	Mon 3/28/22	Mon 5/16/22													
10	South Dune Rebuild - Trucking Required	14 days	Tue 5/17/22	Mon 5/30/22													
11	CAILLOUET ROAD	17 days	Tue 5/31/22	Thu 6/16/22													
12	Mobilization of Caillouet Road Heavy Equipment	3 days	Tue 5/31/22	Thu 6/2/22													
13	Caillouet Road Rebuild	14 days	Fri 6/3/22	Thu 6/16/22													
14	EARTHEN CONTAINMENT DIKE (ECD), INTERNAL TRAINING DIKE	124 days	Mon 3/14/22	Fri 7/15/22													
15	Mobilization of ECD Heavy Equipment	4 days	Mon 3/14/22	Thu 3/17/22													
16	ECD Rebuild (Includes Construction Layout/Staking) [Critical Path]	120 days	Fri 3/18/22	Fri 7/15/22													
17	Internal Training Dike Rebuild (1/2, 2/3, 3/4)	21 days	Sat 6/25/22	Fri 7/15/22													
18	WEIRS, ISP, GRADE STAKES, SAND FENCE	60 days	Tue 5/31/22	Fri 7/29/22													
19	Primary Weir Box Adjustments	8 days	Wed 6/1/22	Wed 6/8/22													
20	Secondary Weir Pipe Adjustments	8 days	Thu 6/9/22	Thu 6/16/22													
21	Weir Filters and Boards Installation	5 days	Fri 6/17/22	Tue 6/21/22													
22	ISP Installation	10 days	Wed 6/22/22	Fri 7/1/22													
23	Grade Stake Installation	14 days	Sun 7/3/22	Sat 7/16/22													
24	Sand Fence Installation (Schedule TBD)	60 days	Tue 5/31/22	Fri 7/29/22													
25	BIRD ABATEMENT	123 days	Tue 3/15/22	Fri 7/15/22													
26	Tier 1 Efforts	3 days	Tue 3/15/22	Thu 3/17/22													
27	Tier 2 Efforts	105 days	Fri 3/18/22	Thu 6/30/22													
28	Tier 3 Efforts	15 days	Fri 7/1/22	Fri 7/15/22													
29	SHORE PIPELINE REPAIRS, SUBMERGED PIPELINE REPAIRS	73 days	Fri 4/8/22	Sun 6/19/22													
30	Shore Pipe Repairs and Re-Installation (Schedule TBD)	45 days	Fri 4/8/22	Sun 5/22/22													
31	,	60 days	Thu 4/21/22	Sun 6/19/22													
32	DREDGING	73.5 days	Sat 7/16/22	Tue 9/27/22						DREI	DGING						
33	Commence Dredging and Fill Operations	1 day	Sat 7/16/22	Sat 7/16/22													
34	Dredging and Fill Operations	72.5 days	Sun 7/17/22	Tue 9/27/22						Dred	ging and Fill Oper	rations					

3 of 3








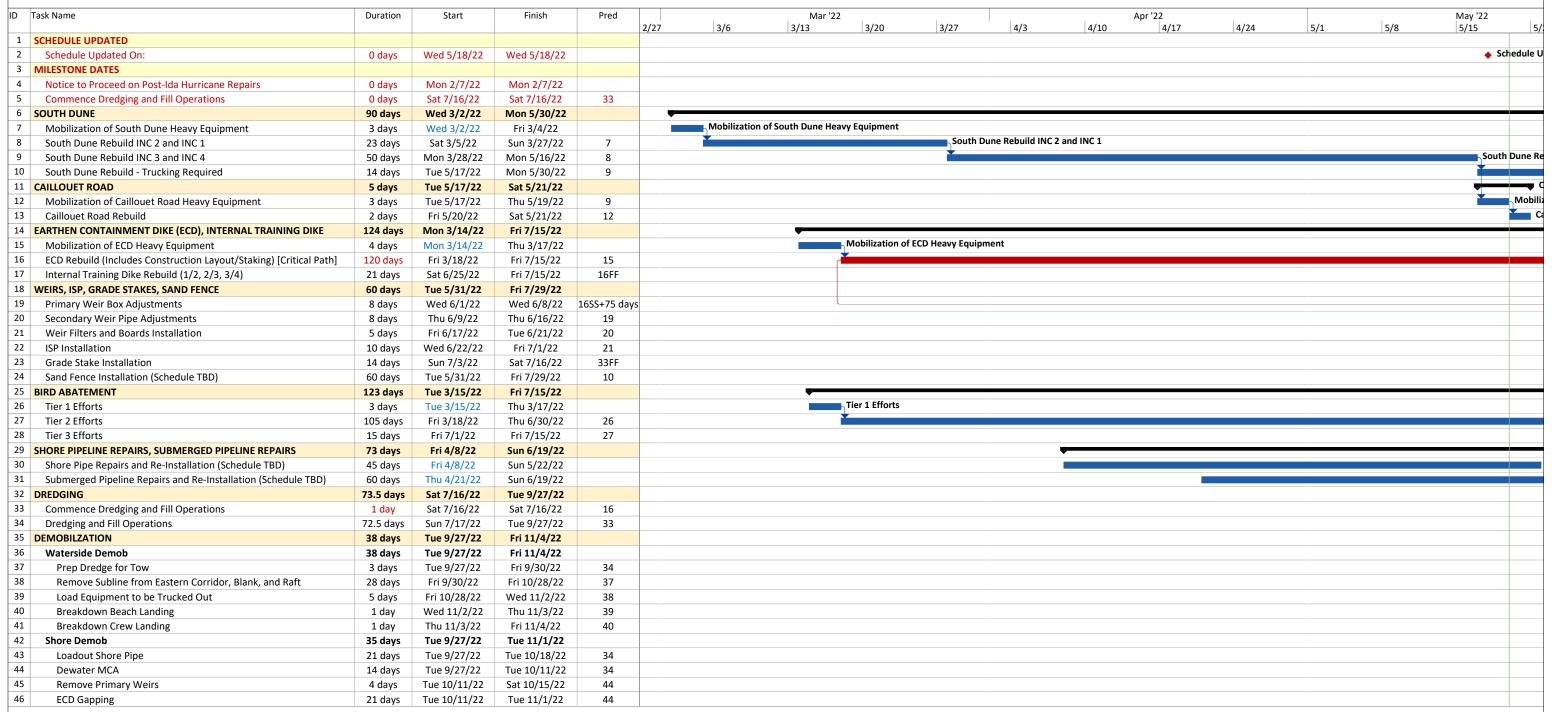







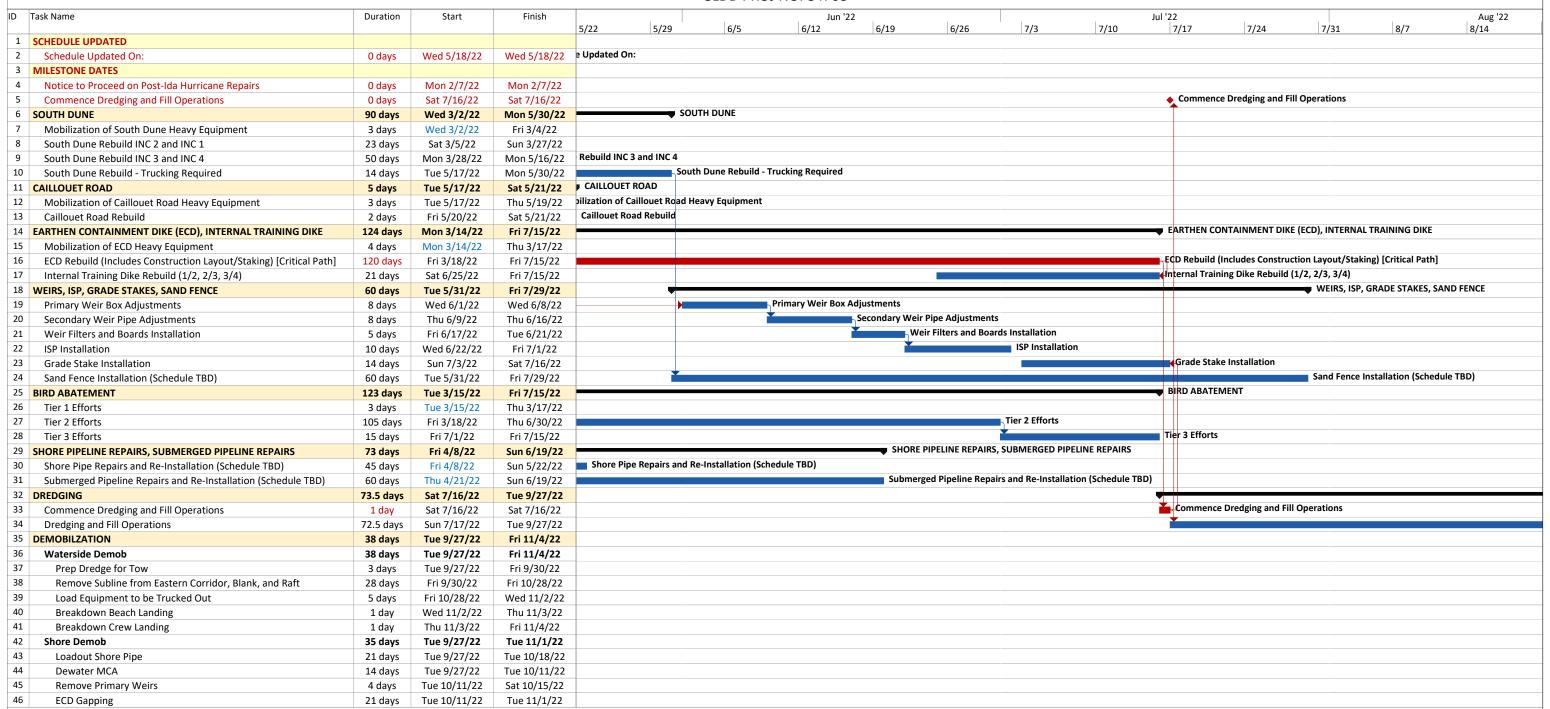




GLDD PROJ NO. 84768





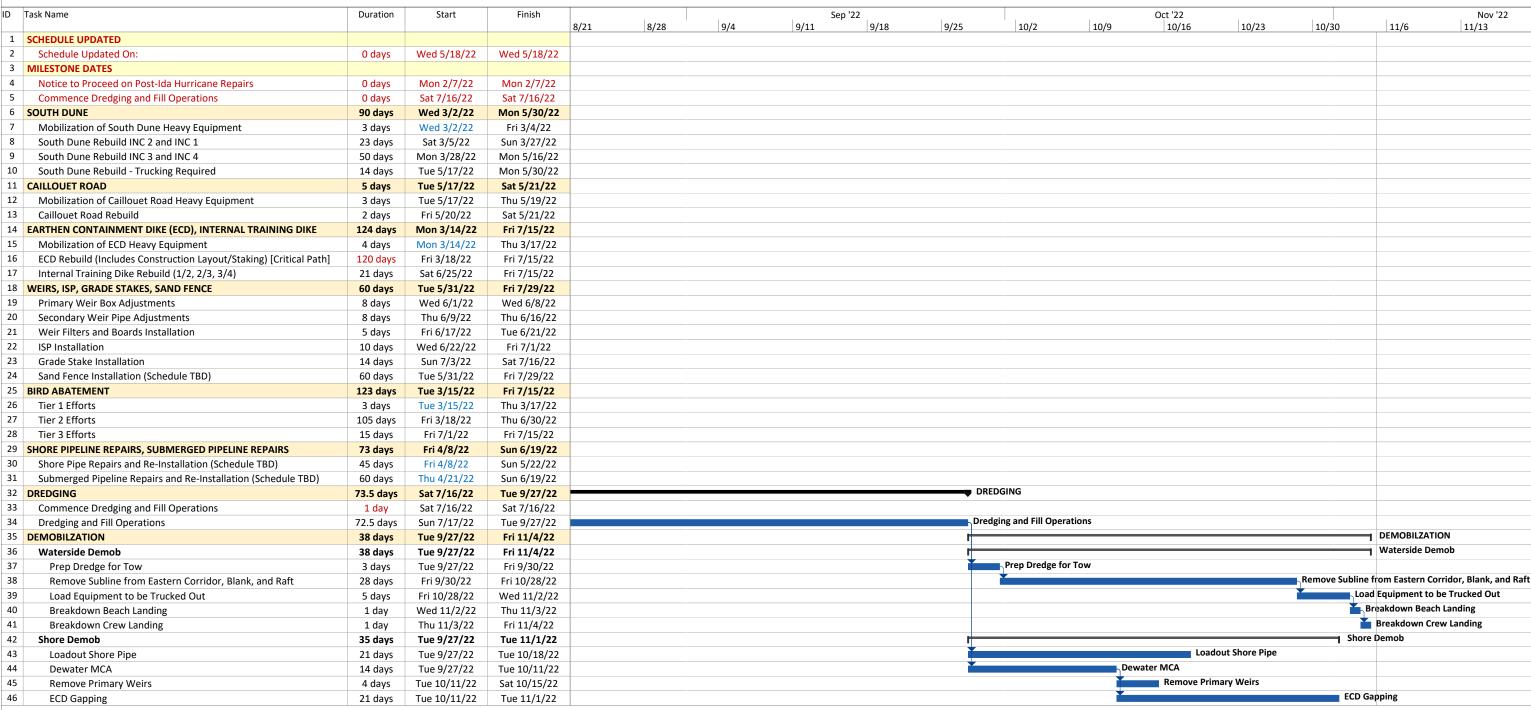


3 of 3








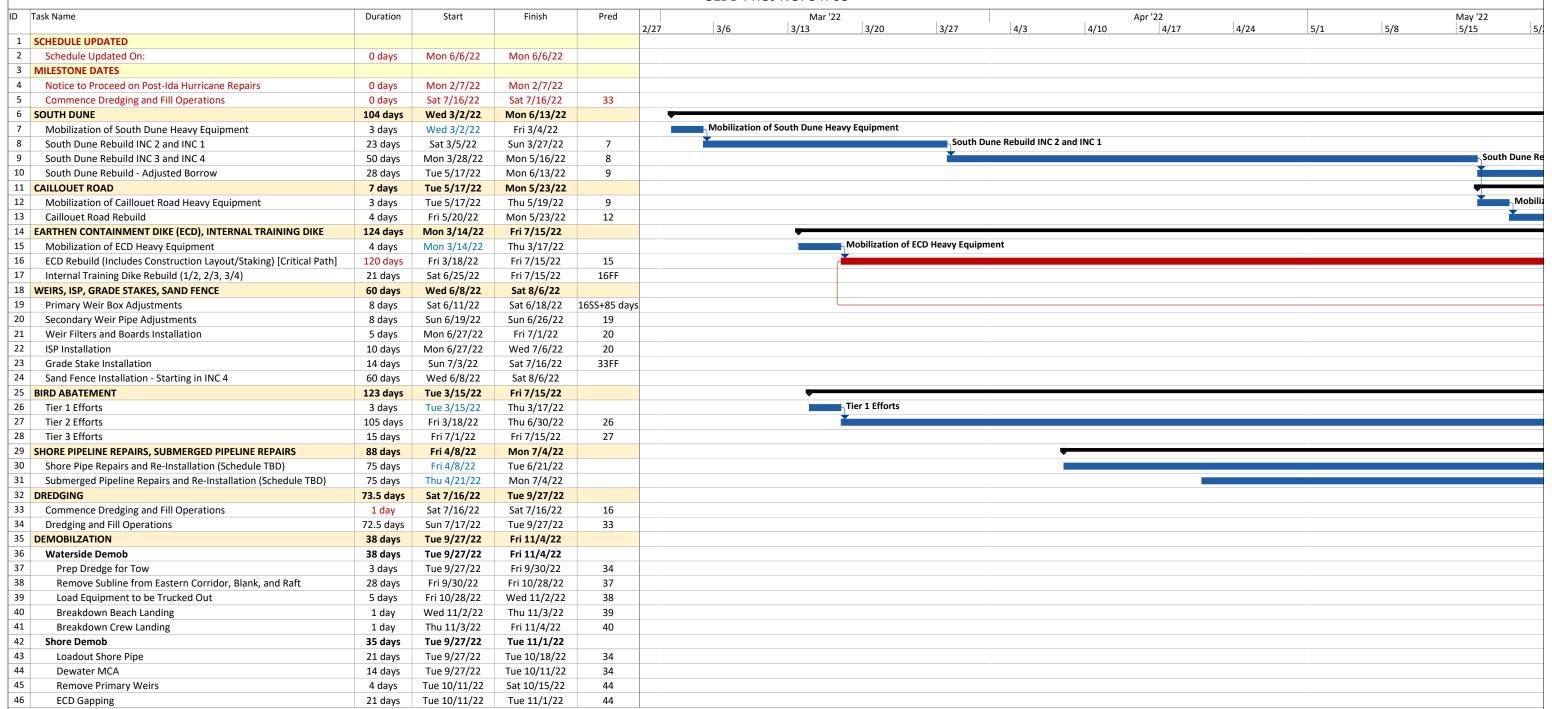








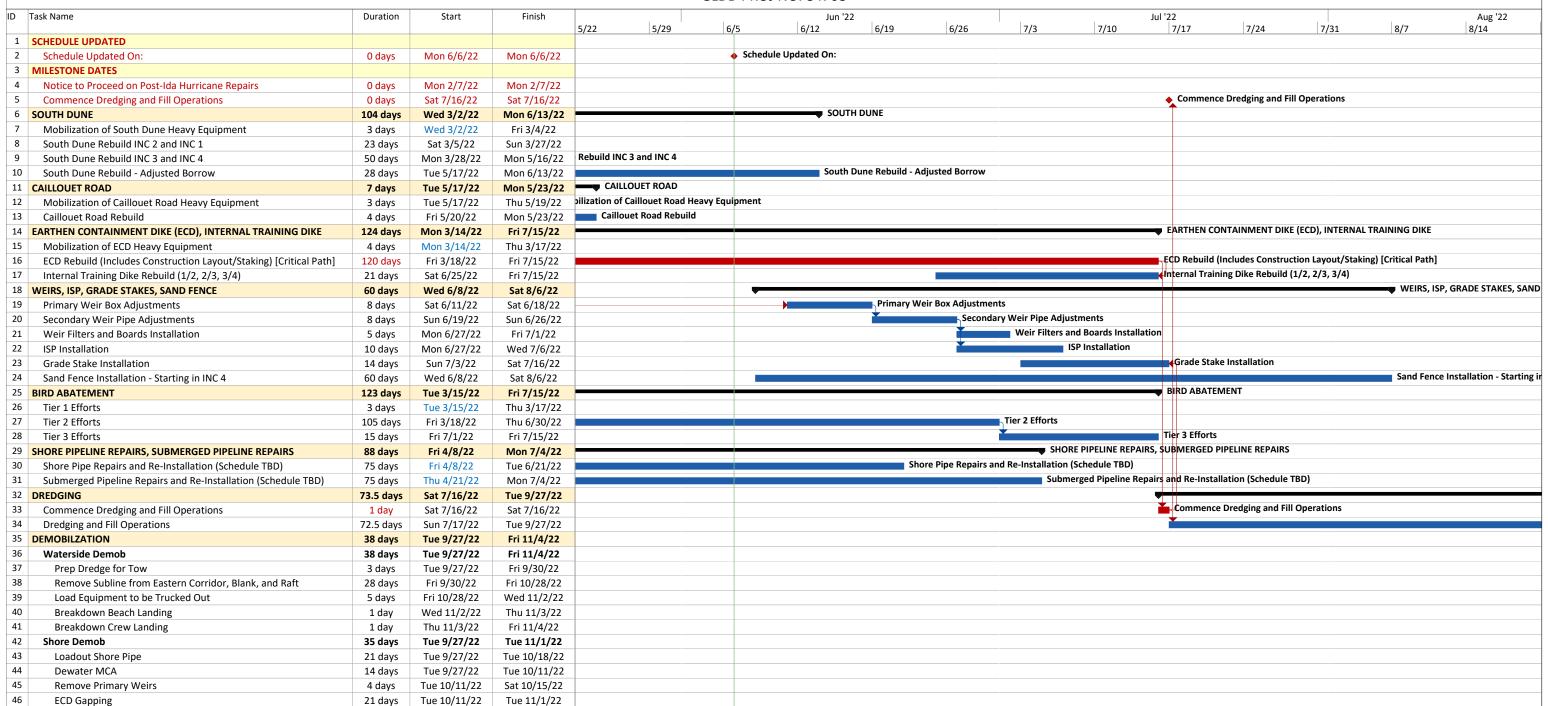







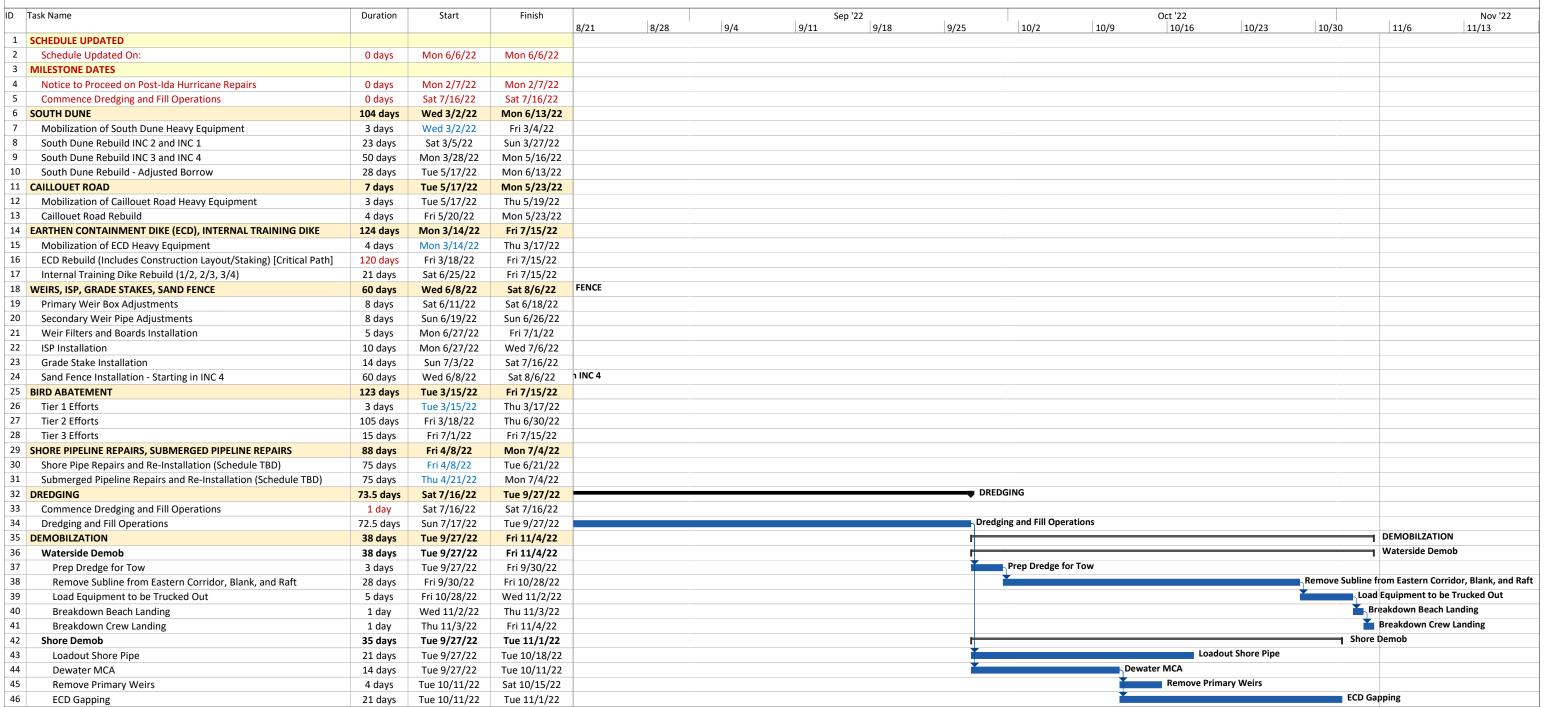




GLDD PROJ NO. 84768





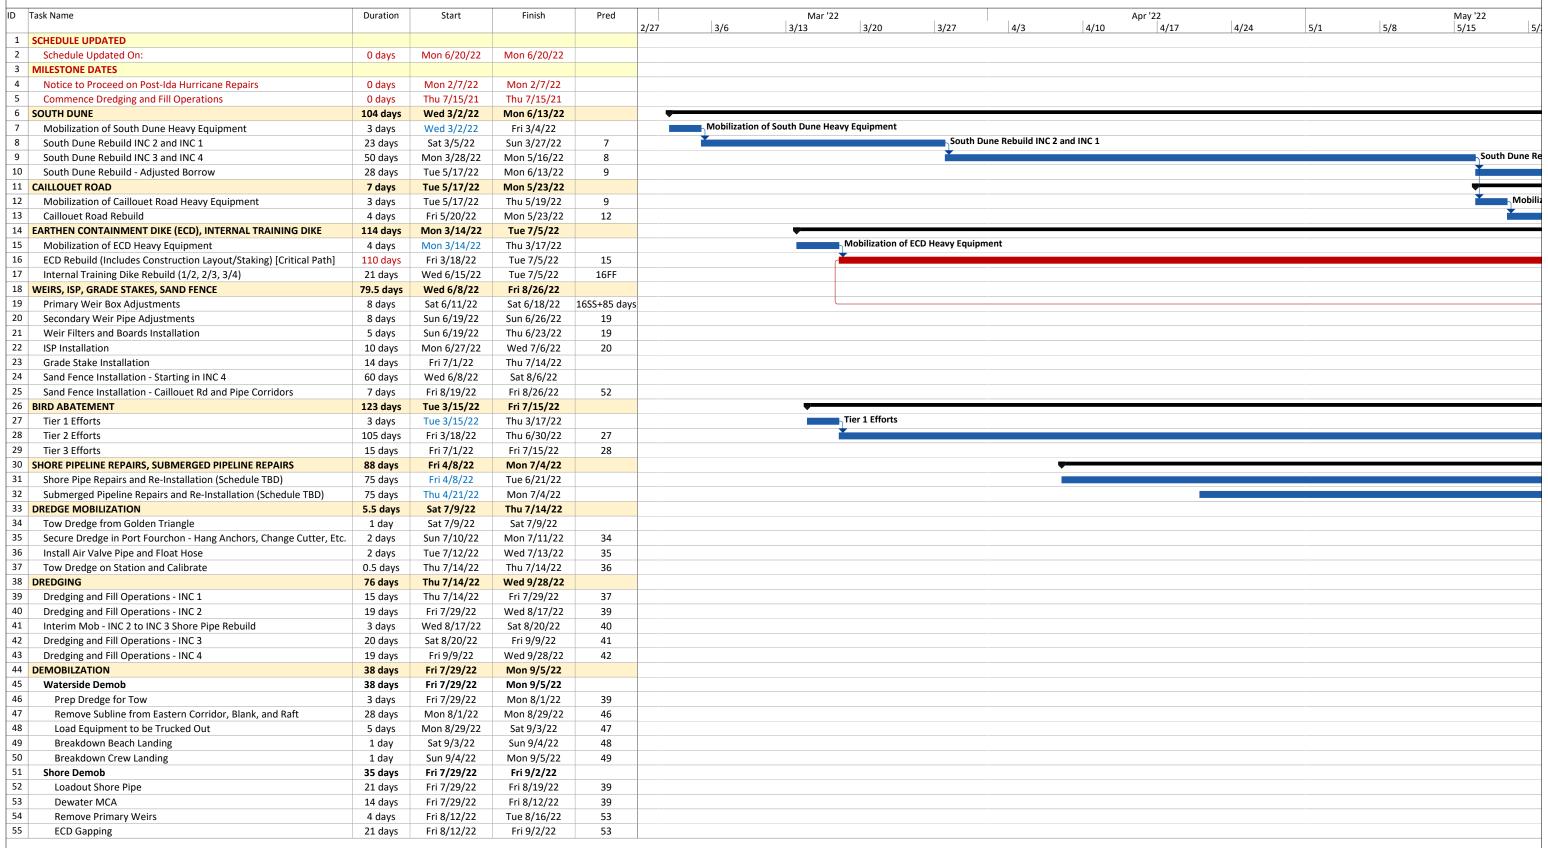


1 of 3








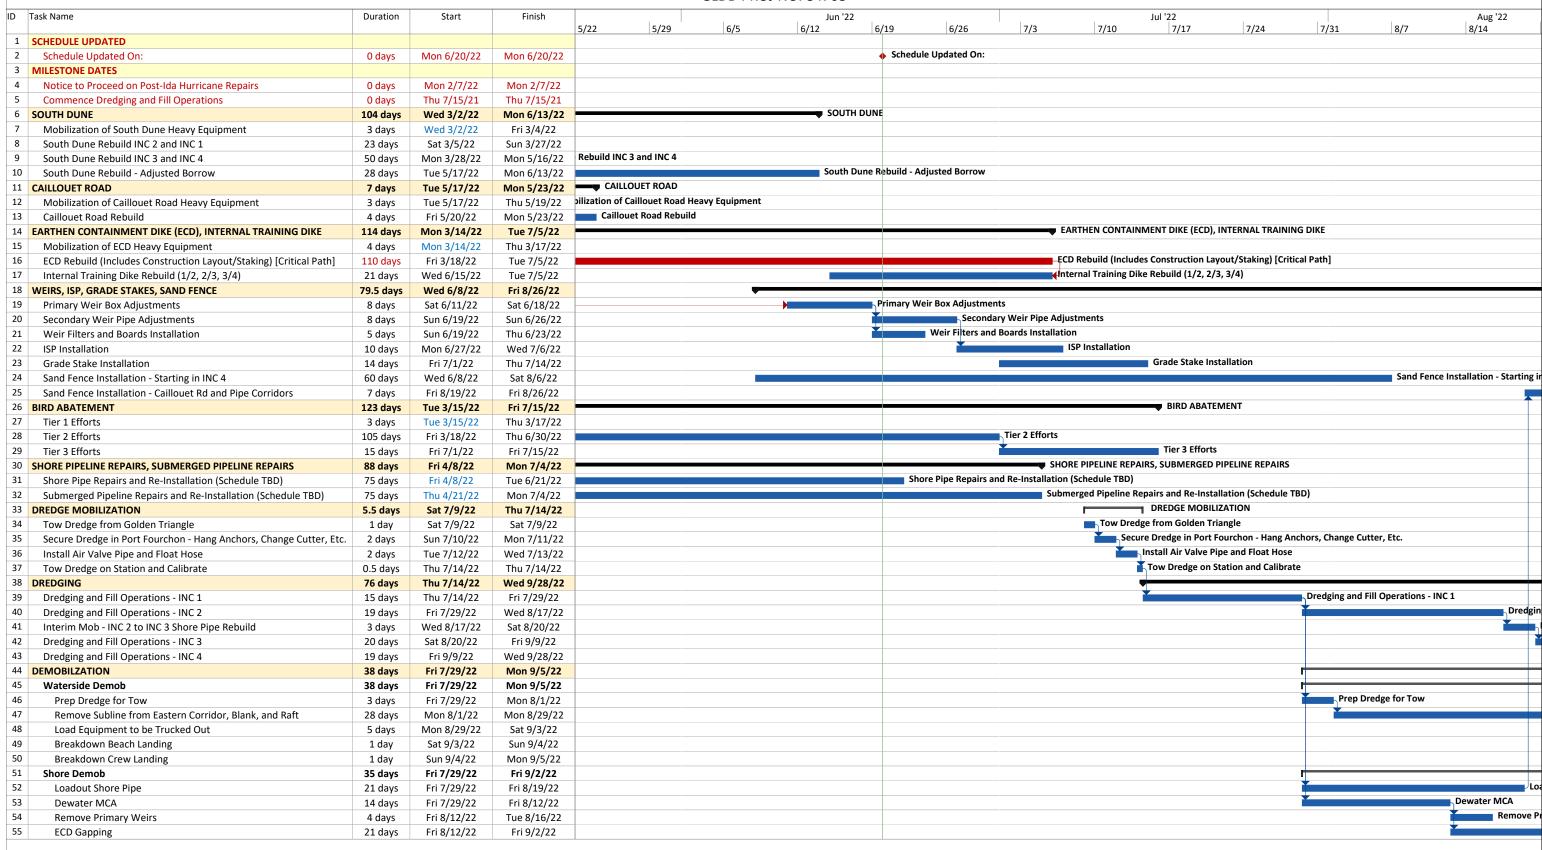








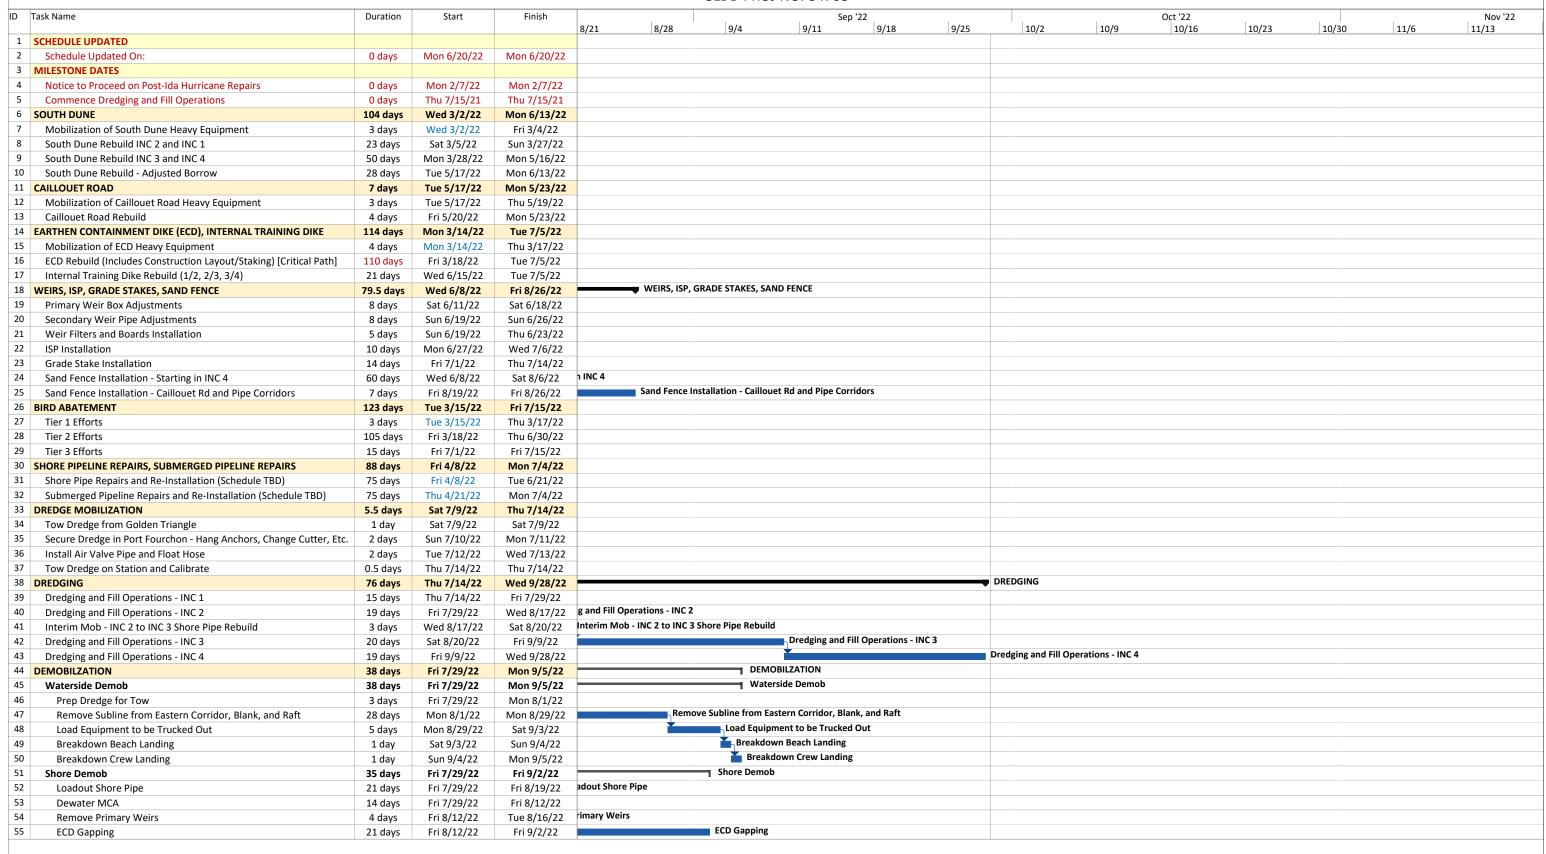







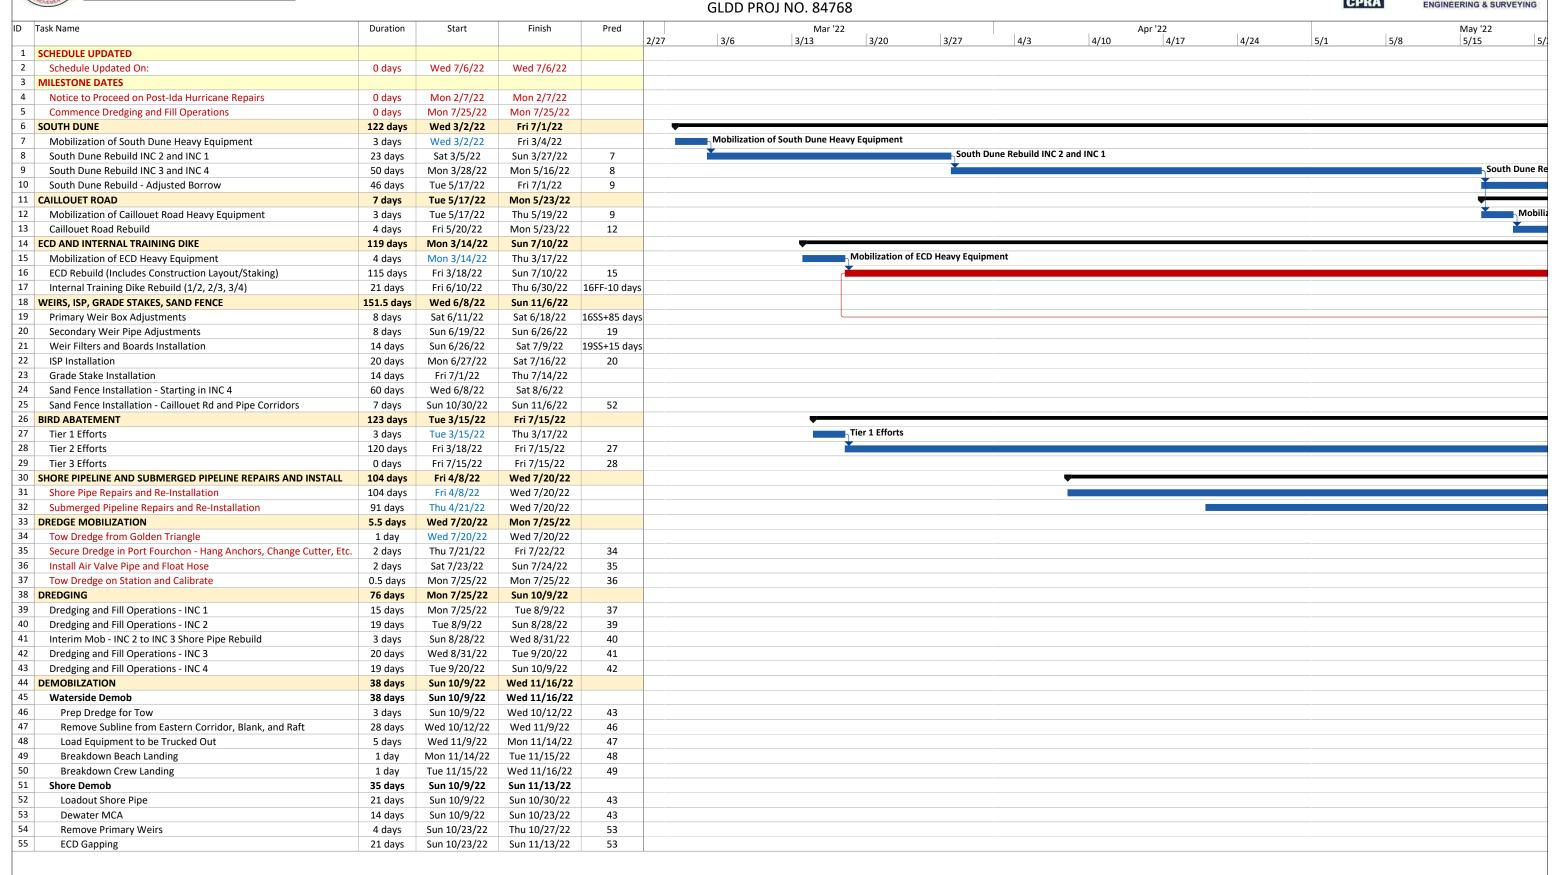


1 of 3








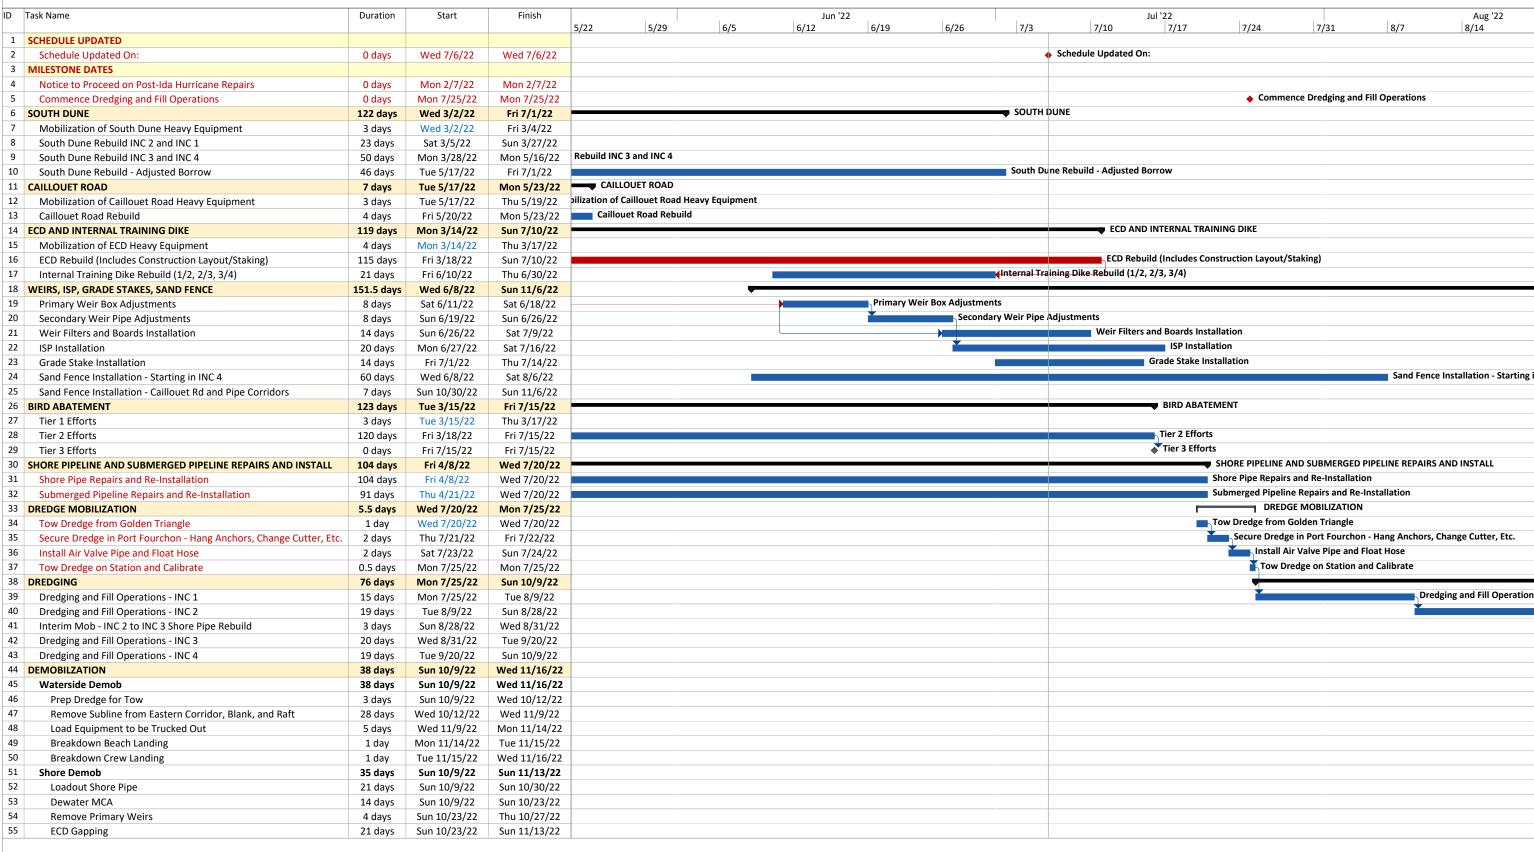








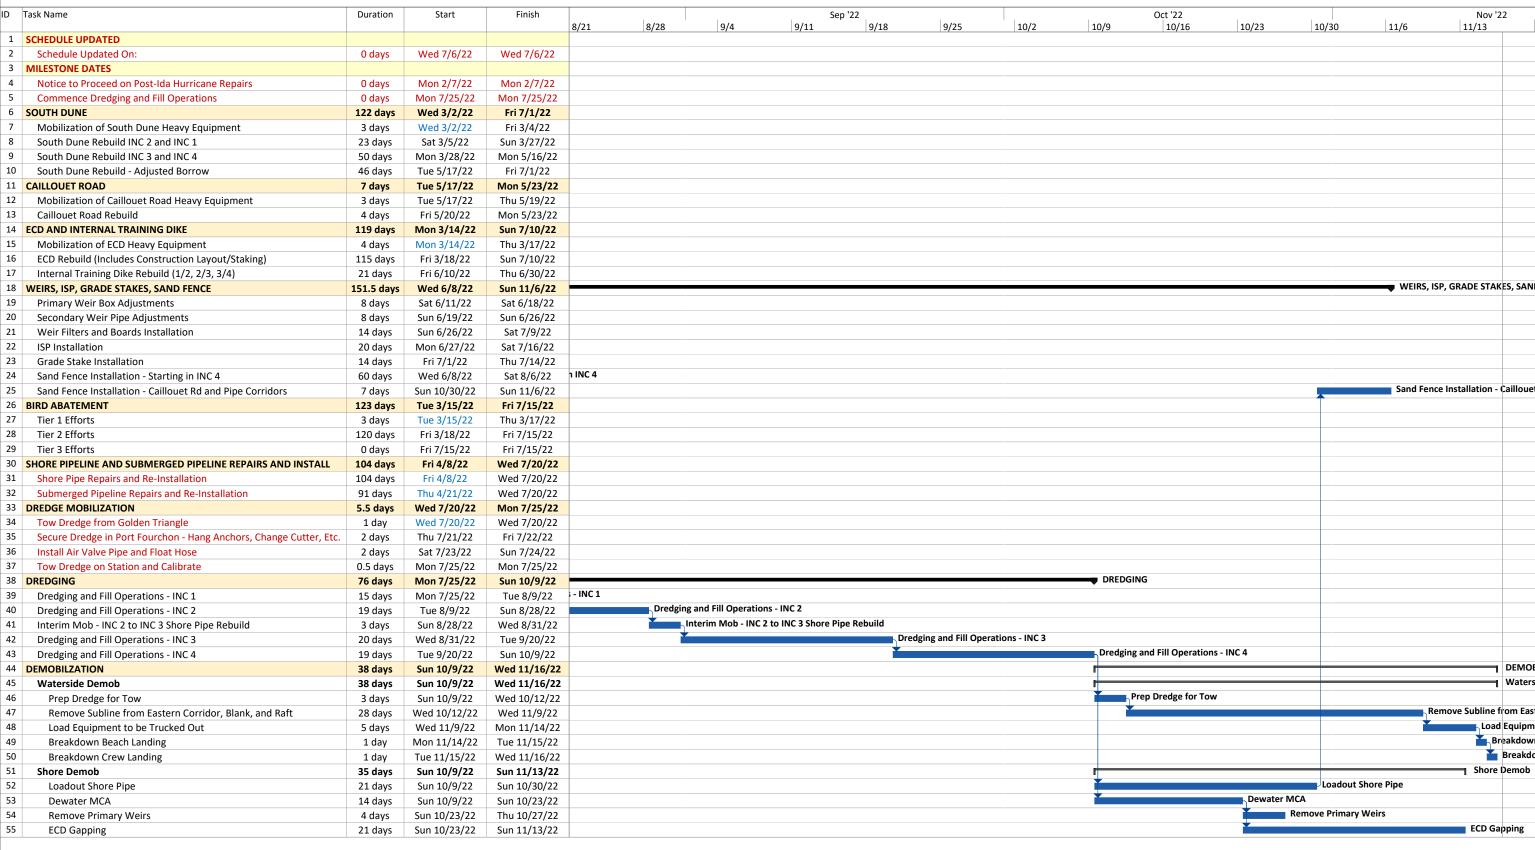








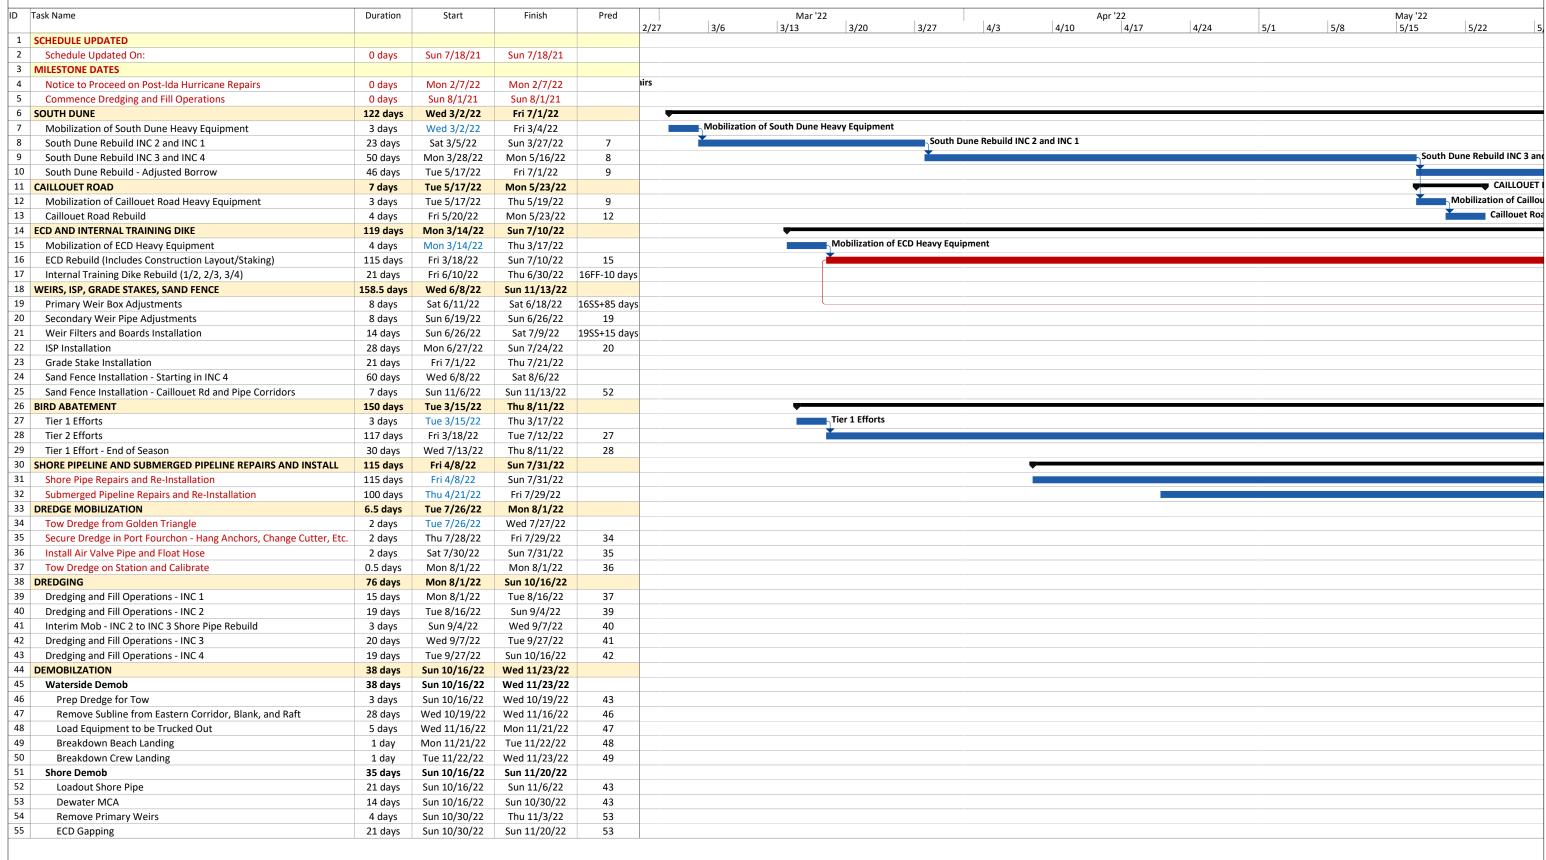








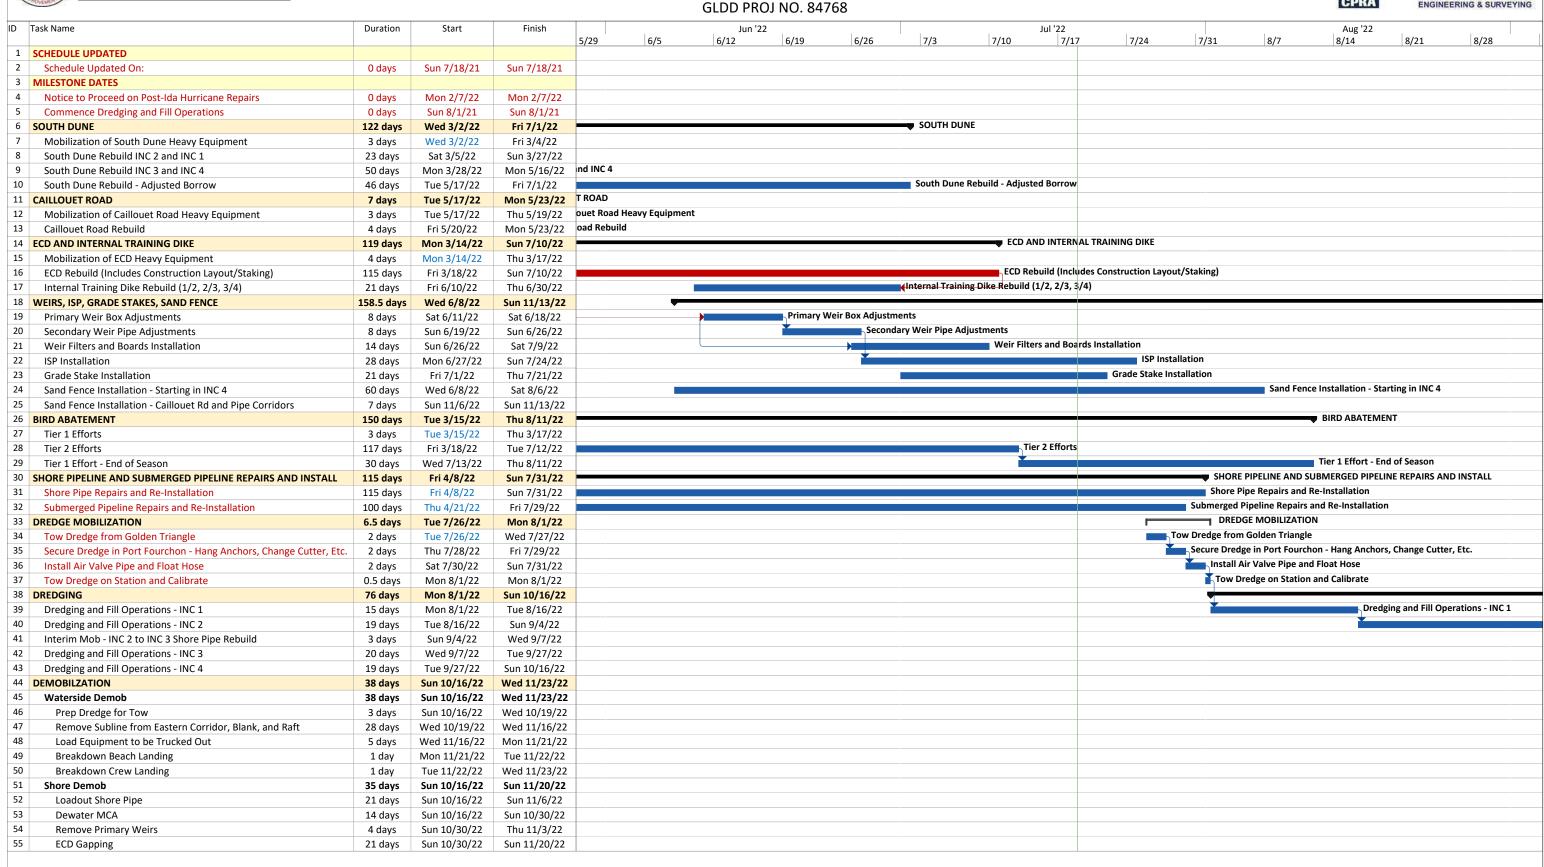








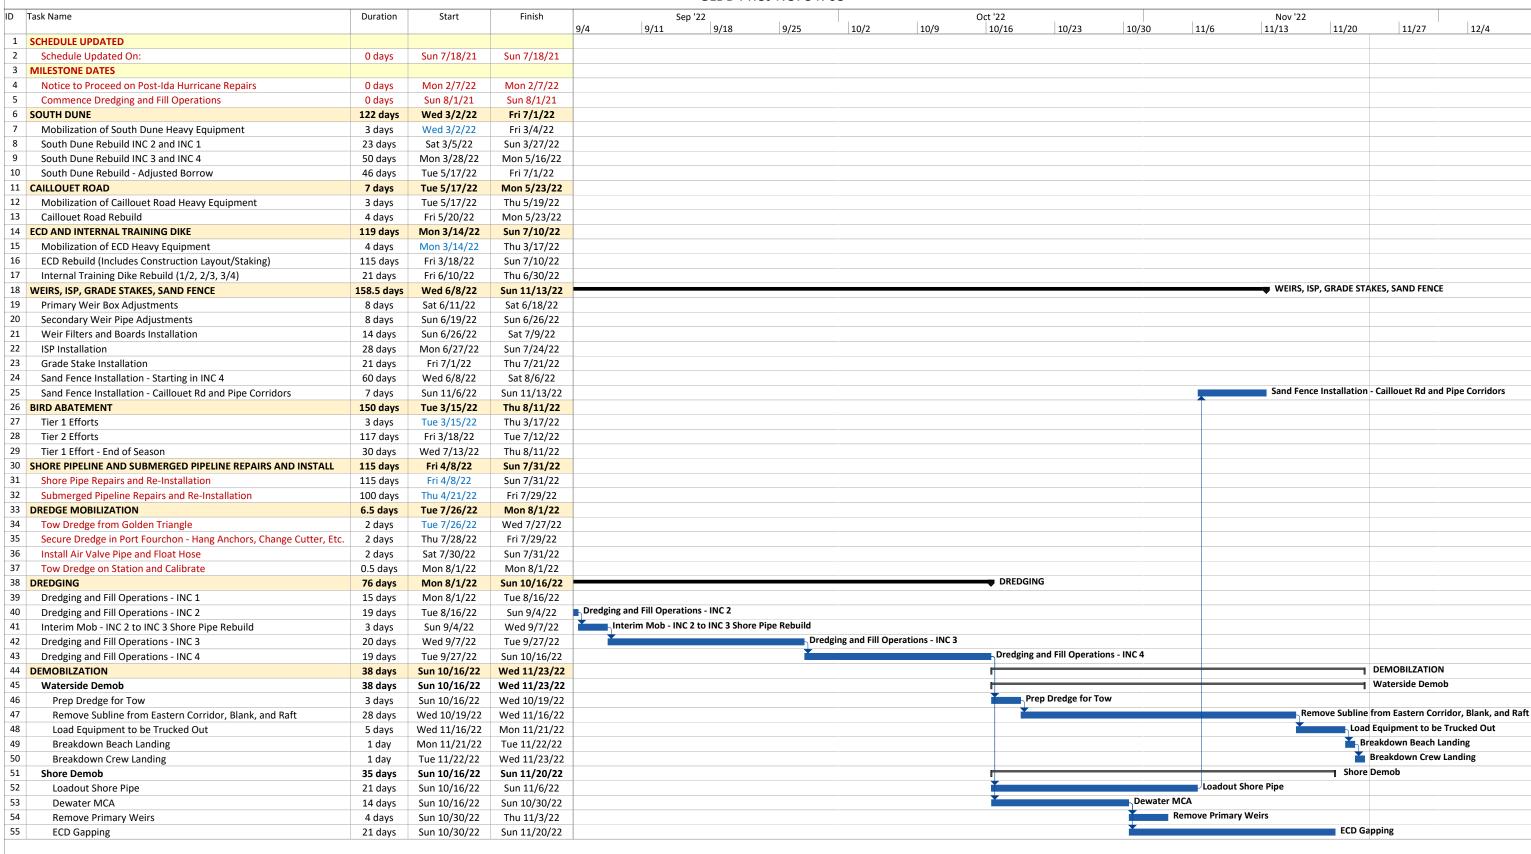







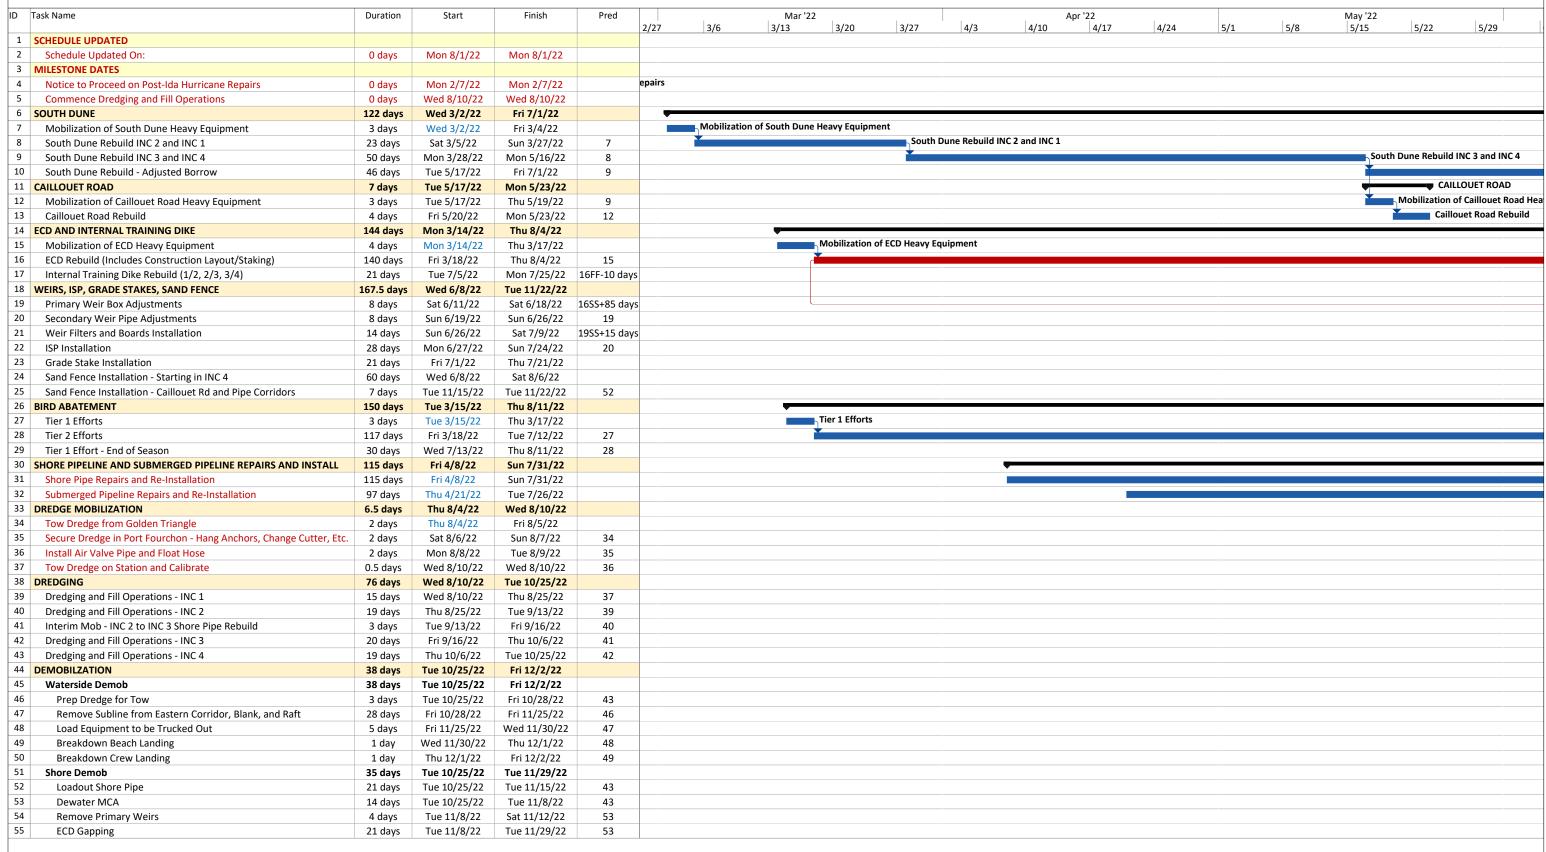




GLDD PROLNO, 84768






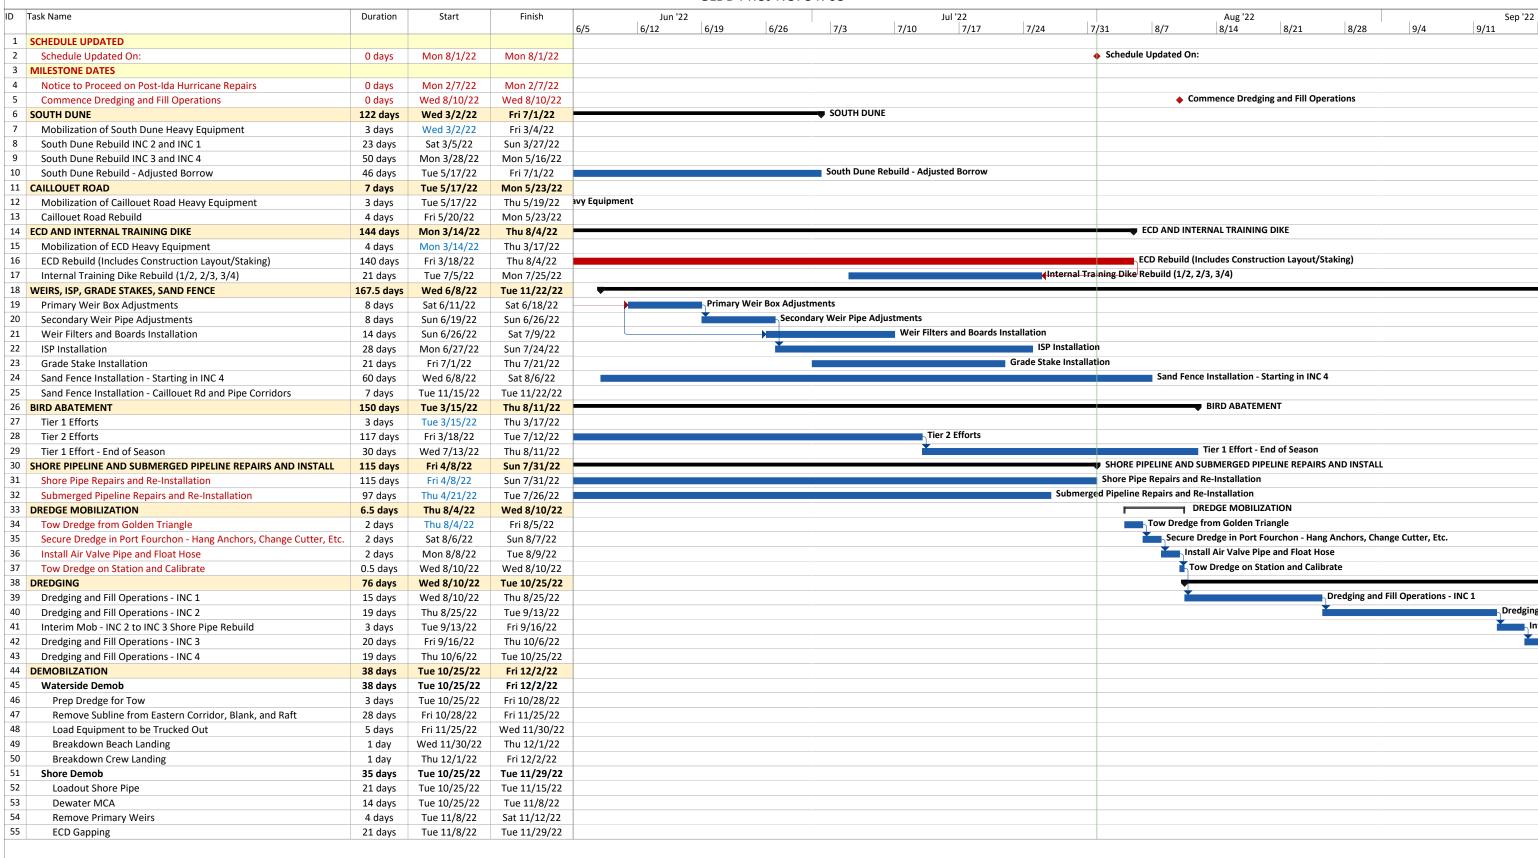








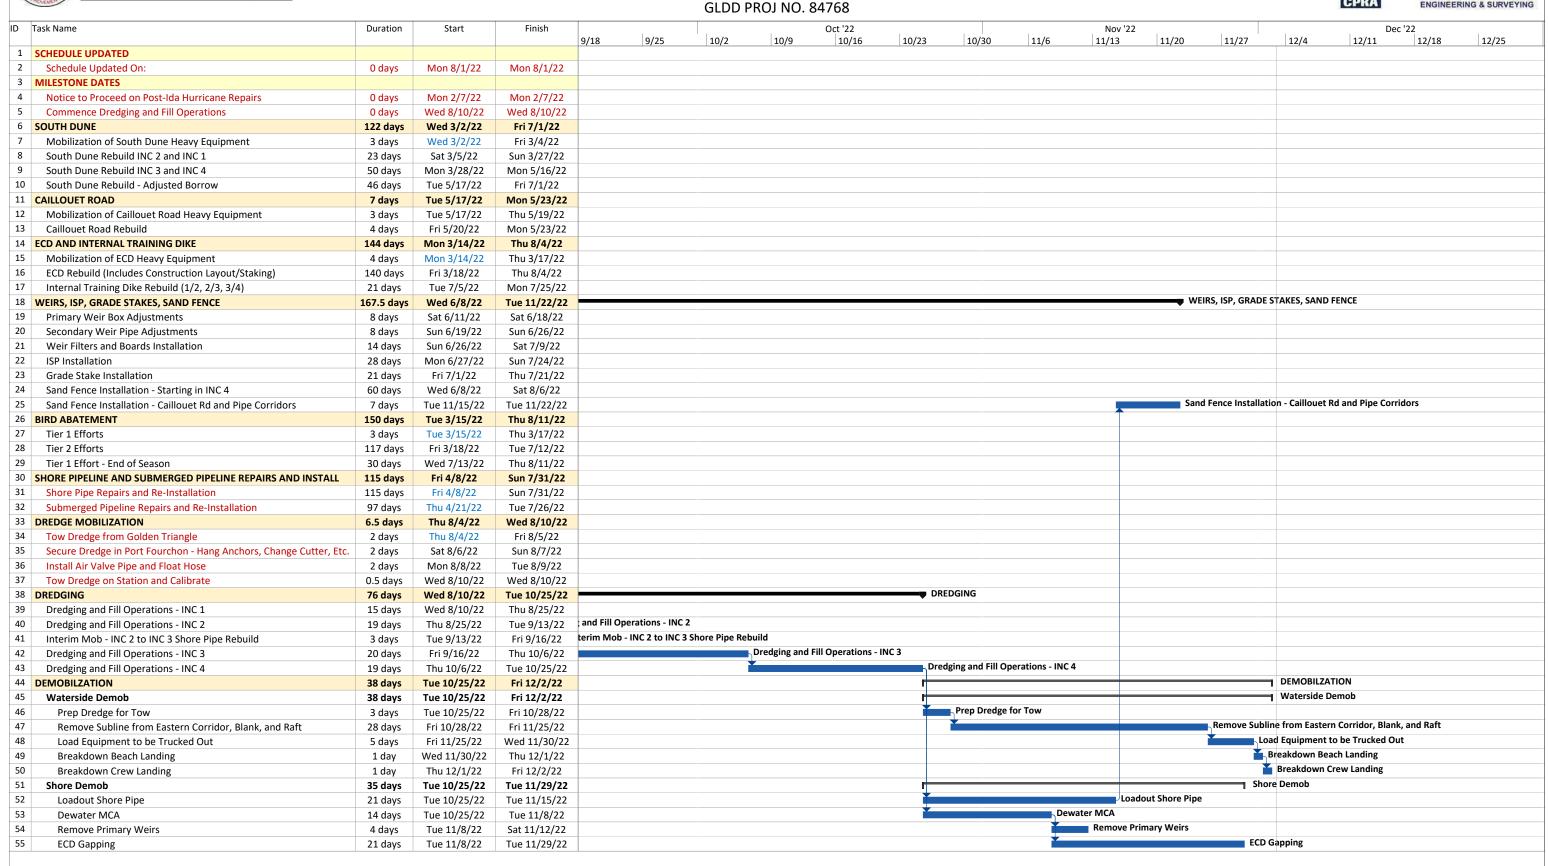







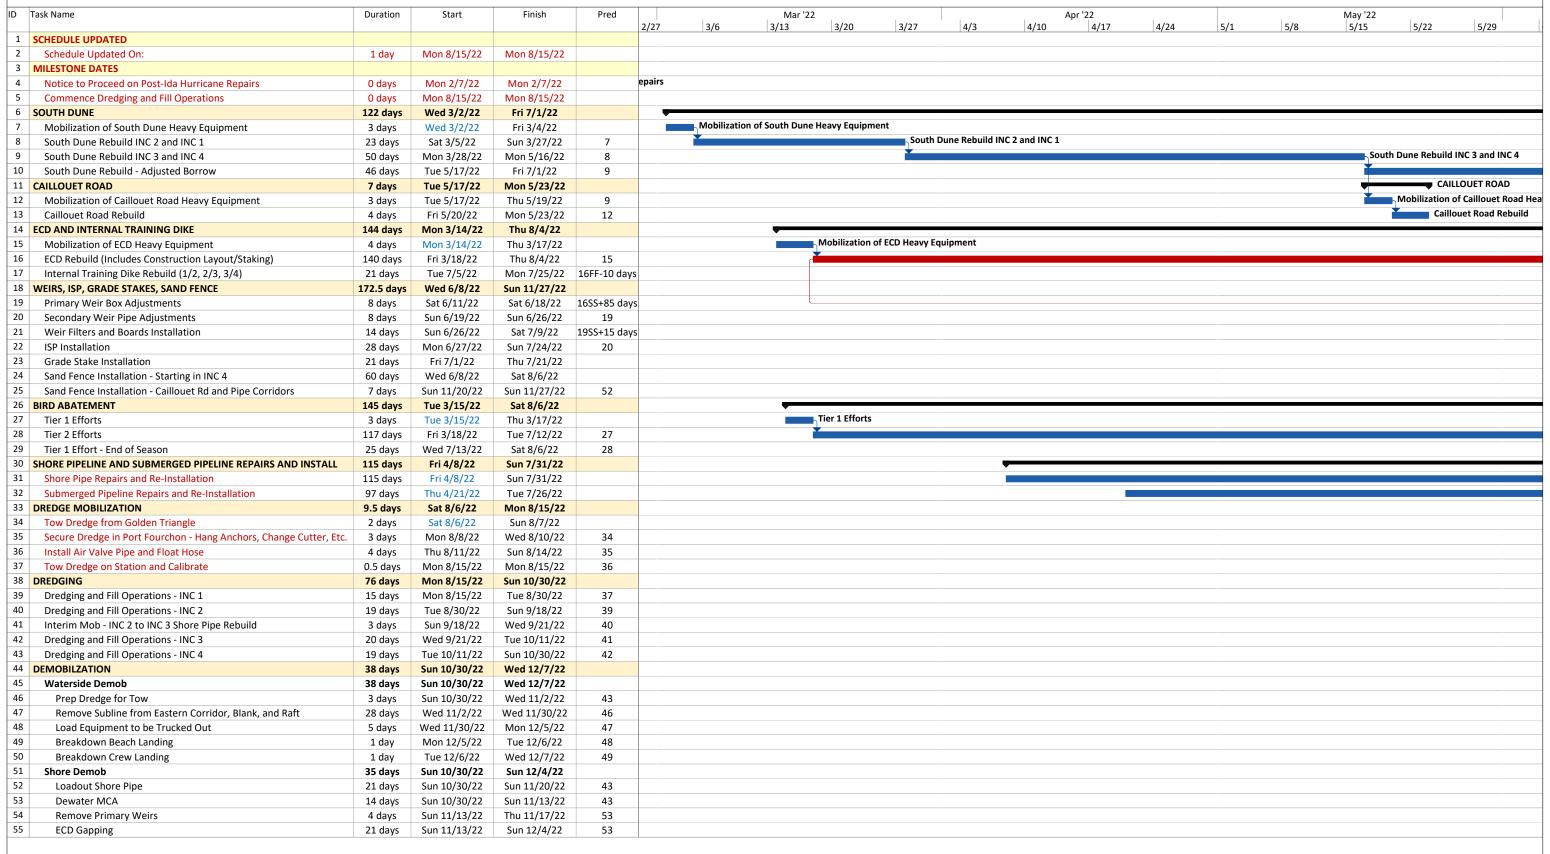




GLDD PROLNO, 84768






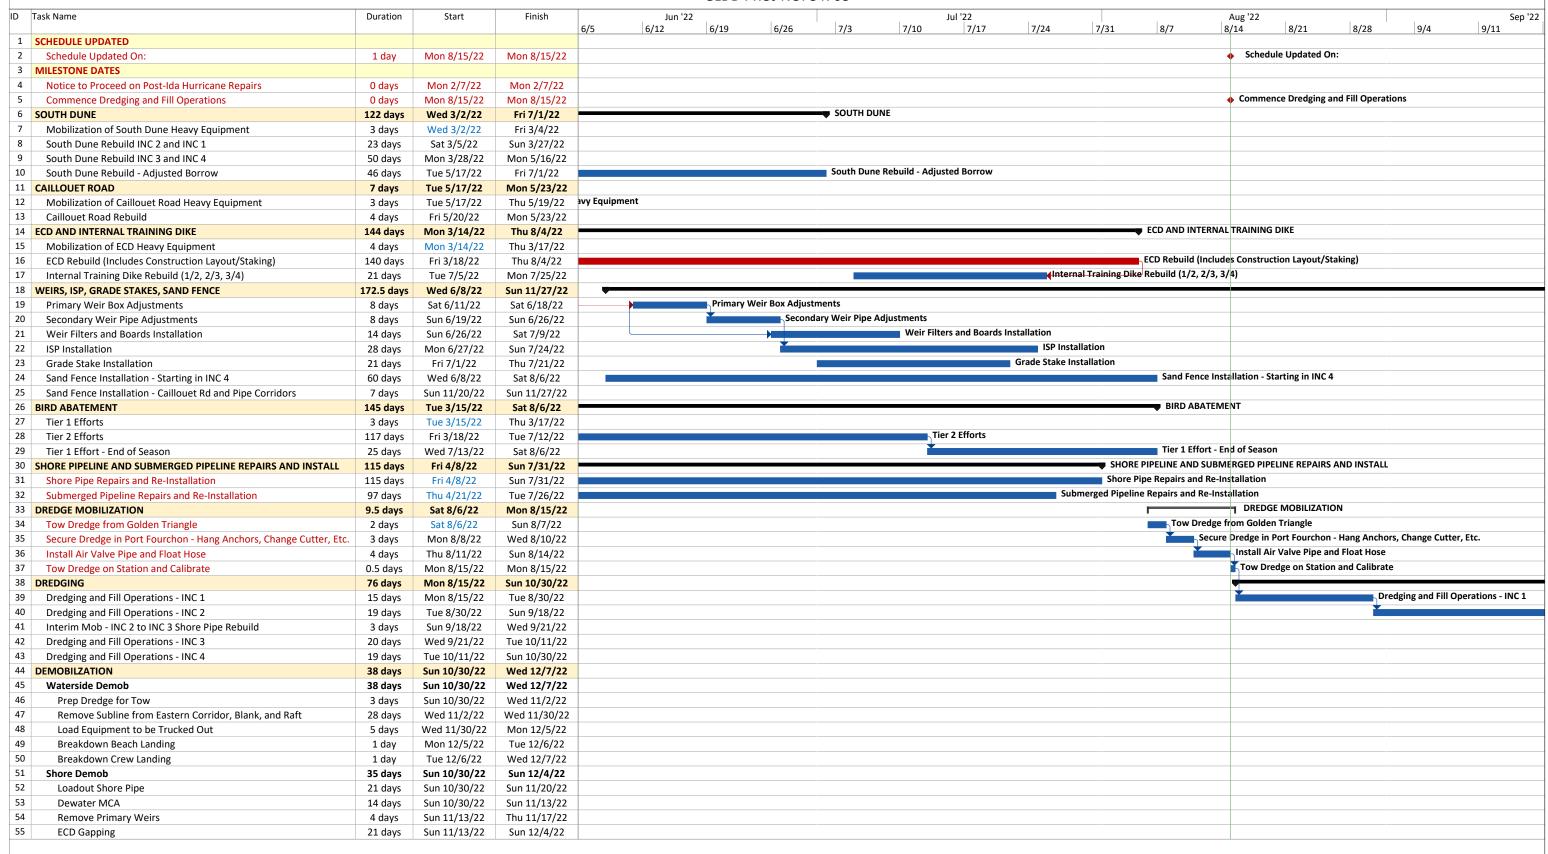







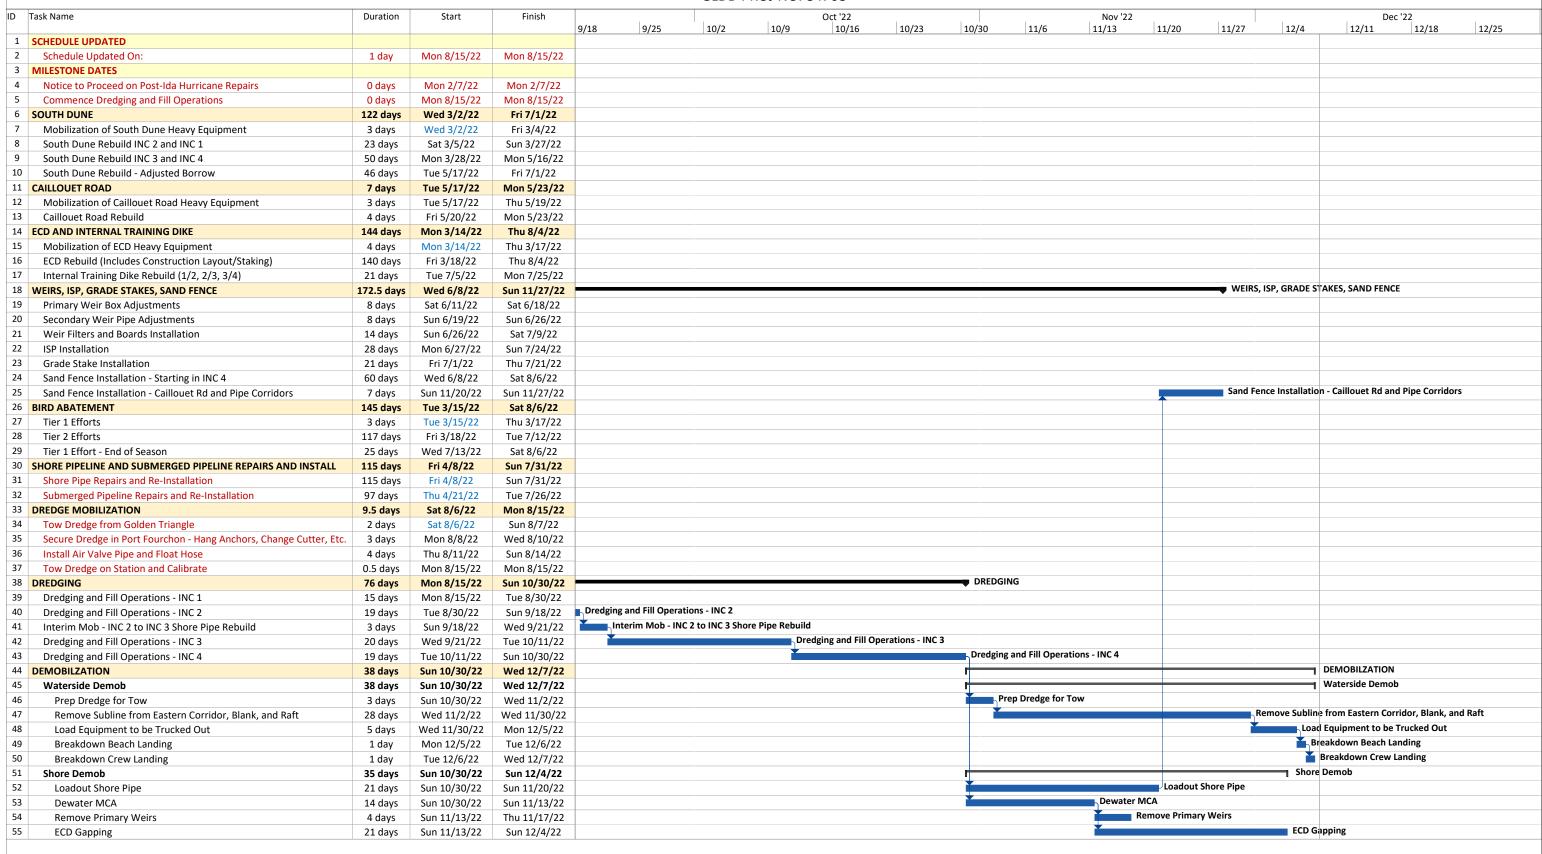




GLDD PROJ NO. 84768





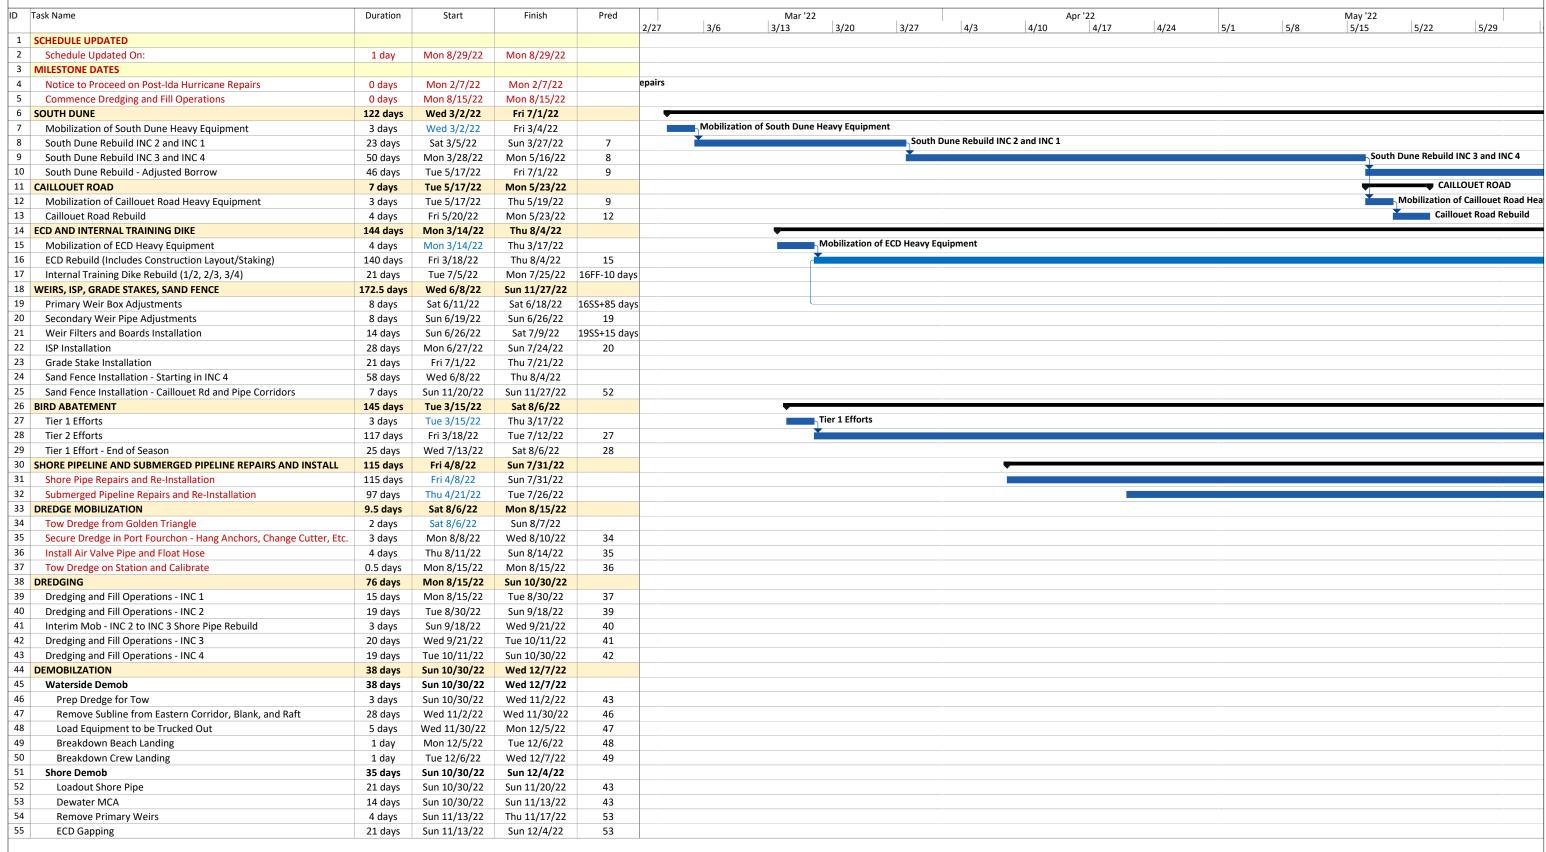


1 of 3



GLDD PROLNO, 84768






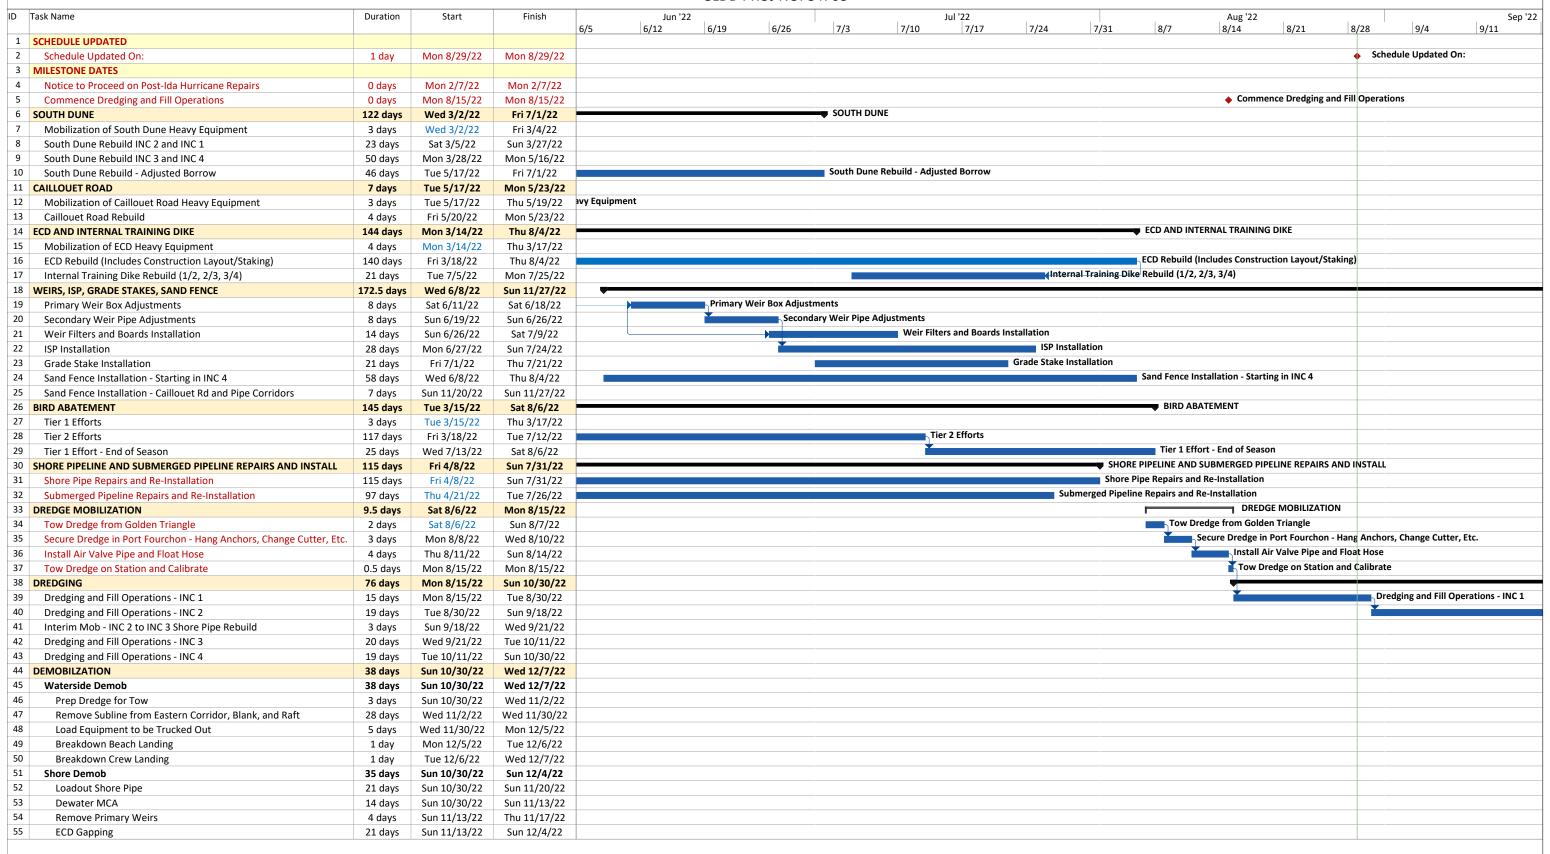








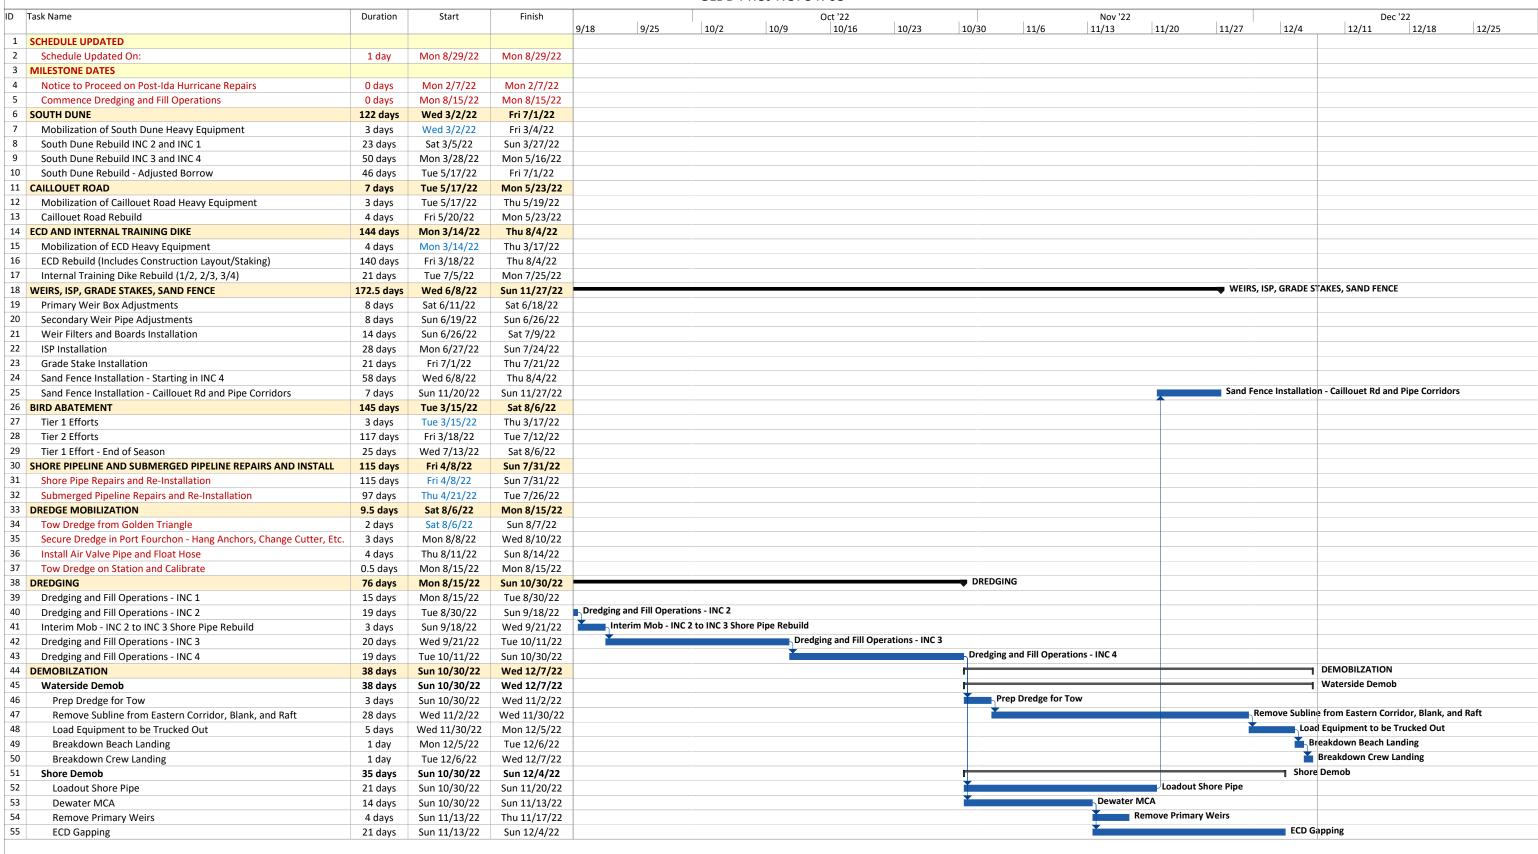







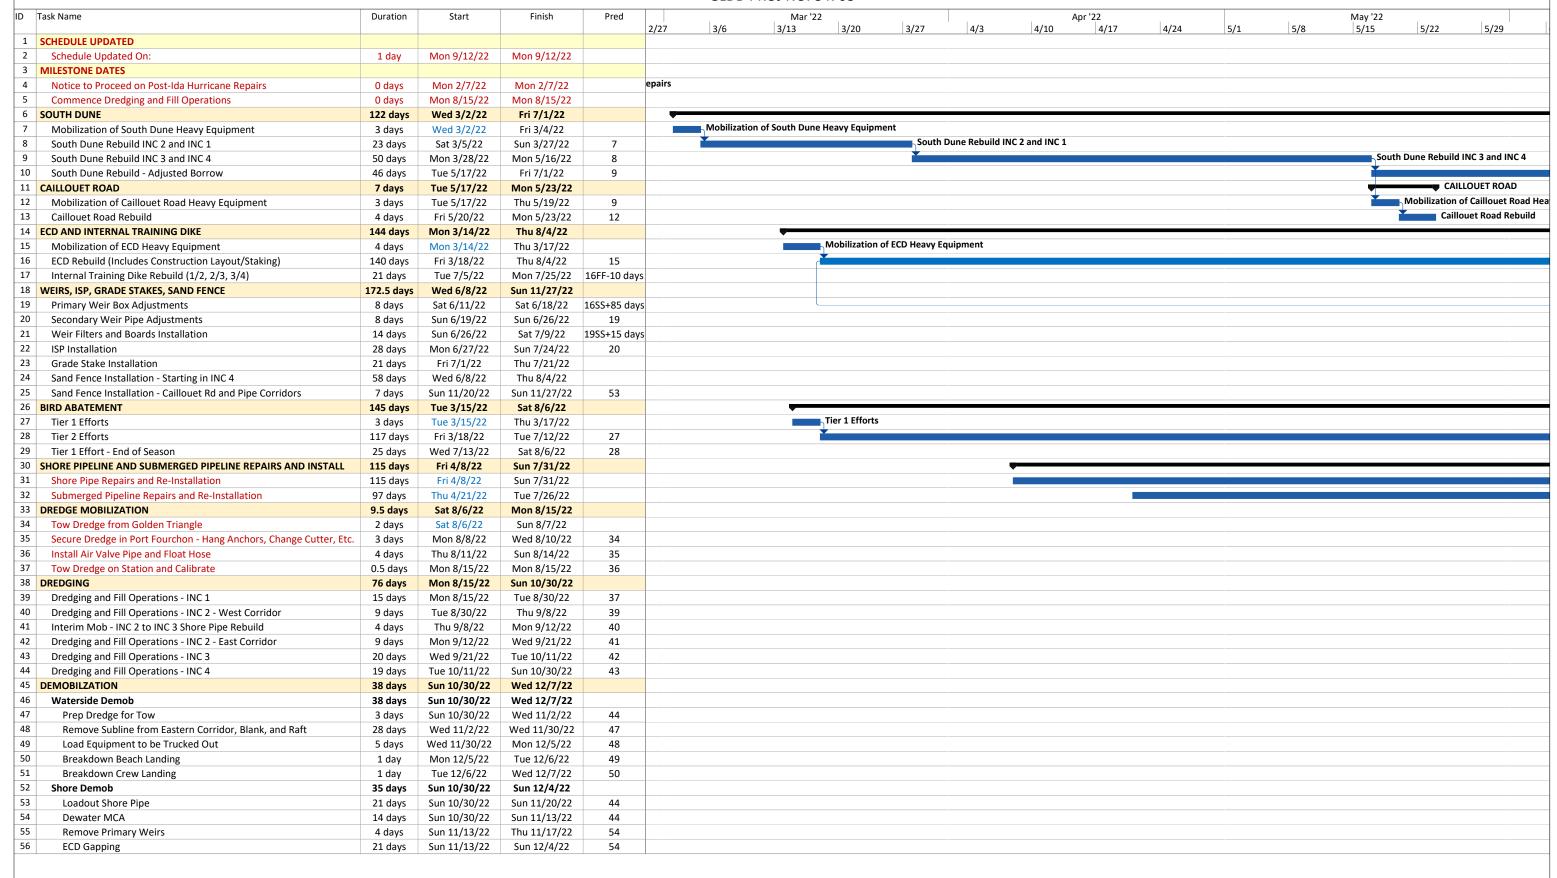




GLDD PROLNO, 84768






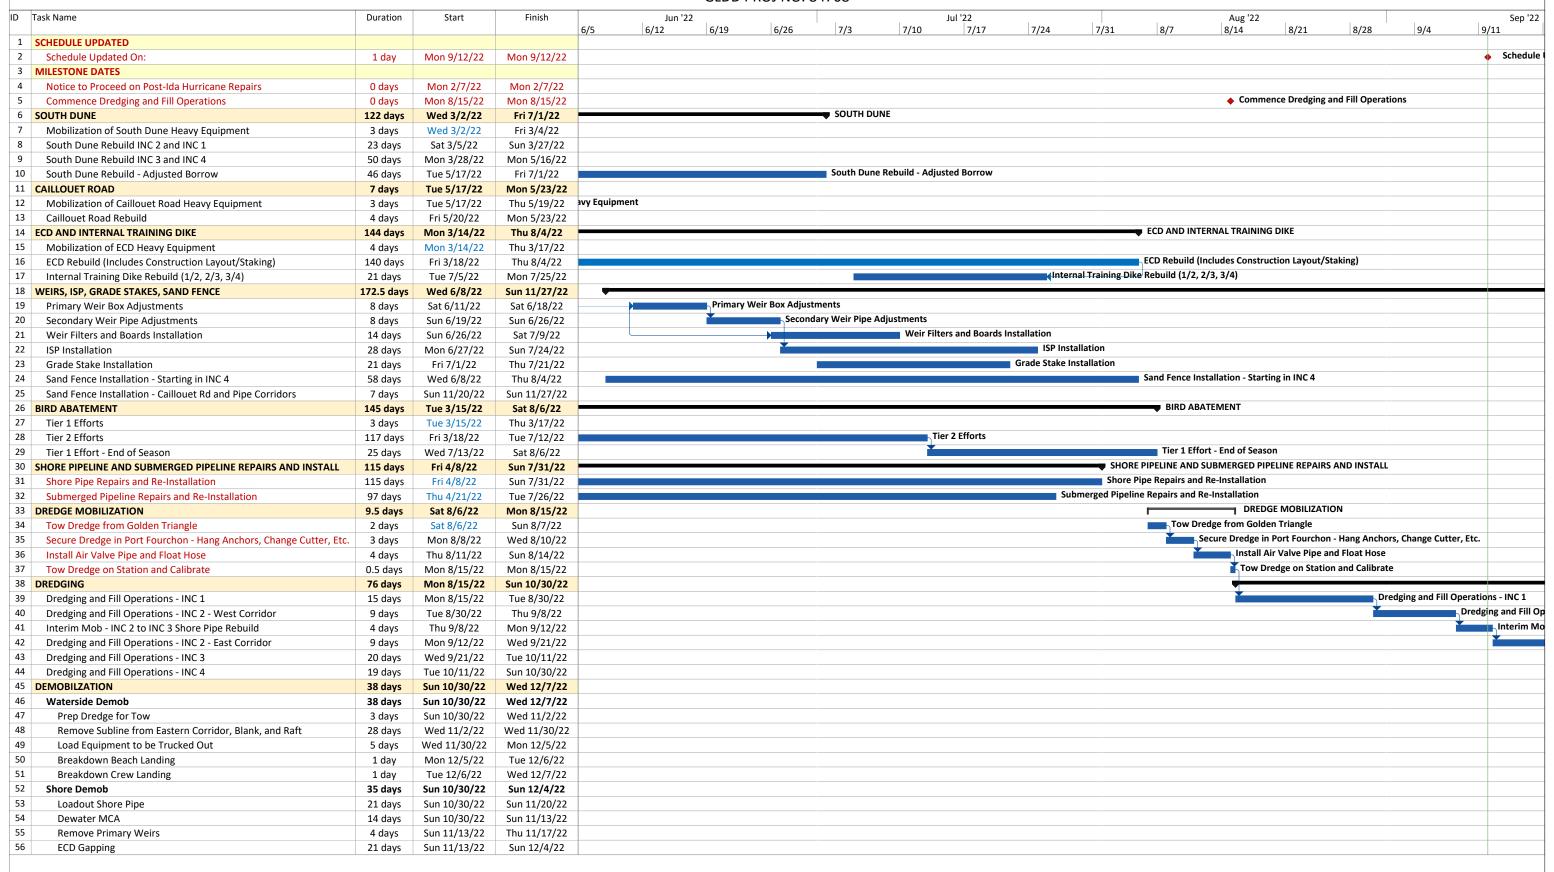








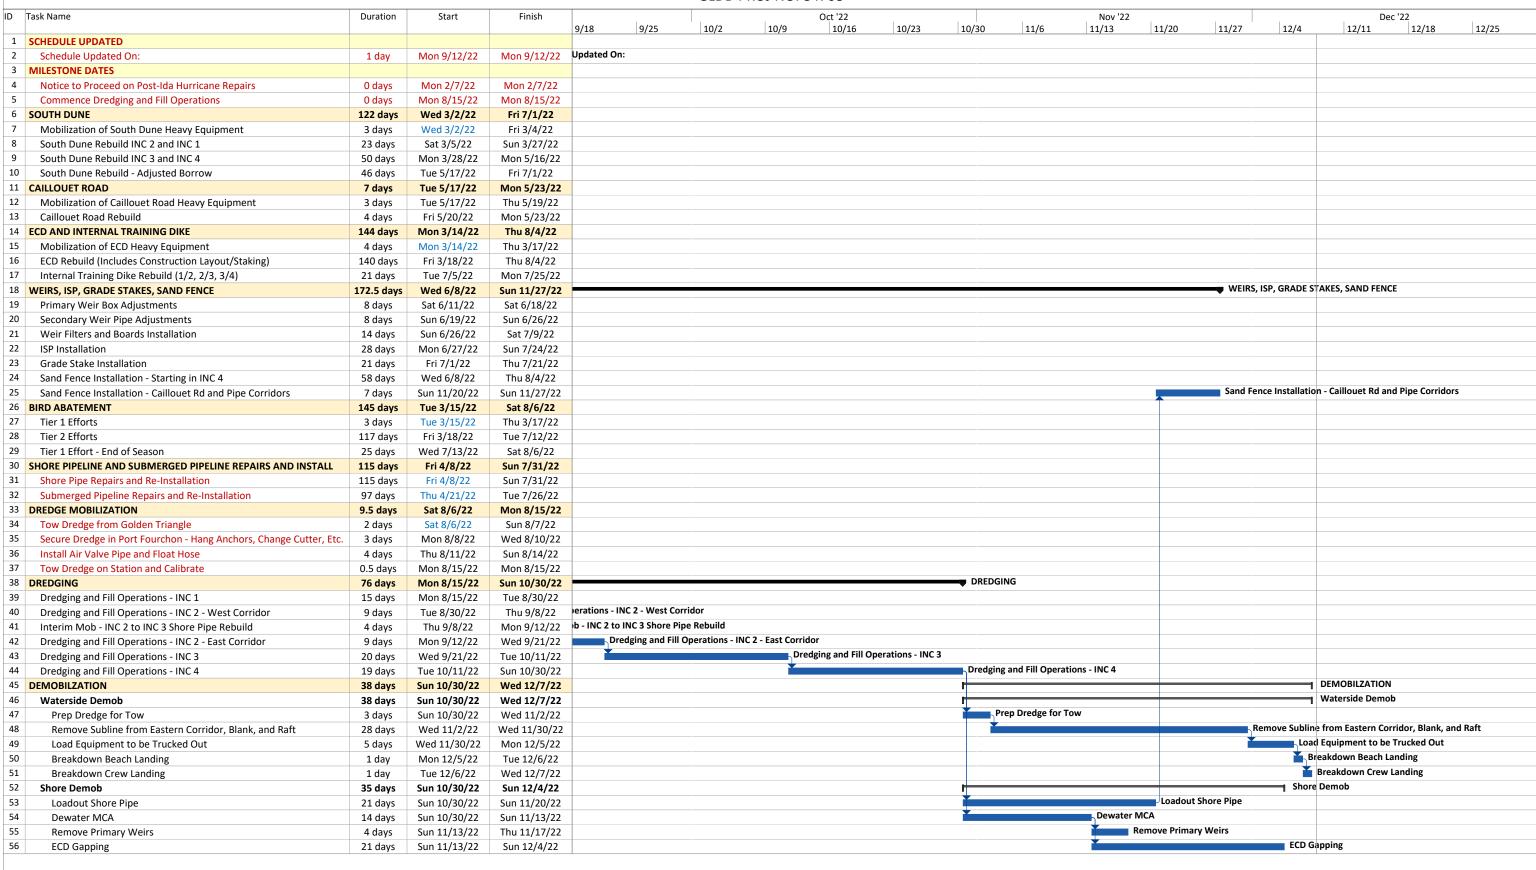







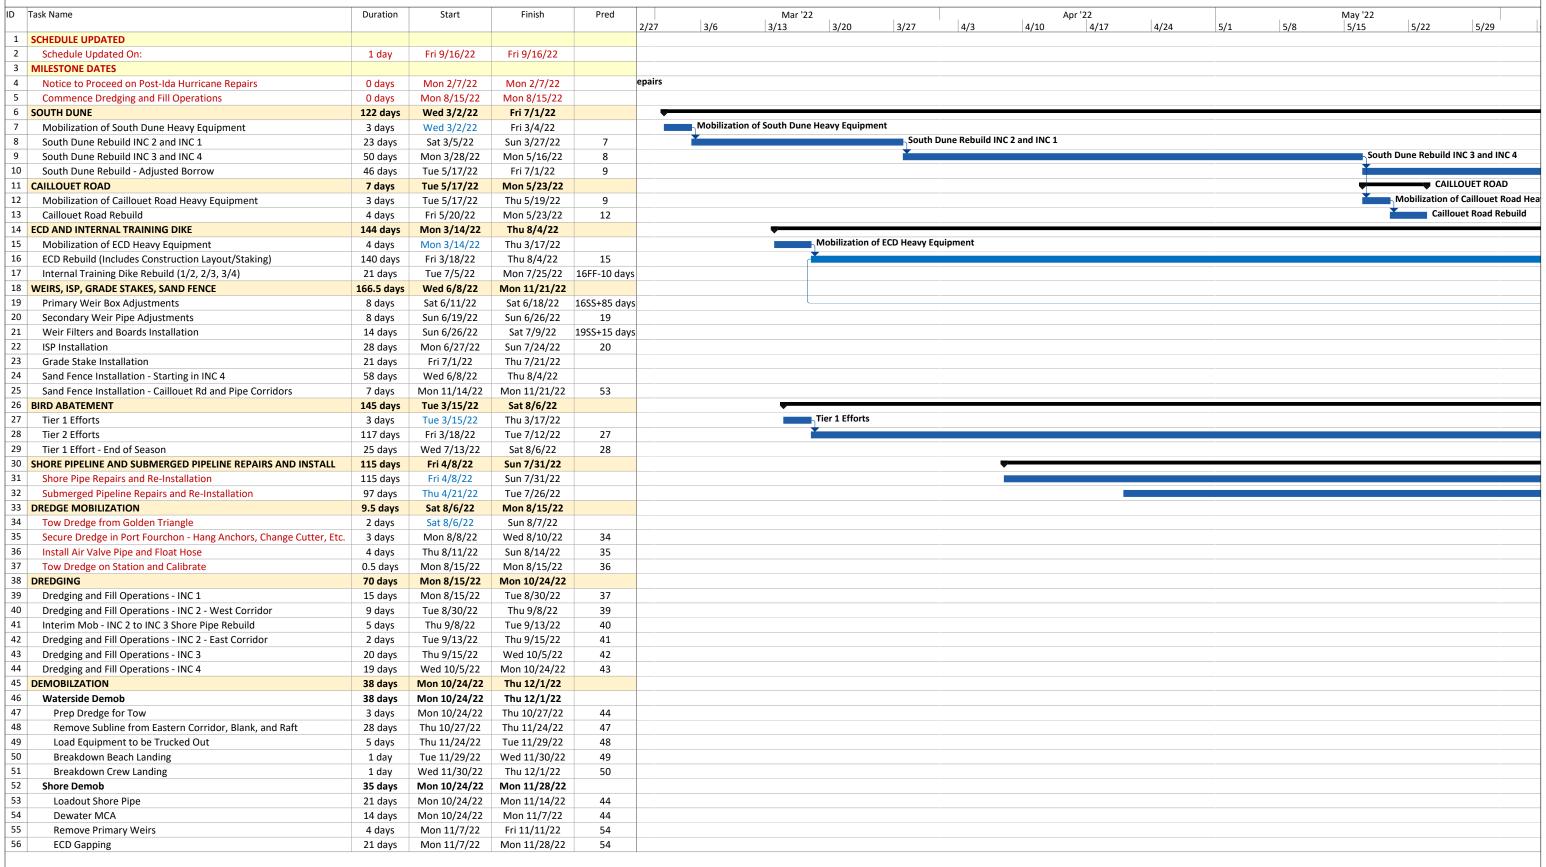




GLDD PROLNO, 84768





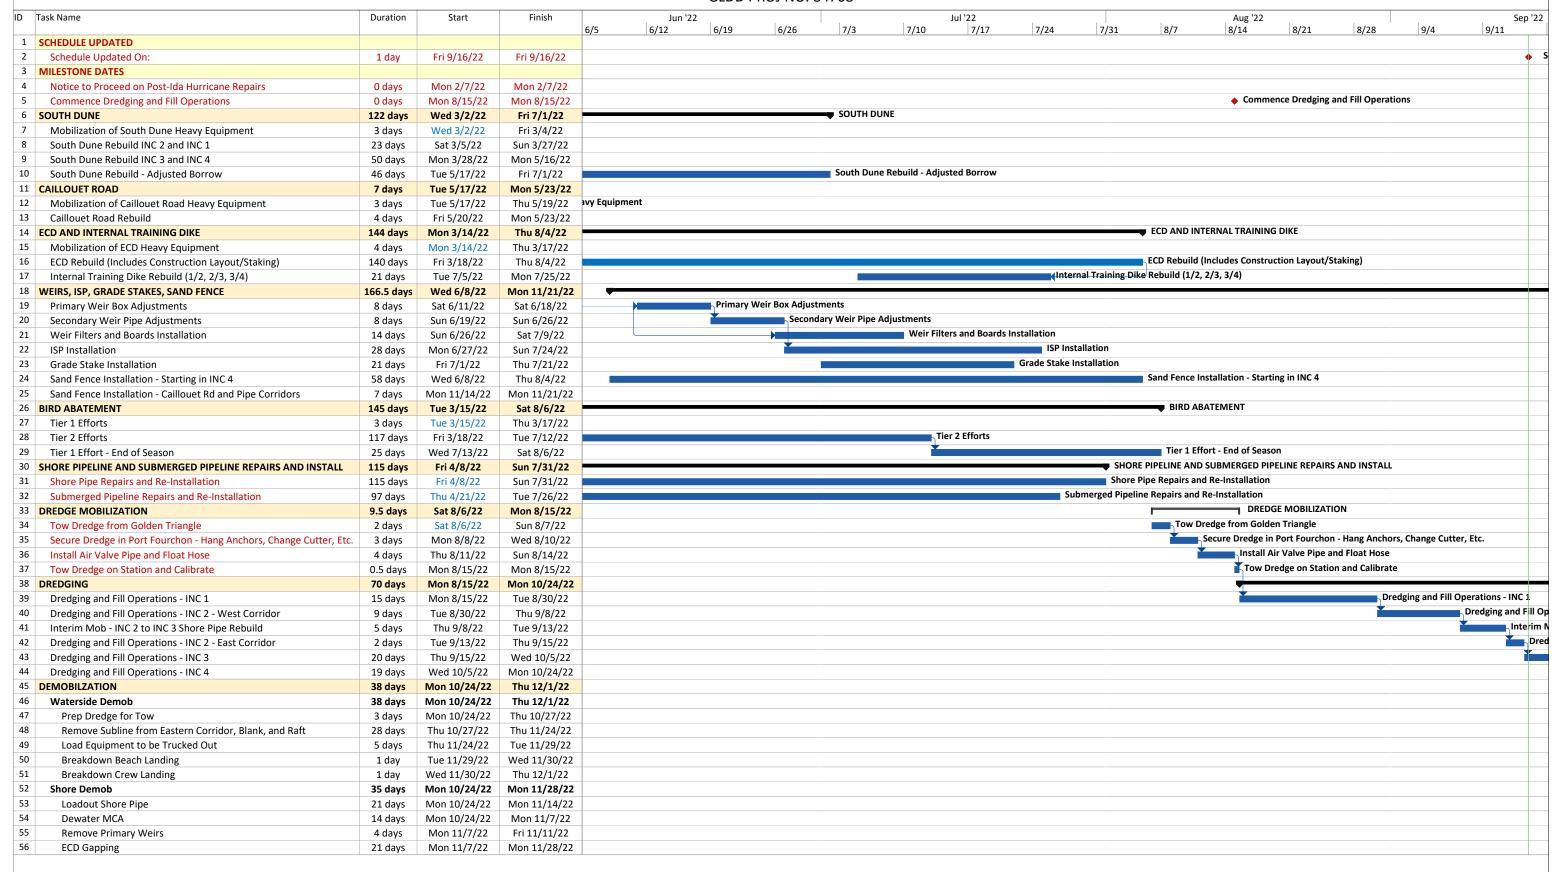




GLDD PROJ NO. 84768





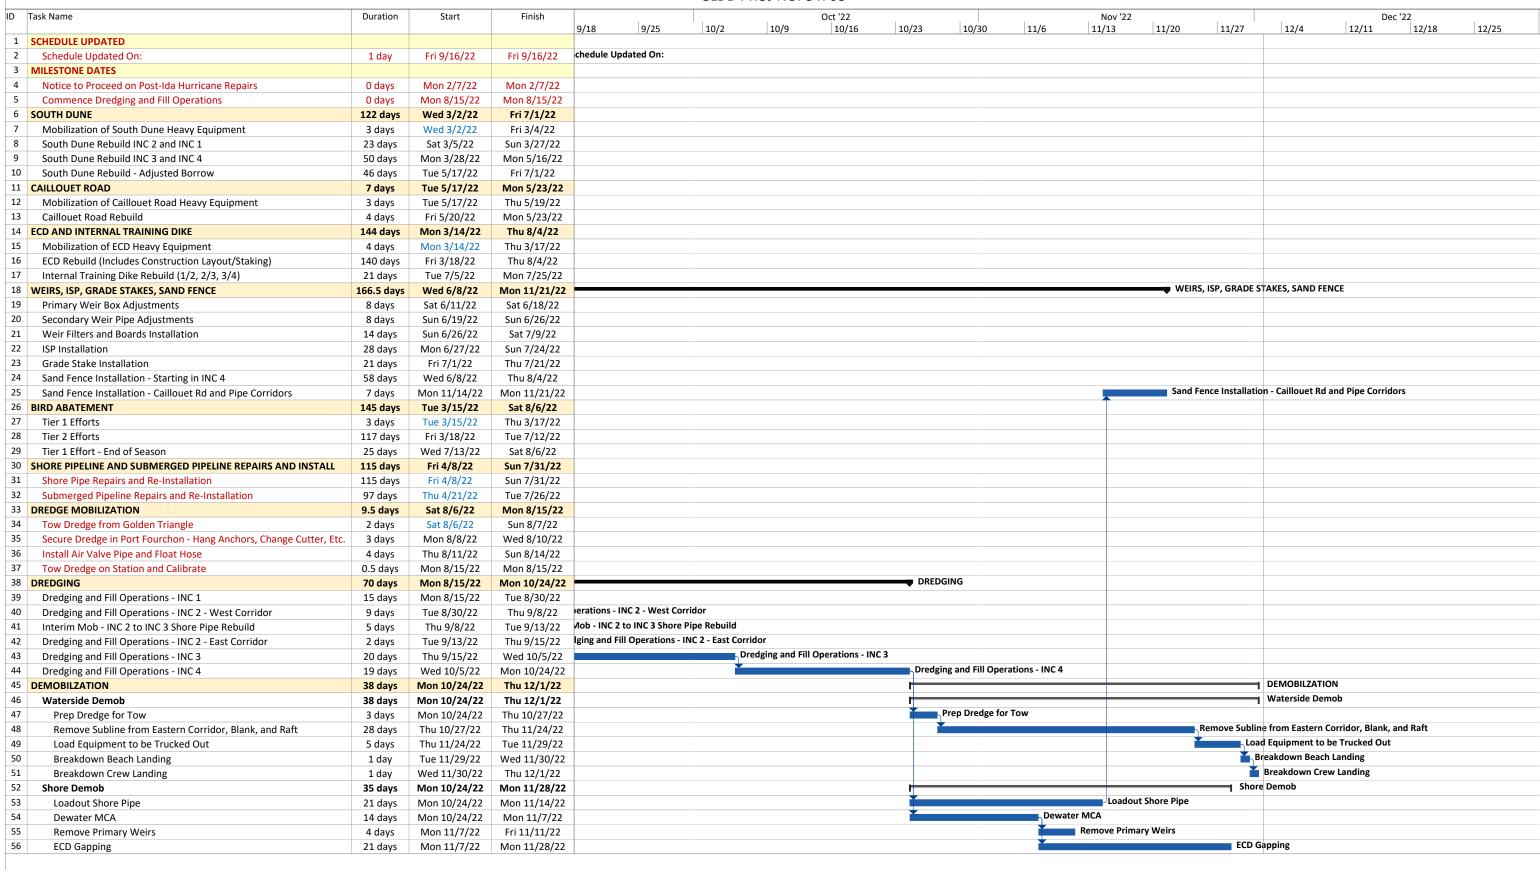




GLDD PROJ NO. 84768





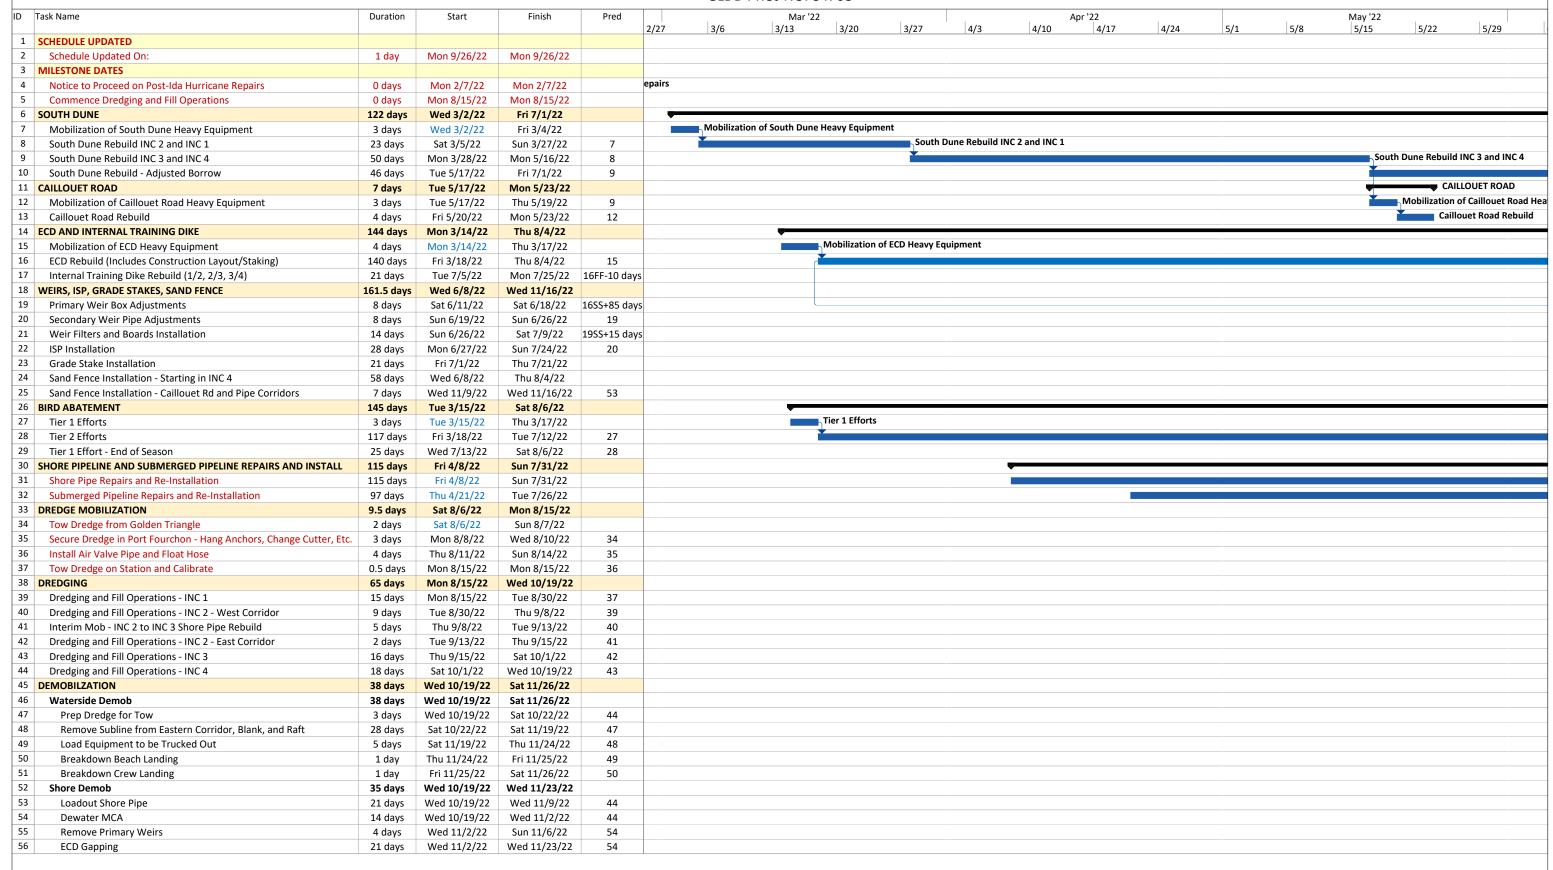




GLDD PROLNO, 84768





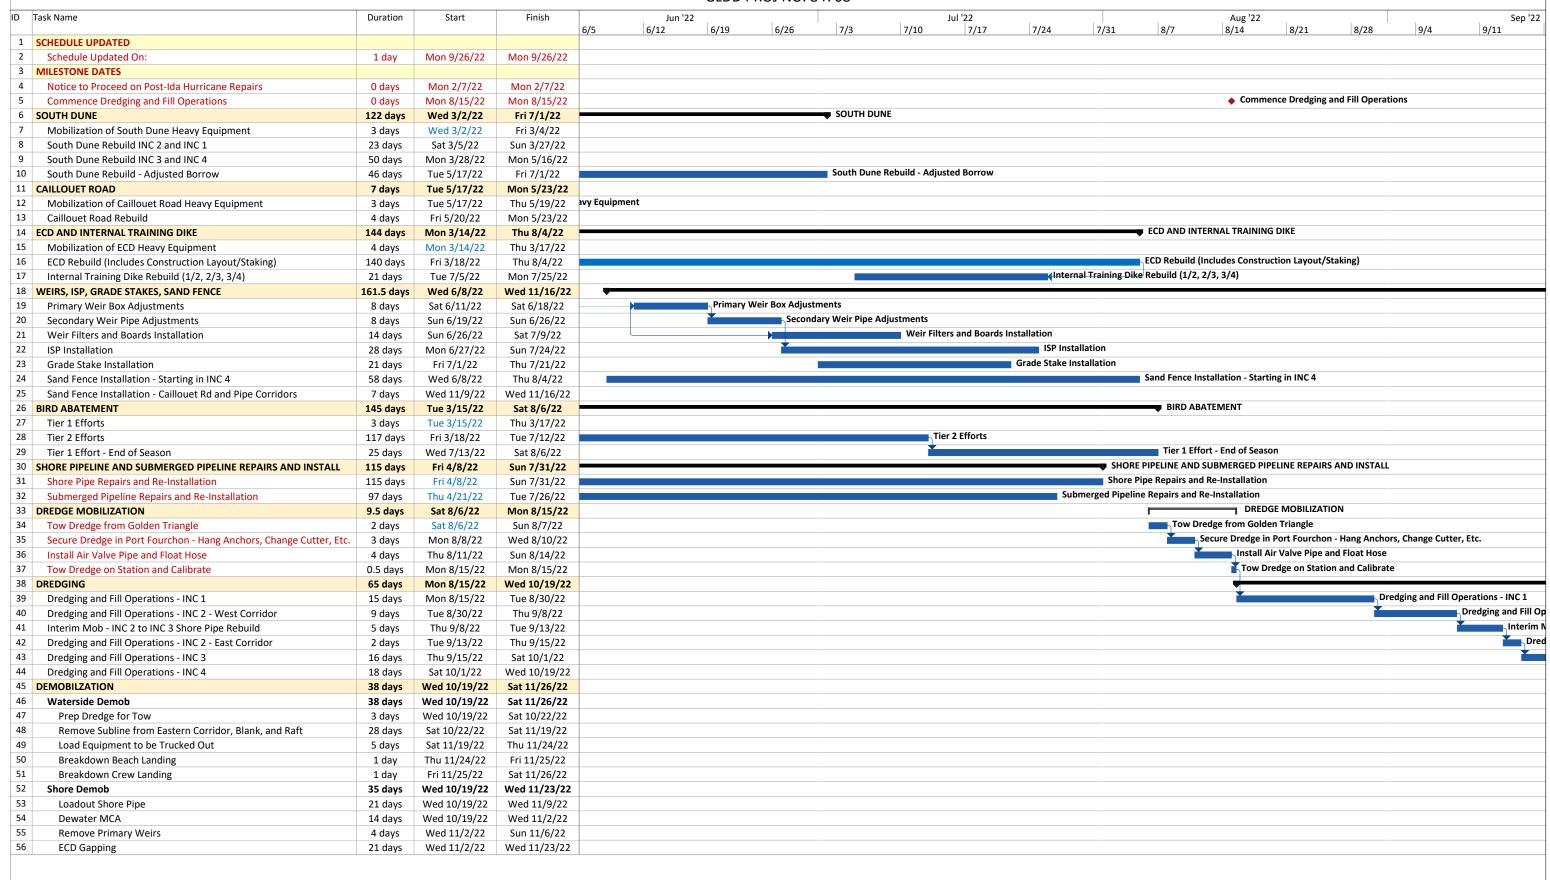




GLDD PROJ NO. 84768





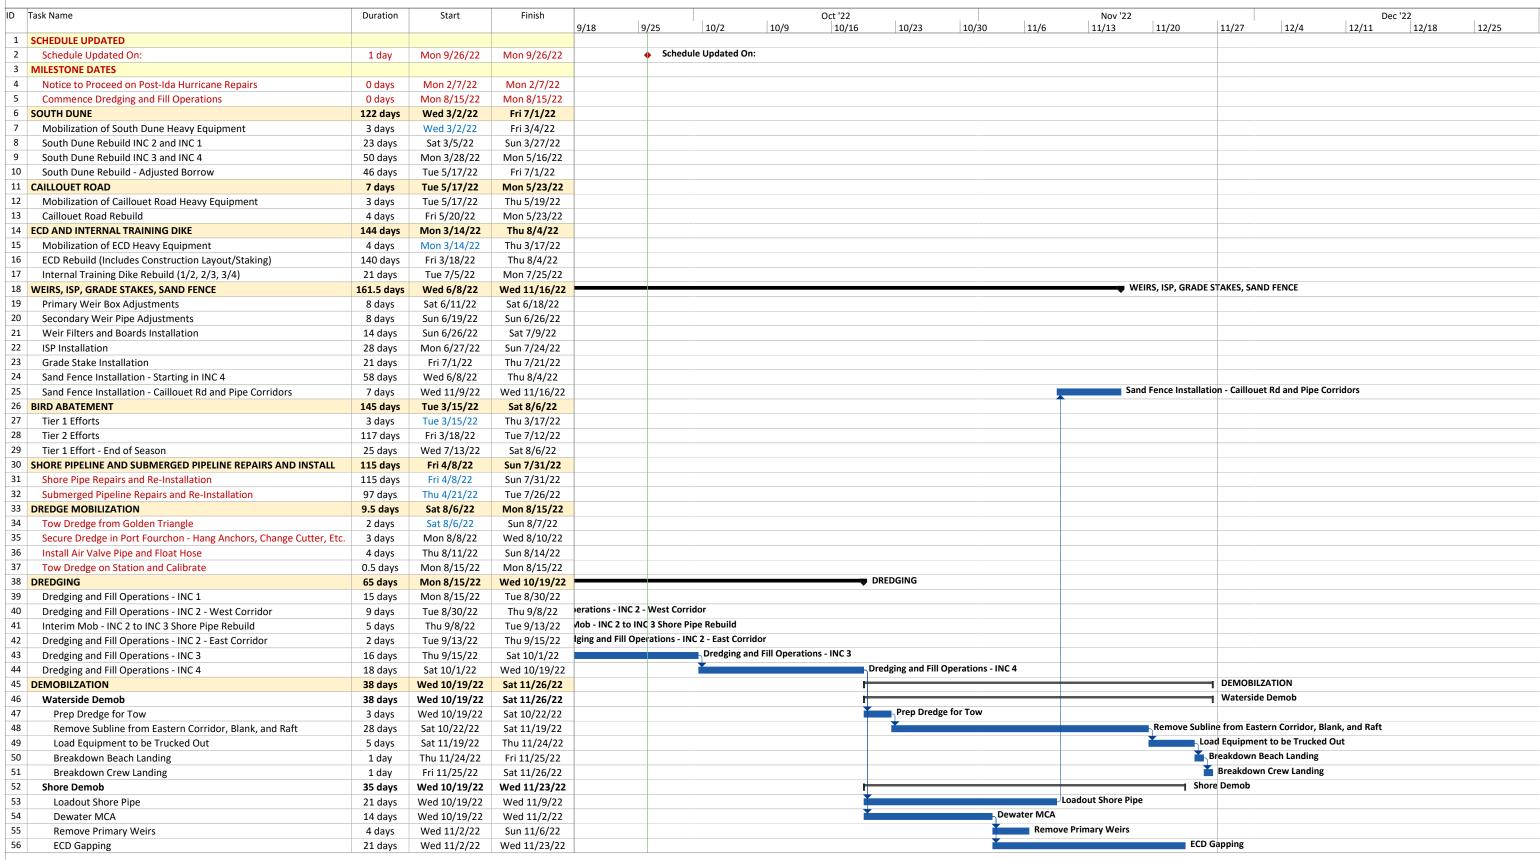




GLDD PROJ NO. 84768





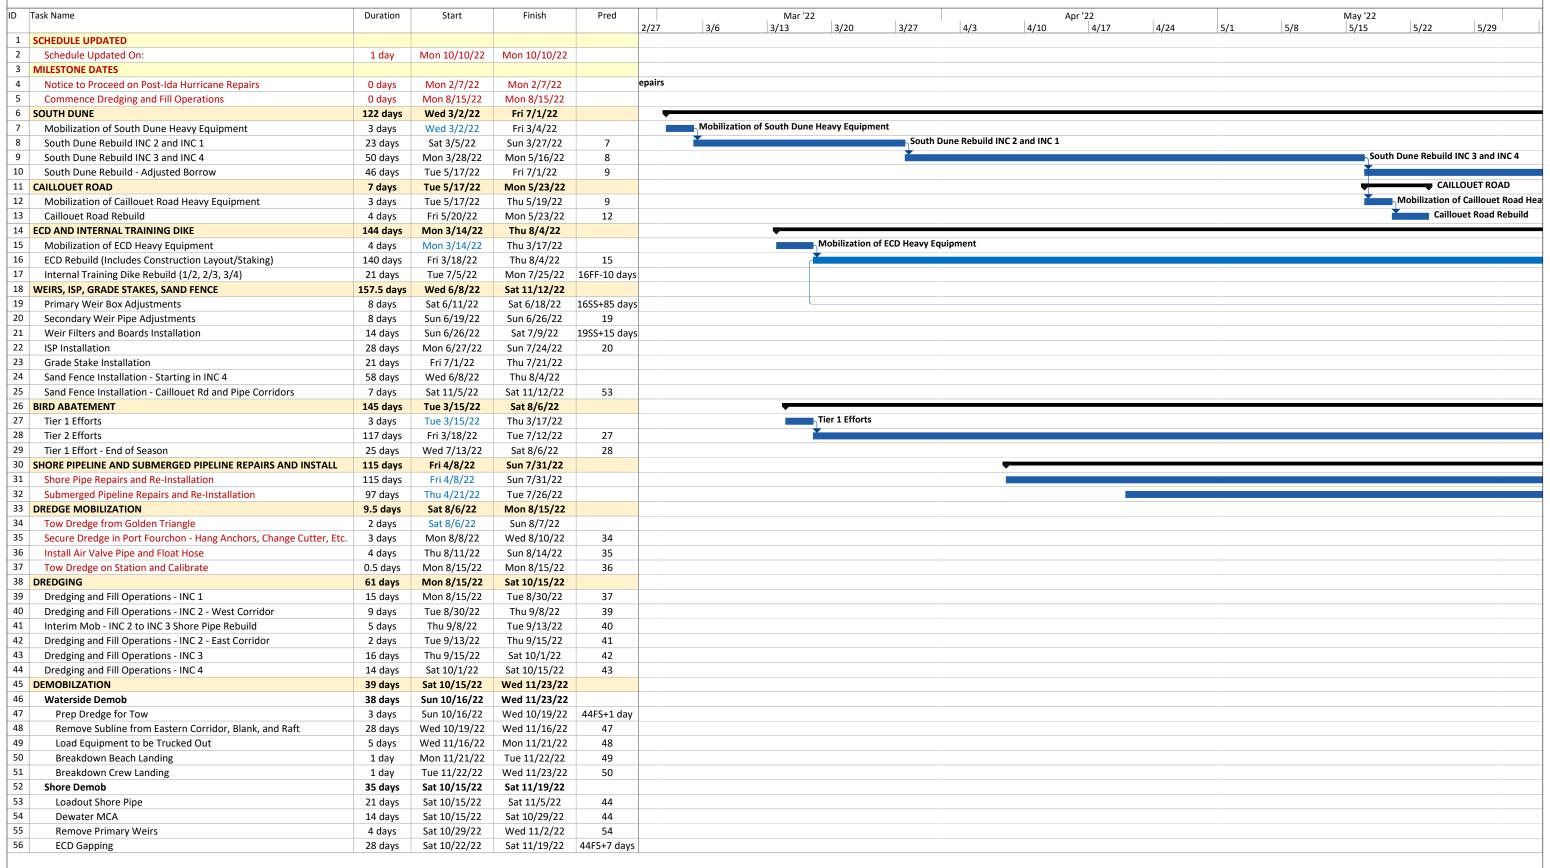




GLDD PROLNO, 84768





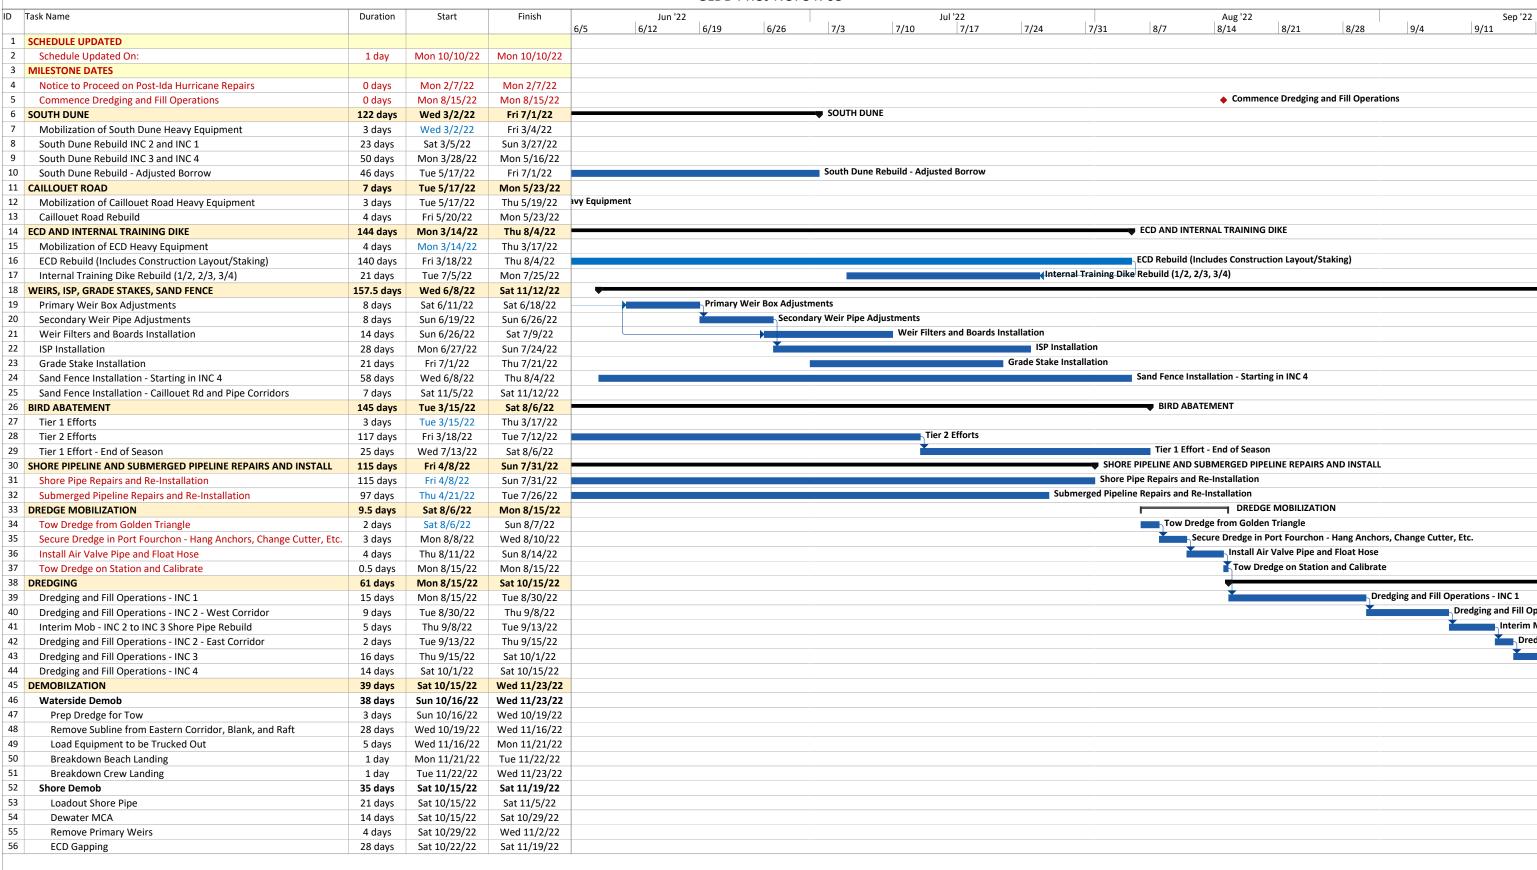




GLDD PROJ NO. 84768






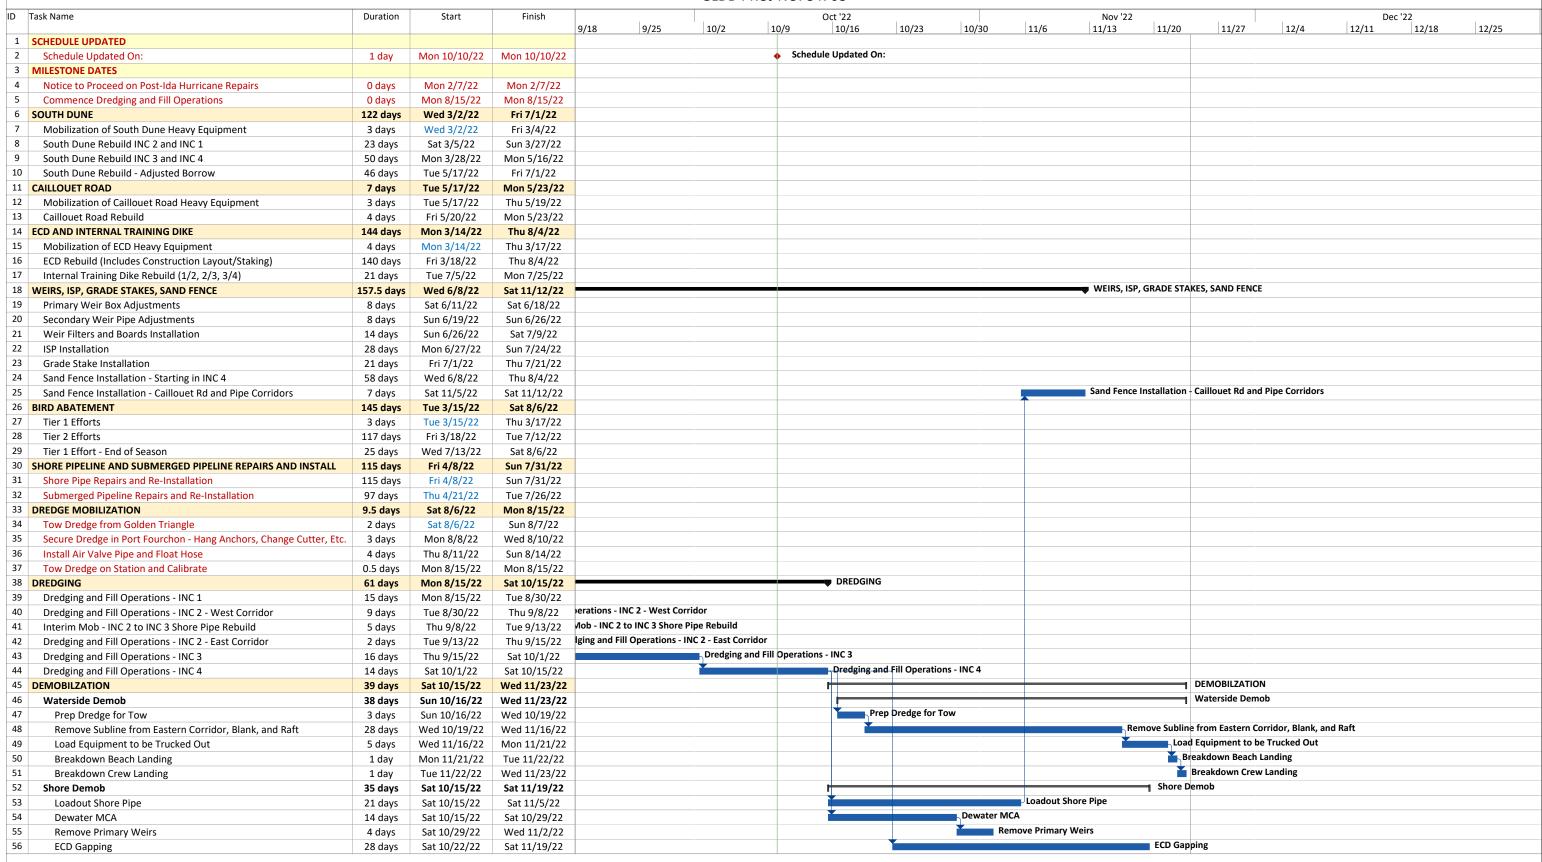







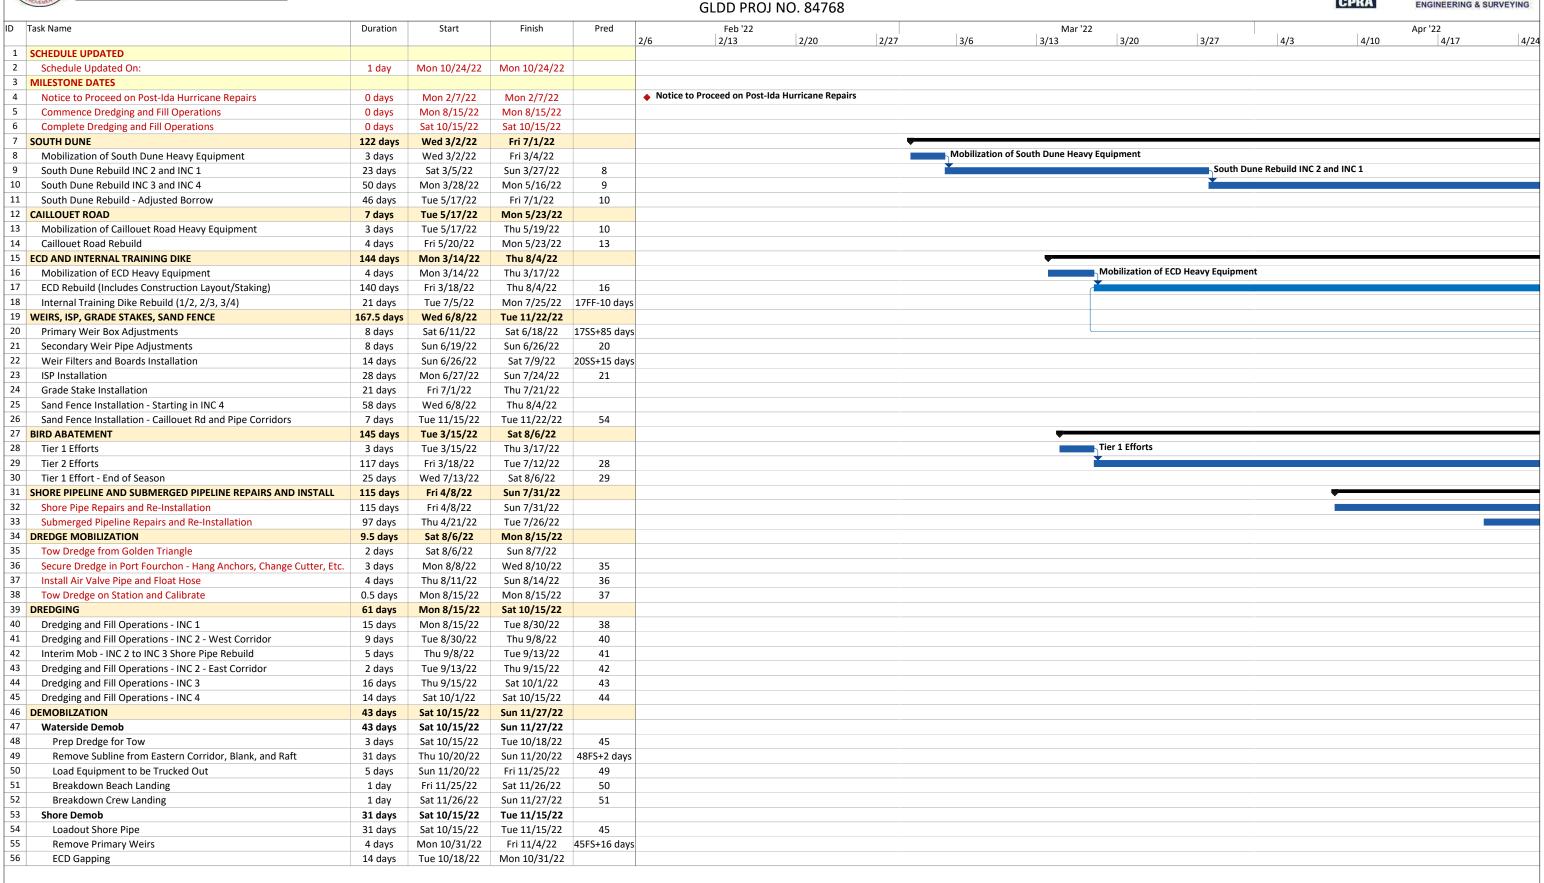




GLDD PROJ NO. 84768






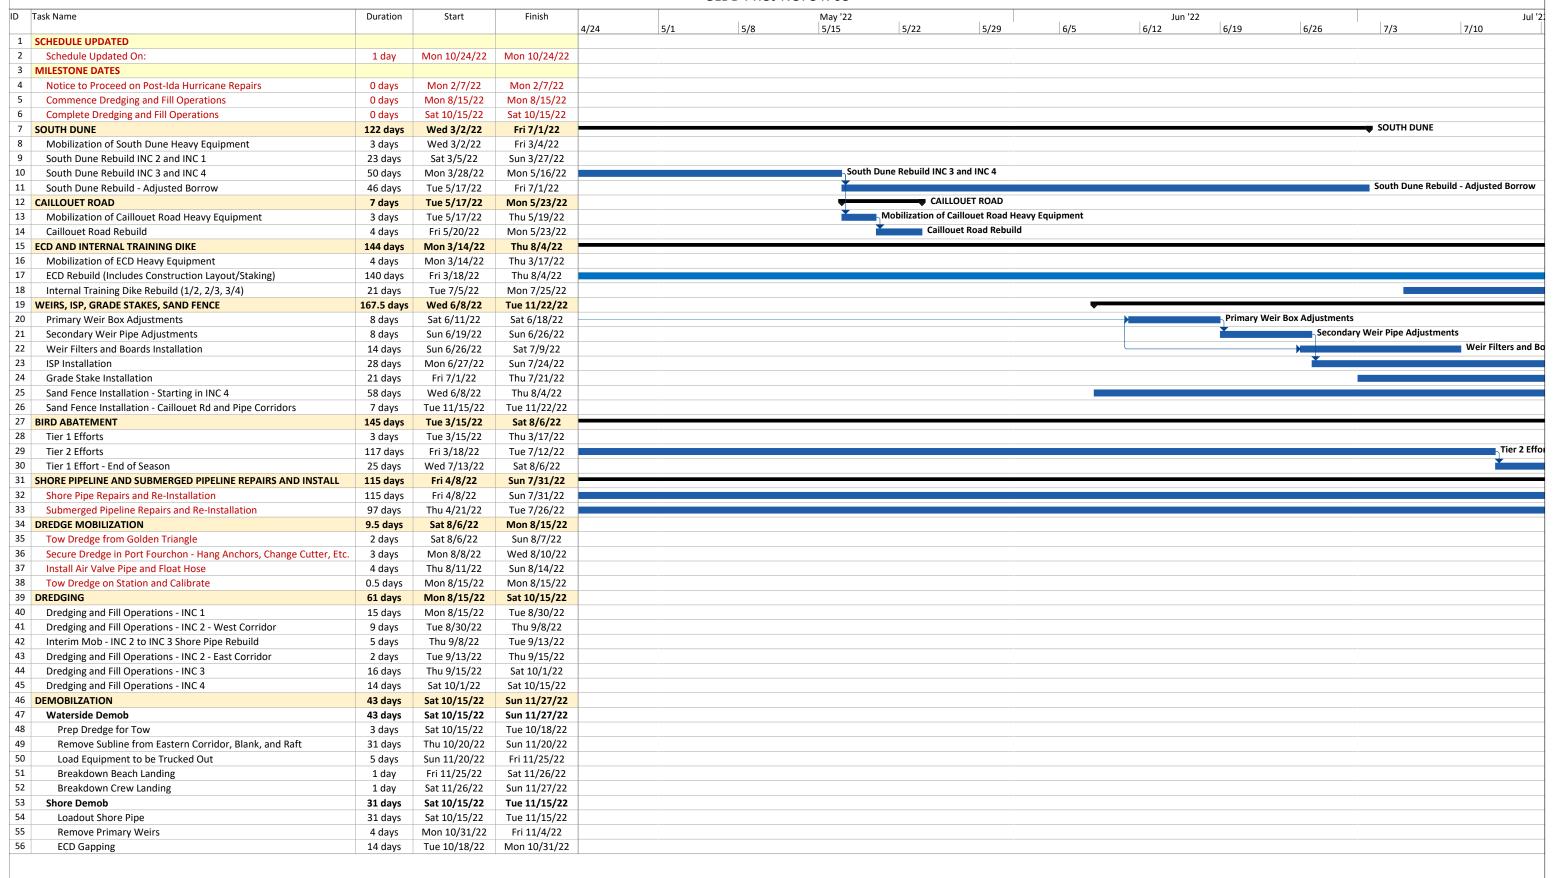







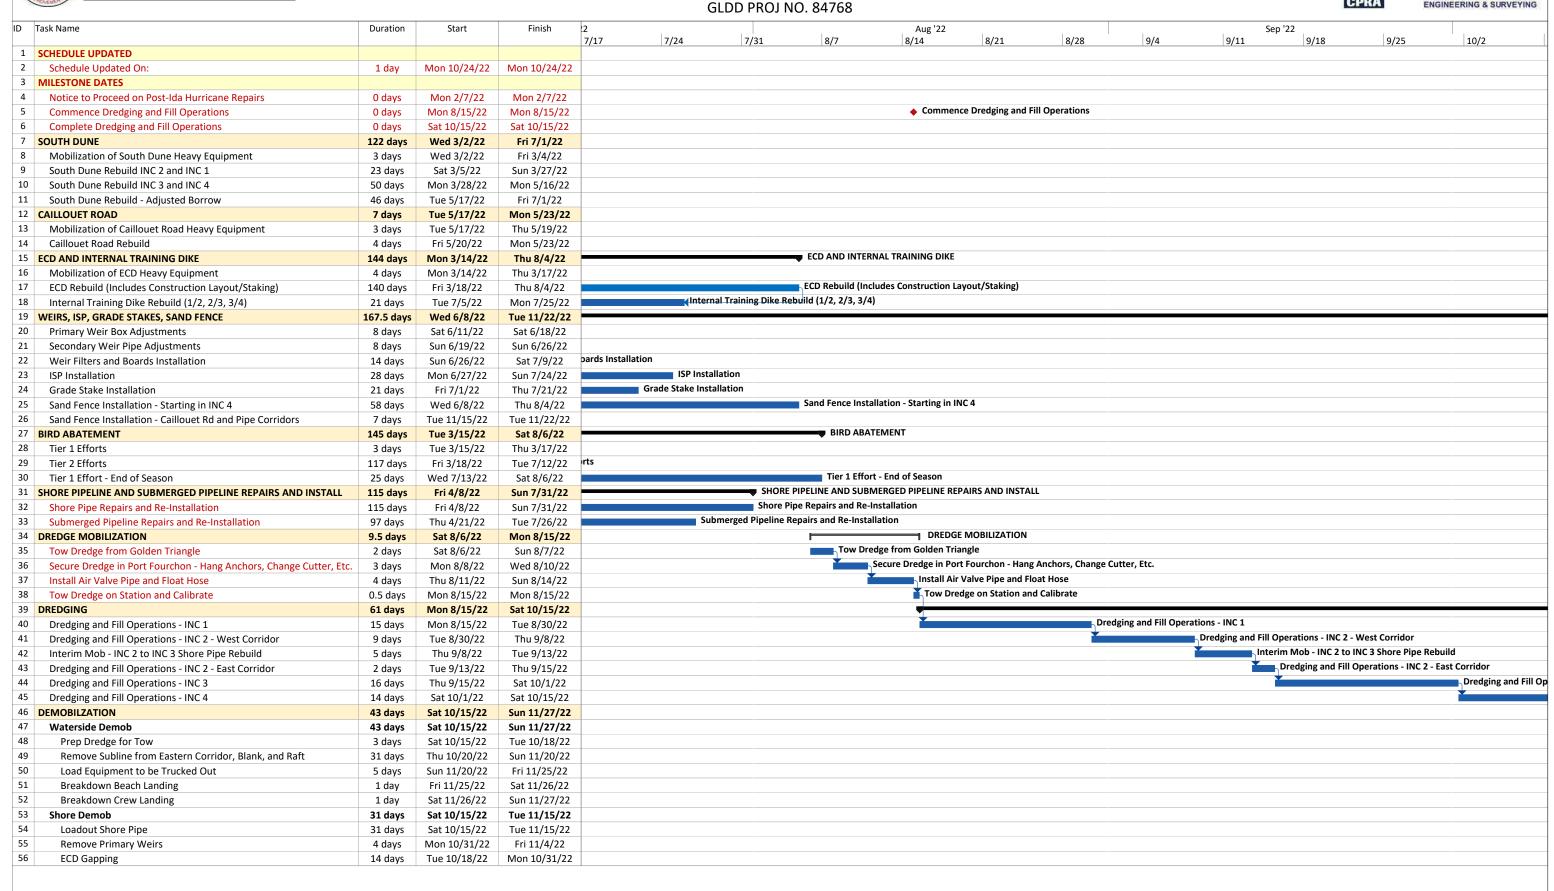



GLDD PROJ NO. 84768





