

State of Louisiana Coastal Protection and Restoration Authority

2016 Annual Inspection Report

for

Naomi Outfall Management

State Project Number BA-03c Priority Project List 5

June 9, 2016 Jefferson Parish

Prepared by:

Luke Prendergast, E.I. Coastal Protection and Restoration Authority New Orleans Regional Office CERM, Suite 309 2045 Lakeshore Drive New Orleans, LA 70122

Table of Contents

I.	Introduction	1
II.	Project Description and History	1
III.	Inspection Purpose and Procedures	3
IV.	Inspection Results	3
	Bayou Dupont Canal Weir	3
	Goose Bayou Canal Weir	4
V.	Conclusions	4
VI.	Recommendations	5
	Immediate Repairs	5
	Programmed Maintenance	5

Appendices

Appendix A	Project Features Map
Appendix B	Photographs
Appendix C	Three Year Budget Projections
Appendix D	Field Inspection Form

i

I. Introduction

The Naomi Outfall Management Project (BA-03c) is located on the west bank of the Mississippi River, south of Lafitte, Louisiana. Although the project features are located entirely in Jefferson Parish, the project outfall area encompasses 27,135 acres in Jefferson and Plaquemines Parishes. Specific project features are located on two streams – Goose Bayou Canal and Bayou Dupont – which connect the Barataria Bay Waterway to the Pen (Appendix A).

II. Project Description and History

The Naomi Siphon went into operation in February, 1993 and has delivered an average of 997 cfs of fresh river water (when operating) into the marshes and streams east of the Pen. Much of this fresh water eventually exits the project area via Goose Bayou Canal and Bayou Dupont Canal which connect the Pen with the Barataria Waterway. During periods of high tide, reverse flow occurs and high-salinity water from the Barataria Waterway enters the Pen via the two subject canals. These two canals provide an avenue for loss of fresh river water from the project area and intrusion of high-salinity water into the project area.

The present project, which consists of fixed crest weirs with boat bays, restricts the hydrologic connections between the Pen and the Barataria Waterway. This restriction is intended to hold diverted water and nutrients in the project area, while restricting the high salinity waters from the Barataria Waterway. The weirs are designed to moderate or dampen the interchange of water into and out of the Pen through Goose Bayou Canal and Bayou Dupont Canal. Thus, retention of sediment-rich fresh siphon water in the outfall area is maximized, and intrusion of high-salinity water is minimized.

Project construction began on June 1, 2002, and was completed on July 15, 2002. Project life is estimated to be 20 years. Annual project inspections are planned.

The principal project features include:

- 1. One stone weir at Goose Bayou Canal
 - a. Total length of weir = 458 ft.
 - b. Bottom width of boat bay = 30 ft.
 - c. Boat bay bottom elevation= -5 ft. (NAVD 88)
 - d. Weir crest = +1 ft. (NAVD 88)
 - e. Rock placed directly on geotextile
 - f. Rock rip rap = 3,967 tons
 - g. Geotextile = 2,851 yards
 - h. Rock conforms to Rock Type 1 of Material Specification 523 with a gradation of:

Percent Lighter Than Rock Unit Weight

100	700 lbs
50-100	300 lbs
15-50	150 lbs
0-15	45 lbs

- i. Four (4) 4-piling clusters with navigation aid lights and warning signs
- j. Six (6) single pilings with warning signs
- k. Thirty-two buoys and associated stainless steel cable

2. One stone weir at **Bayou Dupont Canal**

- a. Total length of weir = 302 ft.
- b. Bottom width of boat bay = 30 ft.
- c. Boat bay bottom elevation = -5 ft. (NAVD 88)
- d. Weir crest +1 ft. (NAVD 88)
- e. Rock placed directly on geotextile
- f. Rock rip rap = 8,505 tons
- g. Geotextile = 3,374 yards
- h. Rock conforms to Rock Type 1 of Material Specification 523 with a graduation of:

Percent Lighter Than	Rock Unit Weight
100	700 lbs
50 -100	300 lbs
15-50	150 lbs
0-15	45 lbs

- i. Four (4) 4-pile clusters with day mark navigation signs and three (3) of the piling clusters have navigation aid lights.
- j. Three (3) single pilings with warning signs (reduced from five (5) in 2006 repair project)
- k. Twenty-two warning buoys with stainless steel cable
- 1. Two (2) marker buoys with warning markings and internal radar reflectors (added during 2006 repair project in place of two (2) single pilings with warning signs).

On June 20, 2006, a contract was awarded to place two warning buoys in places where warning signs were damaged and to replace 5 navigation lights. This project was completed on October 4, 2006.

A second maintenance contract was awarded May 27, 2015 for the replacement of the barrier float buoys and navigation signs at the Goose Bayou weir. Repair work was completed August 10, 2015.

III. Inspection Purpose and Procedures

The purpose of the annual inspection of the Naomi Outfall Management Project (BA-03c) is to evaluate the constructed project features, to identify any deficiencies, and to prepare a report detailing the condition of project features and providing recommended corrective actions if needed. If corrective actions are required, CPRA shall provide in the report a detailed cost estimate for engineering, design, supervision, inspection, and construction contingencies, and an assessment of the urgency of such repairs (O&M Plan, December 24, 2002). The annual inspection report also contains a summary of maintenance projects and an estimated projected budget for the upcoming three (3) years for operation, maintenance and rehabilitation. The three (3) year projected operation and maintenance projects performed since construction of the Naomi Outfall Management Project is provided in Section II.

An inspection of the Naomi Outfall Management Project (BA-03c) was held on June 7, 2016, by Luke Prendergast and Jonathan Sherwood of CPRA, along with Quin Kinler of NRCS. Photographs of that inspection are included in Appendix B of this report.

IV. Inspection Results

BAYOU DUPONT CANAL WEIR

Rock Riprap

The structure was altered to facilitate construction of the South Shore of the Pen (BA-41) Project, and remains in this temporary condition to allow construction access for the Long Distance Sediment Pipeline (BA-43) Project. Rock has been temporarily removed from the weir and stockpiled within the footprint of the structure (Photo #1). The structure will be restored to design condition as part of the BA-43 construction contract.

<u>Pilings</u>

Two pile clusters were removed to enable construction of the BA-41, BA-43, and BA-48 projects. The remaining pilings appeared to be in good condition.

Warning Signs and Day Board Navigation Signs

Remaining signs (unaffected by construction) are in good condition.

Navigation Aid Lights

Two of the navigation aids have been removed to facilitate construction of the BA-41, BA-43, and BA-48 projects; these will be replaced at a later date. Routine navigation light maintenance is performed under a state-wide contract.

Regulatory Marker Buoys

Buoys have been temporarily relocated to enhance access for the BA-41, BA-43, and BA-48 projects.

GOOSE BAYOU CANAL WEIR

Rock Riprap

The structure has settled an average of 2 feet since construction, resulting in most of the rock being submerged below the water surface. As the weir lies within the footprint of the planned Lafitte Ring Levee, no rock maintenance is anticipated at this time.

Pilings

Timber pilings appeared to be in good condition. Reflective tape was replaced as part of the 2015 maintenance event (Photo #2).

Warning Signs and Day Board Navigation Signs

Navigation markers and barrier float cable assemblies were replaced in 2015. Warning signs were in good condition (Photo #2).

Navigation Aid Lights

No defects were observed with the navigation aid lights. Maintenance of these lights is covered under a separate state-wide contract.

V. Conclusions

Overall, the Naomi Outfall Management project is functioning properly and is in good condition. The Bayou Dupont structure remains in an altered condition to allow construction and maintenance access for nearby CWPPRA projects.

VI. Recommendations

Inspection and assessment of project features should continue on an annual basis.

Immediate Repairs


• None at this time.

Programmed Maintenance

• Navigation lights are inspected and maintained under state-wide contract.

Appendix A

Project Features Map

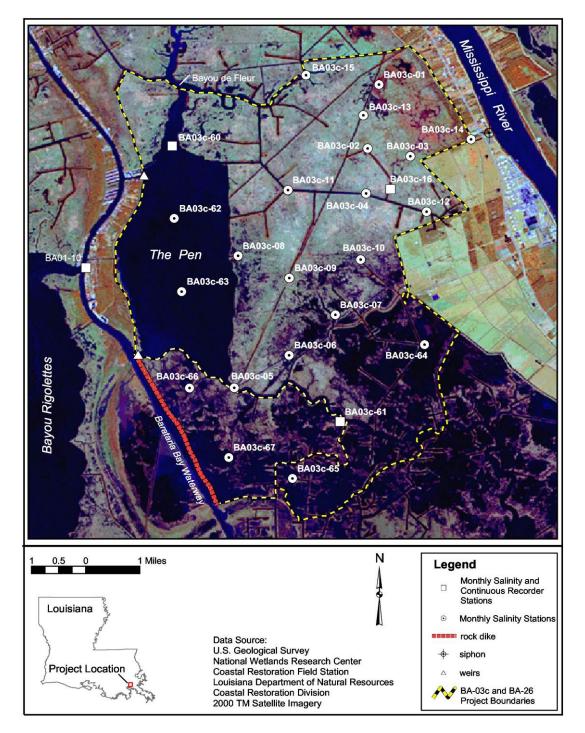

Appendix B

Photographs



Photo #1 – Riprap stockpile for weir restoration (Bayou Dupont)



Photo #2 – New navigation markers (Goose Bayou)



Photo #3 – New barrier floats and cables (Goose Bayou)



Photo #4 – New reflective tape on piles (Goose Bayou)

Appendix C

Three Year Budget Projection

Naomi Outfall Management Project (BA-03c)

Federal Sponsor: NRCS Construction Completed : 8/2002 PPL 5

Current Approved O&M Budget	Year 0	Year - 1	Year -2	Year -3	Year -4	Year -5	Year -6	Year -7	Year -8	Year -9	Year -10	Year -11	Year -12	Year -13	Year -14	Year -15	Year -16	Year - 17	Year -18	Year -19	Project Life
June 2009	FY03	FY04	FY05	FY06	FY07	FY08	FY09	FY10	FY11	FY12	FY13	FY14	FY15	FY16	FY17	FY18	FY19	FY20	FY21	FY22	Budget
State O&M																					\$488,980
Corps Admin																					\$0
Federal S&A																					\$0
Total																					\$488,980

Projected O&M Expenditures							Remaining Project Life
Maintenance Inspection	\$3,899	\$4,000	\$4,104	\$4,211	\$4,320	\$4,432	\$24,966
General Maintenance							\$0
Surveys							\$0
Navigation Aid Maintenance	\$16,738	\$17,173	\$17,619	\$18,077	\$18,547	\$19,030	\$107,184
Federal S&A							\$0
Maintenance/Rehabilitation							\$0
E&D							\$0
Construction							\$0
Construction Oversight							\$0
Total	\$20,636	\$21,173	\$21,723	\$22,288	\$22,867	\$23,462	\$132,149

O&M Expenditures from COE Lana Report	\$264,026	Current O&M Budget	\$488,980	Current Project Life Budget	\$488,980
State O&M Expenditures not submitted for in-kind credit	\$64,897 estimated	Less Expenditures	\$352,414	Total Projected Project Life Budget	\$484,563
Federal Sponsor MIPRs (if applicable)	\$23,491	Remaining Available O&M Budget	\$136,566	Project Life Budget Surplus (Shortfall)	\$4,417
Total Estimated O&M Expenditures (as of June 2016)	\$352,414				

Appendix D

Field Inspection Form

FIELD INSPECTION CHECK SHEET

Project No. / Name: Naomi Outfall Management		Date of Inspection:		_	Time:	12:10 PM		
Structure No.	Bayou Dupont Canal	Inspector(s):		Prend	dergast, Kinler, Sherwoo	od		
Structure Description:	Stone Weir	Water Level:	Inside:	N/A	Outside:	1.90'		
Type of Inspection:	Annual	Weather Conditions:	Weather Conditions:		Mostly sunny, light wind			

Item	Condition	Physical Damage	Corrosion	Photo #	Observations and Remarks
Rock Riprap	See Remarks	See Remarks	N/A	#1	Structure altered to allow construction equipment access to adjacent CWPPRA projects. Weir and signage to be restored to design condition following completion of BA-43 project.
Creosote Piling	See Remarks	See Remarks	None	#1	See above.
Warning Signs and Day Board Navigation Signs	See Remarks	See Remarks	None	#1	See above.
Navigation Aid Lights	See Remarks	See Remarks	None	#1	See above.
Warning Buoys	See Remarks	See Remarks	None	#1	See above.

Warning Buoys

Good

None

FIELD INSPECTION CHECK SHEET

Project No. / Name:	Naomi Outfall Management		_		Date of Inspection:	6/7/201	16	Time:	11:15 AM												
Structure No.	Structure No. Goose Bayou Canal		Goose Bayou Canal		Goose Bayou Canal		Goose Bayou Canal		Goose Bayou Canal		Goose Bayou Canal		Goose Bayou Canal		_		Inspector(s):		Prende	rgast, Kinler, Sherwoo	od
Structure Description:	ucture Description: Stone Weir		_		Water Level:	Inside:	N/A	Outside:	1.90'												
Type of Inspection:		Annual	_		Weather Conditions: Mos			Mostly sunny, light wi	ind												
ltem	Condition	Physical Damage	Corrosion	Photo #		Obr	ervations an	d Pomarks													
nem	Condition	Physical Damage	Corrosion	FIIOLO #	+	Obs	ervations an														
Rock Riprap	Good	None	N/A		Most of rock structure was below water surface elevation.																
Creosote Piling	Good	None	N/A	#2, 3, 4	No defects noted.																
Warning Signs and					1																
Day Board	Good	None	None	#2, 3, 4	No defects noted.																
-	0000	None	None	<i>π2</i> , 3, 4																	
Navigation Signs																					
Navigation Aid					No defecto notor	d Maintana	noo of novinati	on lighto in covered .	under etete wide												
Lights	Good	None	None	#2	No defects noted. Maintenance of navigation lights is covered unde contract.				nder state-wide												

#2, 3, 4

None

No defects noted.
