



State of Louisiana

**Coastal Protection and Restoration
Authority of Louisiana (CPRA)**

**2012/2013 Annual Inspection
Report**

For

**PECAN ISLAND TERRACING
PROJECT
(ME-14)**

State Project Number ME-14
Priority Project List 7

April 17, 2013
Vermilion Parish

Prepared by:

Mel Guidry, ME-14 O&M Manager
CPRA
Lafayette Field Office
635 Cajundome Blvd.
Lafayette, LA 70596



Table of Contents

I. Introduction.....	1
II. Inspection Purpose and Procedures.....	1
III. Project Description and History.....	2
IV. Summary of Past Operation and Maintenance Projects.....	3
V. Inspection Results	3
VI Conclusions and Recommendations	3

Appendices

- Appendix A Project Features Map
- Appendix B Photographs
- Appendix C Three Year Budget Projections
- Appendix D Field Inspection Notes

I. Introduction

The Pecan Island Terracing (ME-14) project is located five miles north of the Gulf of Mexico just south of Pecan Island and Hwy 82 in the Lakes Sub-basin of the Mermentau Basin, Vermilion Parish, Louisiana. The total project area comprises 3,753 acres (1,519 ha) of brackish marsh and open water. Area 1 is primarily open water and was formerly pasture land of approximately 1,938 acres (784 ha). Area 2 consists of 1,715 acres (694 ha) of brackish marsh and open water.

The project features include construction of 197,000 linear feet (60,046 m) of terraces in 500 ft (152.4 m) sections with a 50 ft (15.24 m) break between each terrace, creating approximately 344 terraces. Terraces run east to west in a staggered gap formation. The terraces were constructed by depositing borrow material with a 40 ft (12.19 m) berm for a terrace with 4:1 side slopes and a top width of 10 ft (3.04 m). Initial constructed elevation was approximately 3.75 ft (1.14 m) NAVD 88 which in 5 years should have a final settled elevation approximately 1 ft above marsh elevation. The dredged material was deposited such that the terrace's side slopes were 4:1 to conform to the natural angle of repose for the bottom soil. Breaks were constructed to permit water to move in and out of the interior, which may facilitate the settling of suspended soil particles. *Spartina alterniflora* (smooth cordgrass) plugs were planted every five linear feet on both sides of terrace.

The Pecan Island Terracing Project was authorized by Section 303(a) of Title III Public Law 101-646, the Coastal Wetlands Planning Protection and Restoration Act (CWPPRA) enacted on November 29, 1990 as amended and approved on the seventh Priority Project List. The Pecan Island Terracing Project has a twenty-year (20 year) economic life, which began in September 2003.

II. Inspection Purpose and Procedures

The purpose of the annual inspection of the Pecan Island Terracing Project (ME-14) is to evaluate the constructed project features, identify any deficiencies and prepare a report detailing the condition of project features and recommended corrective actions needed. Should it be determined that corrective actions are needed, CPRA shall provide, in the report, a detailed cost estimate for engineering, design, supervision, inspection, and construction contingencies, and an assessment of the urgency of such repairs (O&M Plan, 2003). The annual inspection report also contains a summary of maintenance projects, if any, which were completed since completion of constructed project features and an estimated projected budget for the upcoming three (3) years for operation, maintenance and rehabilitation. The three (3) year projected operation and maintenance budget is shown in Appendix C.

An inspection of the Pecan Island Terracing Project (ME-14) was held on April 17, 2013 under partly sunny skies and mild temperatures. In attendance were Mel Guidry and Stan Aucoin of CPRA with John Foret representing NOAA/NMFS. All parties met at the CPRA Lafayette Field Office and proceeded to the boat launch on Hwy 82 adjacent to the Pecan

Island Terracing Project (ME-14). The group traveled throughout the project area via NOAA/NMFS's boat inspecting the terraces.

The field inspection included a complete visual inspection of the earthen terraces. Staff gauge readings were used to determine approximate water level and earthen terrace elevation. Photographs were taken of various earthen terraces (see Appendix B) and Field Inspection notes were completed in the field to record measurements and any notable deficiencies (see Appendix D).

III. Project Description and History

The Pecan Island Terracing Project area was originally marshland that was transformed into dry pasture land in the mid 1950's by constructing continuous dikes and pumping out the water. Deterioration and loss of the perimeter levees in recent years has converted the entire area into a shallow, open water lake with a few small marsh islands. The project will convert areas of open water back to vegetated marsh through the construction of earthen terraces, which were completed in August, 2003. The terrace construction will include breaks between the terraces to facilitate sediment settling. Submerged aquatic vegetation growth will be promoted in the terrace area due to reduced turbidity and wave action. Vegetative plantings were completed in September, 2003.

The principal project features include:

1. 196,800 Linear Feet of Earthen Terraces
2. Smooth Cordgrass Plantings on Earthen Terraces

The following goals will contribute to the evaluation of the above objective:

1. Increase land to water ratios by constructing approximately 100 acres (41.3 ha) of earthen terraces in Area 1.
2. Increase land to water ratios by creating over 300 acres (121.4 ha) of land within Areas 1 and 2 over 20 years after construction.
3. Increase percent cover of SAV in remaining open water areas to 50% in Area 1 and 15% in Area 2.
4. Establish emergent vegetated marsh on planted terraces.

IV. Summary of Past Operation and Maintenance Projects

General Maintenance: Below is a summary of completed maintenance projects and operation tasks performed since September 2003, the construction completion date of the Pecan Island Terracing Project (ME-14).

December 2011 - Installation of two staff gauges.

1 – N 29° 38' 49.48", W 92° 30' 30.62"

2 – N 29° 38' 31.16", W 92° 27' 27.48"

Structure Operations:

There are no active operations associated with this project.

V. Inspection Results

Terraces

The majority of the earthen terraces are in good condition. There is some erosion taking place on the north side of the individual terraces. Previously noted erosion on the southernmost sacrificial terraces has worsened. On the west side of the terrace field, the first two rows of the southernmost sacrificial terraces are no longer visible above the water surface. The third row is also beginning to show signs of degradation. In addition, a portion of the first row of the east southernmost terraces is no longer visible above the water surface. (Photos: Appendix B, Photo 1)

Vegetative Plantings


The tops of the terraces are covered with vegetation. Species noted include *Spartina alterniflora*, *Baccharis*, and *Spartina patens*. (Photos: Appendix B, Photo 2)

VI. Conclusions and Recommendations

Overall, the Pecan Island Terracing Project (ME-14) is functioning as designed and in good condition. The erosion of the southern sacrificial terraces will continue to be monitored. NOAA and CPRA have agreed to investigate land rights and possible erosion solutions for these sacrificial terraces. If feasible, an additional request for funding will be needed for this maintenance event.

Annual Inspection Report
PECAN ISLAND TERRACING PROJECT
State Project No. ME-14

Appendix A
Project Features Map

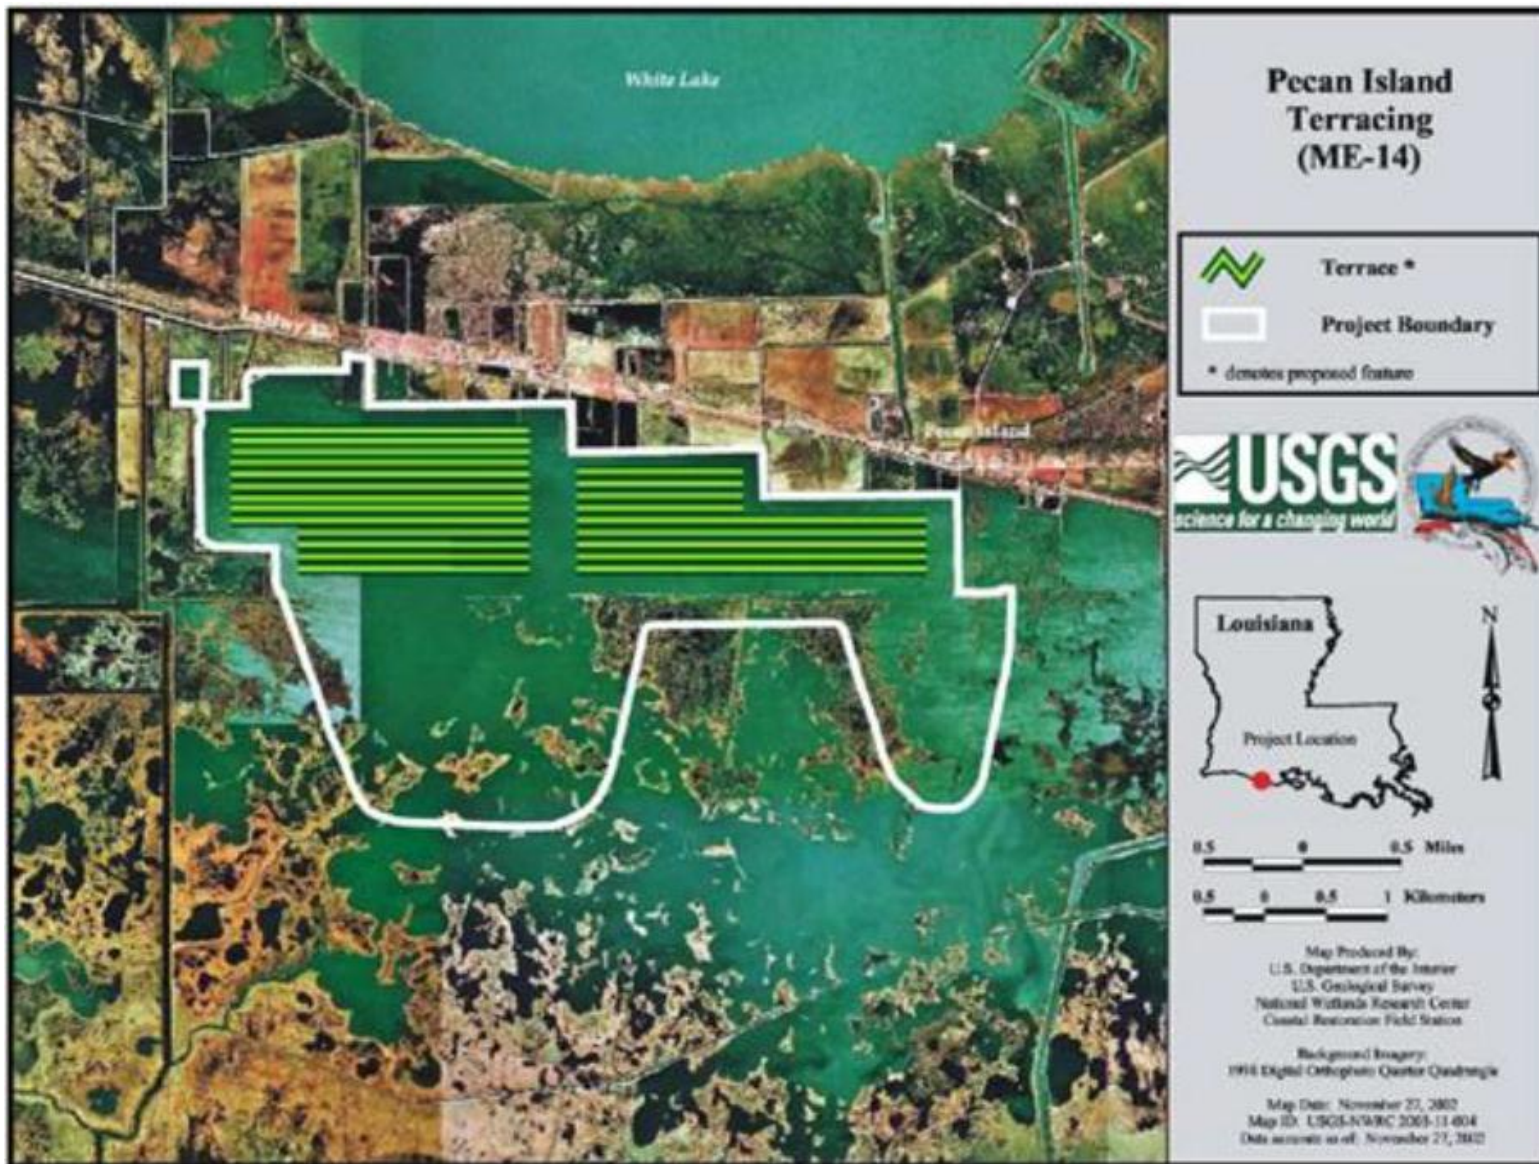

Appendix B

Photographs



Photo No. 1, Southern Earthen Terraces



Photo No. 2, Typical Terrace

Appendix C

Three Year Budget Projection

PECAN ISLAND TERRACING/ ME-14 / PPL 7
Three-Year Operations & Maintenance Budgets 07/01/2013 - 06/30/2016

Project Manager <i>Pat Landry</i>	O & M Manager <i>Mel Guidry</i>	Federal Sponsor <i>NMFS</i>	Prepared By <i>Mel Guidry</i>
--------------------------------------	------------------------------------	--------------------------------	----------------------------------

	2013/2014 (-10)	2014/2015 (-11)	2015/2016 (-12)
Maintenance Inspection	\$ 6,457.00	\$ 6,651.00	\$ 6,851.00
Structure Operation			
State Administration		\$ -	\$ -
Federal Administration		\$ -	\$ -

Maintenance/Rehabilitation

13/14 Description:

E&D	
Construction	
Construction Oversight	
Sub Total - Maint. And Rehab.	\$ -

14/15 Description:

E&D	\$ -
Construction	\$ -
Construction Oversight	\$ -
Sub Total - Maint. And Rehab.	\$ -

15/16 Description:

E&D	\$ -
Construction	\$ -
Construction Oversight	\$ -
Sub Total - Maint. And Rehab.	\$ -

	2013/2014 (-10)	2014/2015 (-11)	2015/2016 (-12)
Total O&M Budgets	\$ 6,457.00	\$ 6,651.00	\$ 6,851.00

O & M Budget (3 yr Total)	\$ 19,959.00
Unexpended O & M Budget	\$ 179,460.00
Remaining O & M Budget (Projected)	\$ 159,501.00

Appendix D

Field Inspection Form

Annual Inspection Report
 PECAN ISLAND TERRACING PROJECT
 State Project No. ME-14

MAINTENANCE INSPECTION REPORT CHECK SHEET

Project No. / Name: Pecan Island Terracing ME-14

Date of Inspection: April 17, 2013 Time: 11:00 am

Structure No.

Inspector(s): Mel Guidry & Stan Aucoin (CPRA)
 John Foret (NMFS)

Structure Description: Earthen Terraces

Water Level @ PVC Wall: 1.3ft

Type of Inspection: Annual

Weather Conditions: Partly Sunny and Mild

Item	Condition	Physical Damage	Corrosion	Photo #	Observations and Remarks
Steel Bulkhead / Caps	N/A				
Steel Grating	N/A				
Stop Logs	N/A				
Hardware	N/A				
Timber Piles	N/A				
Timber Wales	N/A				
Galv. Pile Caps	N/A				
Vegetation	Good				Good coverage of <i>Spartina alterniflora</i> , <i>Spartina patens</i> , <i>Baccharis</i> . A few spots of Roseau Cane.
Signage / Supports	N/A				
Rip Rap (fill)	N/A				
Earthen Terraces	Good			1,2	Two rows on west southernmost field of terraces are eroded below water surface. Portion of first row on east southernmost field of terraces is eroded below water surface. Generally there is good vegetation on the terraces. The northern side of each individual terrace is experiencing some erosion.

What are the conditions of the existing levees?
 Are there any noticeable breaches?
 Settlement of rock plugs and rock weirs?
 Position of stoplogs at the time of the inspection?
 Are there any signs of vandalism?
