



**State of Louisiana  
Coastal Protection and Restoration Authority**

**2020 Annual Inspection Report**

for

**Goose Point / Point Platte Marsh  
Creation Project**

State Project Number PO-33  
Priority Project List PPL-13

December 2021  
St. Tammany Parish

Prepared by:

Taylor M. Daigle, P.E.  
Coastal Protection and Restoration Authority  
New Orleans Field Office  
CERM, Suite 309  
2045 Lakeshore Drive  
New Orleans, LA 70122



**2020 Annual Inspection Report  
for  
Goose Point / Point Platte Marsh Creation Project  
(PO-33)**

**Table of Contents**

I. Introduction.....	1
II. Inspection Purpose and Procedures .....	1
III. Project Description and History.....	1
IV. Summary of Past Operations and Maintenance Projects .....	2
V. Inspection Results .....	3
VI. Conclusions and Recommendations.....	3
VII. References.....	3

**Appendices**

- Appendix A Project Features Map
- Appendix B Photographs
- Appendix C Three Year Operations & Maintenance Budget
- Appendix D Field Inspection Form



## **I. Introduction**

The Goose Point / Point Platte Marsh Creation Project (State Project No. PO-33) was approved on the 13<sup>th</sup> Priority Project List.

The PO-33 project is located on the north shore of Lake Pontchartrain in St. Tammany Parish, within the Big Branch Marsh National Wildlife Refuge. Two marsh creation cells (A & B) are located at Goose Point, and the other three cells (C, D, & E) were built east of Point Platte. The marsh creation cells were constructed using sediment hydraulically dredged from Lake Pontchartrain. All necessary agreements to allow project construction and operation have been executed between the Louisiana Coastal Protection and Restoration Authority (CPRA) and the U.S. Fish and Wildlife Service (USFWS).

A site map showing the project boundaries is included in Appendix A.

## **II. Inspection Purpose and Procedures**

The purpose of the annual inspection of PO-33 is to evaluate the constructed project features to identify any deficiencies and to prepare a report detailing the condition of project features and recommending corrective actions needed. Should it be determined that corrective actions are needed, CPRA shall provide a detailed cost estimate for engineering, design, supervision, inspection, and construction contingencies, and an assessment of the urgency of such repairs. The annual inspection report also contains a summary of maintenance projects (See Section IV) and an estimated budget (See Appendix C) for the upcoming three (3) years for operation, maintenance and rehabilitation.

Due to the COVID 19 pandemic, the project manager from USFWS, the federal sponsor, was unable to travel to the project site for the purposes of the 2020 annual inspection. The project team decided that the site visit conducted on November 5, 2020 will be used as the annual inspection. Weather on November 5<sup>th</sup> consisted of mostly cloudy skies and a temperature of approximately 70° F. All five marsh creation cells were visited. Taking part in the inspection were Taylor Daigle of CPRA, the non-federal sponsor, and representatives from Providence Engineering and Environmental Group, LLC and Marsh Buggies, Inc. who were working on a tidal features maintenance project as described in Section IV below at the time of the inspection. As per the gage installed by the maintenance event contractor, the water level on the morning of the inspection was +0.83' NAVD 88 but appeared to have risen to approximately +1.1' NAVD 88 at the time of the afternoon inspection. Photographs of the inspection are included in Appendix B of this report. It should be noted that the aforementioned construction was ongoing at the time of this inspection, and some tidal features were reworked after this inspection.

## **III. Project Description and History**

There has been a long history of wetland loss in the project area. Interior ponding, and to a lesser extent shoreline erosion, are the major causes of this wetland loss. Interior marsh



loss rates for the Goose Point and Point Platte area were highest during the period from 1956 to 1978 and are estimated to be 31.3 acres/year and 10.42 acres/year, respectively during that period (McCarty 2001). Those high loss rates are associated with hydrologic alterations (construction of Lake Road and two large pipeline canals) which allowed saltwater to penetrate the fresher sawgrass marshes. During the transition to a more brackish marsh hay cordgrass (*Spartina patens*) community, large ponds were formed (McCarty 2001). An extensive seismic survey and the associated marsh buggy traffic conducted in the early 1970's may have worsened the condition of the already stressed marsh (McCarty 2001). The more current loss rates for those same areas from 1978 to 1995 are estimated by McCarty to be 6.42 acres/year and 5.54 acres/year, respectively.

The goal for this project was to recreate marsh habitat in open water behind the existing shoreline. The principal project features as constructed include 620 linear feet of composite sheet pile along the lake rim at Cells D and E, 49,557 linear feet of earthen perimeter containment dikes, 417 acres of marsh creation, and 195 acres of marsh nourishment among five (5) marsh creation cells as distributed below:

**Cell A** – approximately 479,903 cubic yards of dredge material was placed in Cell A creating approximately 64 acres of new marsh and some 23 acres of marsh nourishment.

**Cell B** – approximately 949,700 cubic yards of dredge material was placed in Cell B creating approximately 125 acres of new marsh and some 77 acres of marsh nourishment.

**Cell C** – approximately 863,176 cubic yards of dredge material was placed in Cell C creating approximately 120 acres of new marsh and some 49 acres of marsh nourishment.

**Cell D** – approximately 149,370 cubic yards of dredge material was placed in Cell D creating approximately 13 acres of new marsh and approximately 6 acres of marsh nourishment.

**Cell E** – approximately 658,770 cubic yards of dredge material was placed in Cell E creating approximately 95 acres of new marsh and approximately 40 acres of marsh nourishment.

The project was accepted on February 12, 2009.

Annual project inspections are included in the O&M Plan, but the project team has jointly decided to conduct biannual inspections for this project. The Project has a 20 year economic life, which began at completion of construction in 2009.

#### **IV. Summary of Past Operations and Maintenance Projects**

There are no operable structures in the project.

A marsh grass planting project was completed in the shallow open-water areas in Cells A, B, C, and E. This effort was completed in early 2014 at a cost of \$194,778.50. Several additional volunteer-led plantings have been completed by USFWS in the project area.



In 2020, the Tidal Features Maintenance Project was completed to re-establish hydraulic connections and water flow. This involved the construction of 4,923 linear feet of tidal creeks and the installation of 13 dike gaps for a total cost of \$153,746.78. The tidal features maintenance project was accepted on February 9, 2021.

## **V. Inspection Results**

The marsh creation areas generally appear to be in a good condition. The marsh appears to be healthy, and the recently constructed creeks and gaps will further help marsh health by creating hydraulic connections to areas that were previously impounded. See the description of the existing condition of each of the project features on the Field Inspection Form (Appendix D).

## **VI. Conclusions and Recommendations**

### **Project Condition**

CPRA concludes that the Goose Point / Point Platte Marsh Creation Project (PO-33) is achieving the project objective to create and nourish marsh.

### **Immediate Repairs**

No maintenance is recommended at this time.

### **Programmed Maintenance**

Continue to inspect the project features biannually to document and assess site conditions.

## **VII. References**

McCarty, P. V. 2001. The Genesis of the Big Branch Coastal Wetlands: The Geologic and Geomorphic Evolution of the Bayou LaCombe Area, Late Pleistocene to the Present. Master's Thesis, Department of Geology, University of New Orleans. New Orleans, Louisiana.



**Appendix A**  
**Project Features Map**



**Goose Point / Point Platte Marsh Creation (PO-33)**



Scale  
1:46,000

Imagery: 2012 CIR DOQQ  
Map produced August 2014  
CPRA, New Orleans Regional Office

Legend	
	PO-33 Project Boundary
	PO-33 Marsh Creation Units
	CRMS_Sites

**Appendix B**  
**Photographs**



**Photo 1: Cell A**  
Recently constructed northern gap



**Photo 2: Cell A**  
Recently constructed northern creek, facing the eastern containment dike. This area is lower than the surrounding marsh.



**Photo 3: Cell A**  
Recently constructed southern gap



**Photo 4: Cell A**  
Recently constructed southern creek



**Photo 5: Cell B**  
Recently constructed northwestern gap



**Photo 6: Cell B**  
Recently constructed north/middle gap



11/5/20, 2:37 PM  
N 30° 16' 3", W 89° 58' 27"  
Lacombe LA 70445  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 7: Cell B**

Northeastern gap – Contractor was working on this gap at the time of the inspection.



11/5/20, 2:36 PM  
N 30° 16' 1", W 89° 58' 35"  
Lacombe LA 70445  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 8: Cell B**

Recently constructed northern creek



**Photo 9: Cell B**  
Recently constructed southeastern gap




**Photo 10: Cell B**  
Recently constructed southern creek



**Photo 11: Cell B**  
Recently constructed southwestern gap



**Photo 12: Cell C**  
Recently constructed western gap

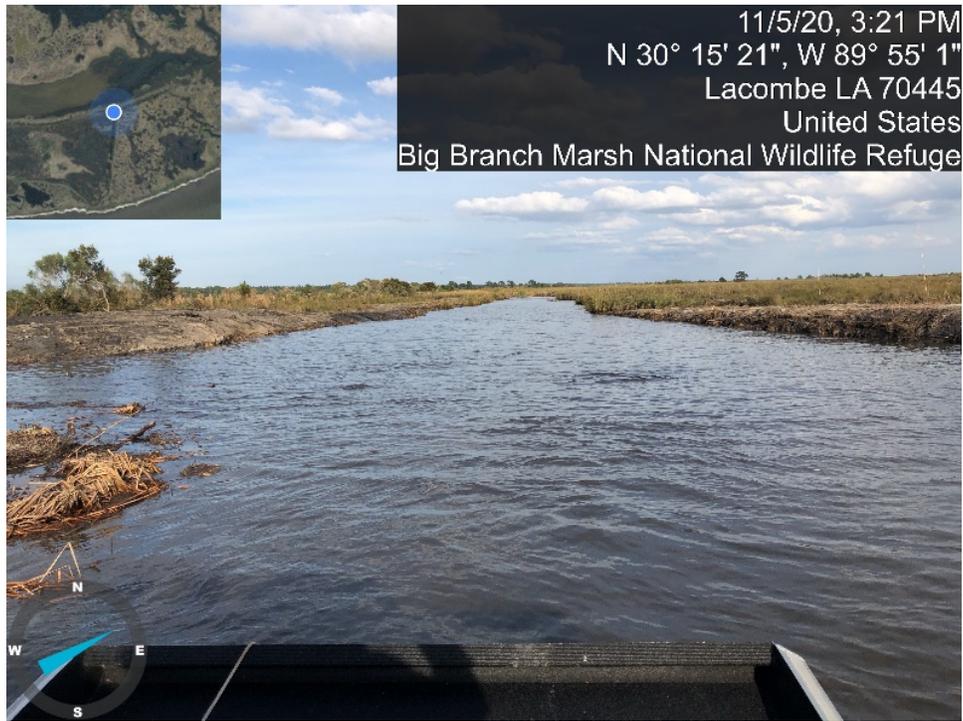

**Photo 13: Cell C**  
Recently constructed eastern gap looking into creek



**Photo 14: Cell C**  
Recently constructed creek



**Photo 15: Cell D**  
Recently constructed gap



**Photo 16: Cell D**  
Recently constructed creek



11/5/20, 3:37 PM  
N 30° 15' 41", W 89° 54' 17"  
Lacombe LA 70445  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 17: Cell E**  
Recently constructed creek



11/5/20, 3:40 PM  
N 30° 15' 36", W 89° 54' 12"  
Lacombe LA 70445  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 18: Cell E**  
Recently constructed western gap



11/5/20, 3:44 PM  
N 30° 15' 40", W 89° 53' 39"  
Slidell LA 70460  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 19: Cell E**  
Recently constructed middle gap



11/5/20, 3:47 PM  
N 30° 15' 44", W 89° 53' 18"  
Slidell LA 70460  
United States  
Big Branch Marsh National Wildlife Refuge

**Photo 20: Cell E**  
Recently constructed eastern gap

## **Appendix C**

### **Three-Year Operations & Maintenance Budget**

Goose Bayou/Point Platte Marsh Creation Project (PO-33)

Federal Sponsor: USFWS

Construction Completed: January, 2009

PPL #13

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12	Year 13	Year 14	Year 15	Year 16	Year 17	Year 18	Year 19	Year 20	Project Life	Currently	
Current Approved O&M Budget	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	Budget	Funded	
State O&M	\$3,156	\$3,222	\$571,227	\$3,359	\$3,430	\$3,502	\$3,575	\$3,650	\$3,727	\$3,805	\$3,885	\$3,967	\$4,050	\$4,135	\$4,222	\$4,311	\$4,401	\$4,494	\$4,588	\$4,684	\$645,391		
Corps Admin	\$762	\$778	\$794	\$811	\$828	\$845	\$863	\$881	\$900	\$919	\$938	\$958	\$978	\$998	\$1,019	\$1,041	\$1,062	\$1,085	\$1,107	\$1,131	\$18,696		
Federal S&A	\$2,938	\$3,000	\$3,630	\$3,128	\$3,193	\$3,260	\$3,329	\$3,399	\$3,470	\$3,543	\$3,617	\$3,693	\$3,771	\$3,850	\$3,931	\$4,013	\$4,098	\$4,184	\$4,272	\$4,361	\$72,680		
<b>Total</b>	<b>\$6,856</b>	<b>\$7,000</b>	<b>\$575,652</b>	<b>\$7,298</b>	<b>\$7,451</b>	<b>\$7,607</b>	<b>\$7,767</b>	<b>\$7,930</b>	<b>\$8,097</b>	<b>\$8,267</b>	<b>\$8,440</b>	<b>\$8,618</b>	<b>\$8,799</b>	<b>\$8,983</b>	<b>\$9,172</b>	<b>\$9,365</b>	<b>\$9,561</b>	<b>\$9,762</b>	<b>\$9,967</b>	<b>\$10,176</b>	<b>\$736,767</b>	<b>\$648,375</b>	
																					Remaining	Current 3 year	
																					Project Life	Budget	
<b>Projected O&amp;M Expenditures</b>																							
Maintenance Inspection													\$4,050	\$4,135	\$4,222	\$4,311	\$4,401	\$4,494	\$4,588	\$4,684	\$34,885	\$12,407	
General Maintenance																					\$0	\$0	
Structure Operations																					\$0	\$0	
Corps Admin																					\$0	\$0	
Federal S&A													\$3,771	\$3,850	\$3,931	\$4,013	\$4,098	\$4,184	\$4,272	\$4,361	\$32,479	\$11,552	
State S&A																				\$1,918	\$1,918	\$0	
Construction																					\$0	\$0	
Professional Services:																					\$0	\$0	
E&D																					\$0	\$0	
Engineering Surveying																	\$70,000			\$70,000	\$0		
Construction Administration																				\$0	\$0		
Inspection																				\$0	\$0		
<b>Total</b>													<b>\$7,821</b>	<b>\$7,985</b>	<b>\$8,153</b>	<b>\$8,324</b>	<b>\$8,499</b>	<b>\$8,677</b>	<b>\$8,860</b>	<b>\$9,044</b>	<b>\$10,964</b>	<b>\$139,282</b>	<b>\$23,959</b>

Note: Currently Funded amount is as of the February 2021 LANA report, the most recent LANA report that CPRA has received.

**Appendix D**  
**Field Inspection Form**

**FIELD INSPECTION CHECK SHEET**

**Project No. / Name:** Goose Point / Point Platte M.C. (PO-33)

**Date:** 11/5/2020

**Time:** 1:00 PM

**Structure No. :** n/a

**Inspector(s):** Taylor Daigle (CPRA)

**Description:** Marsh creation fill areas

**Water Level:** Rising from +0.83' NAVD88 (Contractor installed gage)

**Type of Inspection:** Annual

**Weather Cond:** Mostly cloudy

Project Feature	Condition	Physical Damage	Photo #	Observations and Remarks
<u>Cell A</u>	Good	None	1-4	Some large areas are noticeably lower than the surrounding marsh. The surrounding marsh appears to be healthy.
<u>Cell B</u>	Very Good	None	5-11	The marsh appears to be healthy.
<u>Cell C</u>	Very Good	None	12-14	The marsh appears to be healthy.
<u>Cell D</u> Vinyl Sheet Pile	Very Good	None	15-16	The marsh appears to be healthy. The vinyl sheet pile was not visited as a part of this annual inspection.
<u>Cell E</u> Vinyl Sheet Pile	Very Good	None	17-20	The marsh appears to be healthy. The vinyl sheet pile was not visited as a part of this annual inspection.
